TORVIEW COMMUNITY STORAGE NY, LLC

BESS FACILITY

STORMWATER POLLUTION PREVENTION PLAN

30 October 2026

Prepared by:

Tectonic Engineering Consultants, Geologists & Land Surveyors, D.P.C.,
205 Ridgewood Avenue
Brandon, FL 33510



Mark Privette
Digitally signed by Mark Privette
Date: 2026.11.02 10:30:49 -05'00'

J. Mark Privette, P.E.
Manager of Engineering

Project Contact Info

205 Ridgewood Avenue Brandon FL 33510
(813)374-9177 Tel

tectonicengineering.com
Equal Opportunity Employer

TABLE OF CONTENTS

SECTION	ITEM	PAGE
1.0	NARRATIVE	pg. 03-06
2.0	SITE CONDITIONS	pg. 07-09
3.0	POLLUTION CONTROL PLAN	pg. 10-15
4.0	CONSTRUCTION IMPLEMENTATION	pg. 16-22

APPENDICES

Appendix A	General Permit for Construction Activity (GP-0-25-001)
Appendix B	Engineer's Certification
Appendix C	Owner/Operator Certification
Appendix D	Contractor/Subcontractor Certification
Appendix E	List of Contractors and Subcontractors
Appendix F	NRCS Soils Mapping
Appendix G	FEMA Flood Map
Appendix H	Construction Inspection Log Book and Certification Forms
Appendix I	Corrective Action and SWPPP Amendments Logs
Appendix J	Site Construction Plans

1.0 INTRODUCTION

1.1 PROJECT NARRATIVE

The proposed development is an unmanned 2.6 MW / 10.4 MWh Battery Energy Storage System depicted in the attached Site Development Plans. The facility will be located on the grounds of a community swim club in Ossining, NY, having a property area of 12.85 Ac at 25 Stormytown Rd, in the Town of Ossining NY. The project involves the installation of a battery energy storage system (BESS) and associated equipment/infrastructure within a 2,464 sf (0.053 Ac) fenced compound having a total ground disturbance LOD of 6,400.7 sf (0.146 Ac), which includes the areas for resurfacing of the existing entrance drive as well as the perimeter landscape buffer. The Town of Ossining has requested that a SWPPP be prepared for the project in accordance with Article II, Section 168-8 B. (1) of the town code, indicating the pollution and ES&C measures being employed during the construction of this site and that it is in compliance with the State Pollution Discharge Elimination System (SPDES) General Permit for Construction Activities (GP-0-25-001) requirements.

This SWPPP is prepared to instruct Owners/Operators and their Contractors on mitigation measures used to prevent pollutants in stormwater runoff from entering the waters of the United States. Stormwater discharges from construction activities are required to obtain permit coverage through New York State's SPDES. Appendix A contains a copy of the New York State Department of Environmental Conservation (NYSDEC) SPDES General Permit for Construction Activities permit GP-0-25-001.

1.2 STANDARDS AND GUIDELINES

The following documents were utilized in the design process:

- NYSDEC; New York State Standards and Specifications for Erosion and Sediment Control, November 2016.
- New York State Stormwater Management Design Manual, July 2024.
- Town of Ossining Town Code, Article II of Chapter 168-8, section B. (1).

1.3 CERTIFICATION

The SWPPP preparer, the Owner/Operator and each Contractor and Subcontractor must complete and sign the appropriate certification. All appropriate signatures must be obtained prior to work commencing on the project site.

The Owner/Operator must identify the Contractor(s) and Subcontractor(s) that will be responsible for installing, repairing, inspecting and maintaining the erosion and sediment control practices required in the SWPPP. Each Contractor and Subcontractor must identify at least one trained individual from their company that will be responsible for implementation of the SWPPP. At least one trained individual must be on site on a daily basis when soil disturbance activities are being performed.

1.4 SUBMITTALS

The Contractor shall submit a "Construction Phasing Plan" indicating the sequence of construction, installation of erosion and sediment control practices, a list of areas to be disturbed associated with each construction activity and the procedure for stabilizing inactive disturbed areas. These submittals must be in substantial conformance with the measures outlined in this report. Proposed dates shall be provided for all the construction activities including temporary and permanent stormwater control measures.

1.5 SWPPP AVAILABILITY

The owner or operator shall maintain a copy of the General Permit (GP-0-25- 001), , SWPPP, inspection reports, responsible contractor's or subcontractor's certification statement, and all documentation necessary to demonstrate compliance with the approved SWPPP at the construction site until all disturbed areas have achieved final stabilization. The documents must be maintained in a secure location, such as a job trailer, on-site construction office, or mailbox with lock. The secure location must be accessible during normal business hours to an individual performing a compliance inspection.

1.6 PRE-CONSTRUCTION REQUIREMENTS

Prior to any soil disturbance at the project site the 'Construction Site Logbook' must be present on- site with all required signatures. The pre-construction meeting and inspection form must be completed and all required temporary erosion control measures must be installed for the involved phases of the project.

1.7 SITE LOCATION

The project parcel is located at 25 Stormytown Rd, in the Town of Ossining NY. Location and aerial maps are provided in Figures 1.a and 1.b at the end of this section.

1.8 SITE OWNER/OPERATOR

The name and address of the host property owner is:

Owner/Operator: Torview Swim and Tennis Club, Inc

Contact: Cristopher Moroni – Club President
Address: 25 Stormytown Road, PO Box 304
Ossining, NY 10562
Phone Number: (941) 941-1818

The name and address of the Owner/Operator, including the contact person is:

Owner/Operator: Luminace Holdings, LLC

Contact: Tessa Goodman
Address: 111 S. Calvert Street, Suite 1500
Baltimore, MD 21202
Phone Number: (941) 441-6252

1.a. Site Location and Aerial Maps

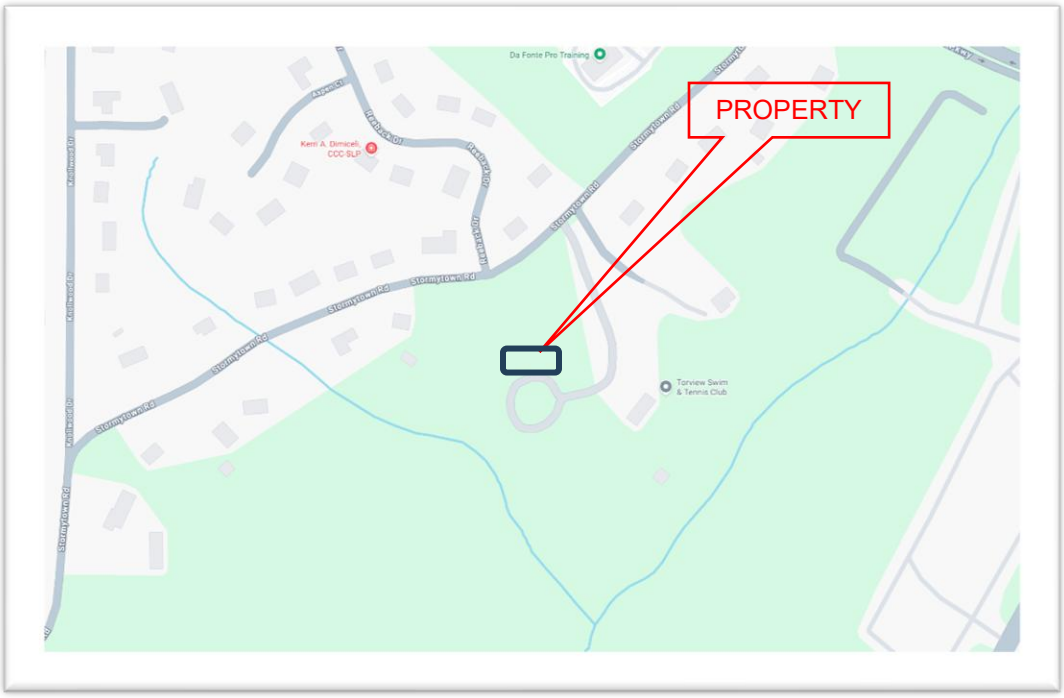

Figure 1.a. - Site Location Map

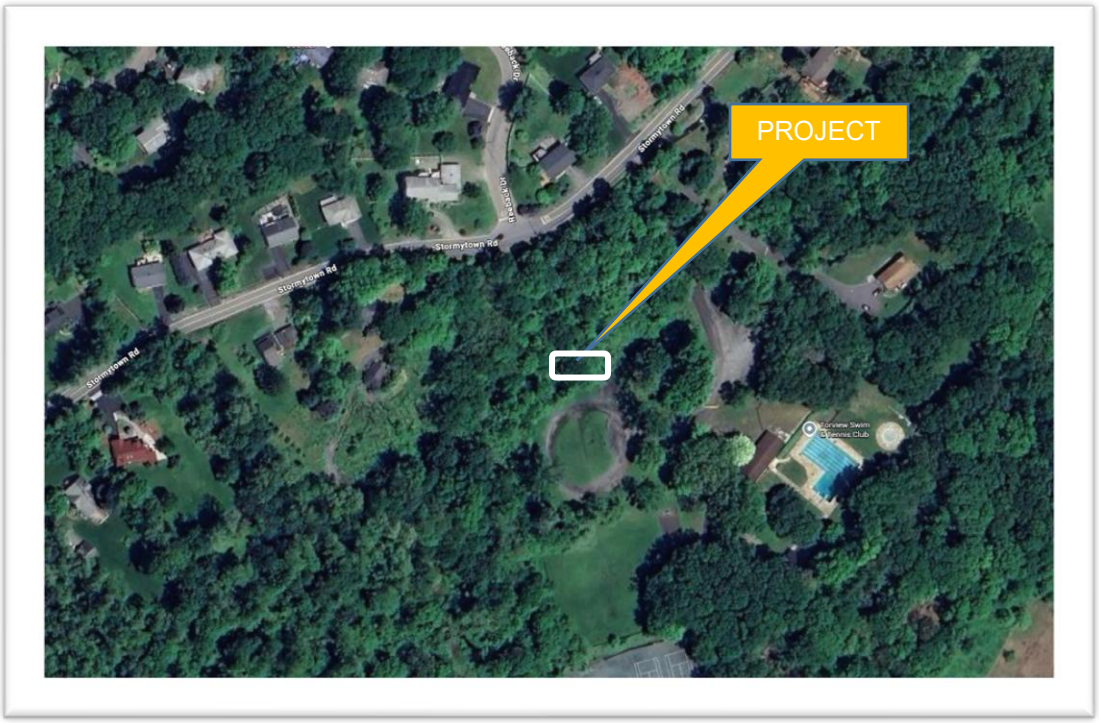

Figure 1.b. - Site Aerial Map

2.0 SITE CONDITIONS

2.1. TOPOGRAPHY

The project site is located within a developed recreational property characterized by rolling topography and wooded areas. Ground elevations across the overall property generally range from approximately 250 feet above mean sea level adjacent to Sing Sing Brook to approximately 360 feet in the western portion of the parcel. Surface drainage generally follows the natural topographic gradient toward Sing Sing Brook located southeast of the project area.

The proposed project area is situated within an existing developed portion of the property and occupies relatively moderate slopes compared to the steeper wooded areas located adjacent to the drainage corridor. Existing site improvements, maintained landscaping, and established vegetation currently provide stabilization throughout the project area. Topographic conditions were considered in the development of the erosion and sediment control measures described herein.

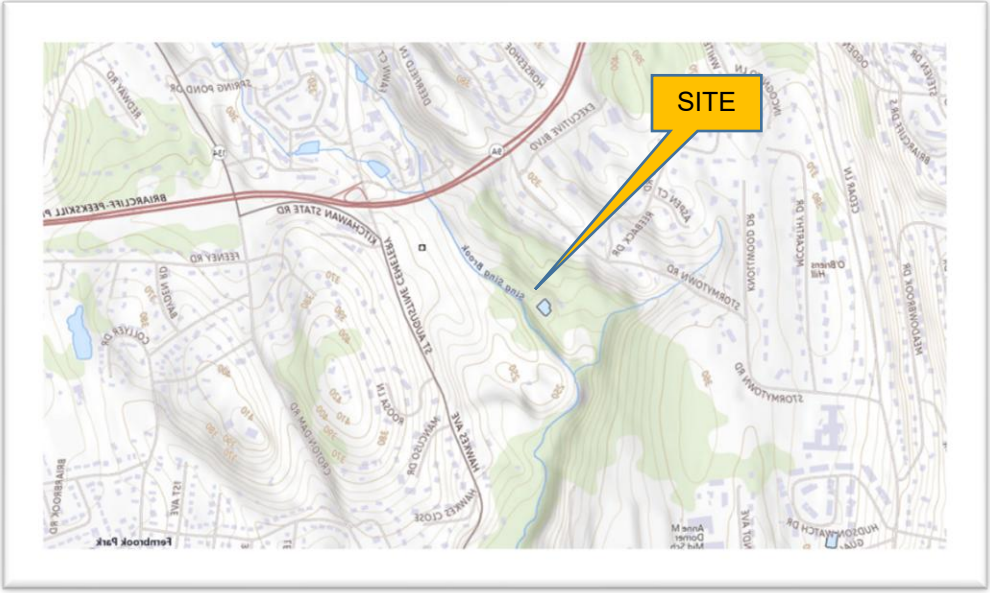

Figure 2.a. – Site Topographic Map

2.2. FLOODPLAINS AND FLOODWAYS

According to FEMA (FIRM Panel #361241F, 09/28/2007) this parcel is located in Zone "X", outside any designated 100 year flood plain or floodway.

2.3. WATERSHED DESIGNATION

The project is located in the Lower Hudson watershed (HUC 02030101).

2.4. WETLANDS AND WATERBODIES

A review of available mapping indicates that Sing Sing Brook is located on the eastern portion of the property and drains generally from north to south through the site. In addition, a small pond is present adjacent to the brook within the drainage corridor. These features are situated outside the proposed project area.

Based on available aerial imagery and topographic mapping, the proposed project area is located within an existing developed portion of the site and does not appear to contain jurisdictional wetlands, streams, or other surface water features. Existing woodland vegetation and topographic relief separate the project area from the onsite drainage corridor associated with Sing Sing Brook.

Any jurisdictional determination of wetlands or waters of the United States, if required, should be based on field delineation and review by the appropriate regulatory agencies.

2.5. SOILS

The soil types, within the proposed development site as indicated by the NRCS soil survey, consist primarily of Chatfield-Hollis-Rock and Udorthents, with 76.4% +/- of the soils hydrologically grouped as type "D" soils and the balance listed as type "B". The locations are depicted in the soils mapping provided in Appendix F. For the purposes of stormwater analysis and design, the on-site soils were assigned an HSG of type "D" soils. The soil types present on this parcel are primarily rated with a whole soil erosion K factor of 0.20 to 0.32, which indicates a slight to moderate susceptibility of erosion by runoff and as such, only standard ES&C measures are anticipated to be required.

Map unit symbol	Map unit name	Rating	Acres in AOI	Percent of AOI
Map unit symbol	**Map unit name**	**Rating**	**Acres in AOI**	**Percent of AOI**
CrC	Charlton-Chatfield complex, 0 to 15 percent slopes, very rocky	B	0.29	1.36%
CuD	Chatfield-Hollis-Rock outcrop complex, 15 to 35 percent slopes	D	0.63	2.92%
Ub	Udorthents, smoothed	B	3.00	13.88%
Totals for Area of Interest			**21.60**	**100.0%**

Table 2.5.a. – Site Drainage Basin Soils Table

2.6. VEGETATION

The project site is currently developed as a recreational facility consisting of swimming pool facilities, tennis courts, landscaped areas, and maintained open space. Existing vegetation is dominated by managed turf grass associated with the recreational use, with mature woodland vegetation and scattered landscaped plantings located throughout the property and along portions of the site perimeter.



Photo 2.6.a. Aerial view of project area

Review of available aerial imagery and existing site conditions indicates that vegetative cover is well established across the property, with wooded areas consisting primarily of mature deciduous tree cover and localized understory vegetation. No significant areas of exposed soil or sparsely vegetated ground were observed outside of existing developed features. Vegetation within areas not subject to disturbance will remain in place to the maximum extent practicable throughout construction activities.

For hydrologic modeling purposes, the existing land cover is characterized as a combination of maintained open space and woodland cover consistent with observed site conditions and applicable NRCS TR-55 methodologies.

2.7. EXISTING LAND USE

The existing property is currently developed and operated as a private recreational facility (Torview Swim & Tennis Club) consisting of outdoor swimming pools, tennis courts, recreational amenities, and ancillary support facilities on approximately 12.85 acres. The site is therefore classified as an existing recreational/open-space use rather than residential, commercial, industrial, or agricultural land use.

3.0 POLLUTION CONTROL PLAN

3.1 POLLUTION PREVENTION MEASURES

All debris and waste materials from construction activities will be disposed of using an on-site trash dumpster to minimize stormwater pollution.

Expected construction materials to be stored on-site include solar panels, racking supports, fencing, geotextile and aggregate fill material. No pollutants are known to be associated with any of these materials. The aggregate material will be protected to prevent sediment runoff during storm events. Potential pollutant sources due to construction activities include diesel fuel, gasoline and concrete slurry.

- Diesel Fuel (30 to 100 gal) – Mobile fueling truck w/spill kit on board, no full time storage.
- Gasoline (Less than 50 gal) - Mobile fueling truck w/spill kit on board, no full time storage.
- Concrete Slurry – Utilized for directional boring at locations indicated on sheet C6 of the plans. Volume as determined by contractor

Fuels and Oil

Vehicles requiring refueling or lubrication shall be brought to a portion of the site away from environmentally sensitive areas (such as wetlands, storm drains, culverts, wells, etc.). All construction equipment shall be refueled at least 100 feet from a waterbody, wetland, rare species habitat, or unique natural community and in an upland area away from conveyance channels. The Contractor shall take precautions to ensure that drips, spills, or seeps do not enter the ground. The use of absorbent towels and/or a portable basin beneath the fuel tank is recommended. Refueling activities shall be performed under continual surveillance with extreme care.

Where there is no reasonable alternative, refueling may occur within these setbacks, but only under the observation of the Trained Contractor and after proper precautions are taken to prevent an accidental spill. Drip pans shall be used and a supply of absorbent pads shall be available and utilized, as required. In the event of a release, the spill shall be promptly cleaned up in accordance with the NY State spill response and clean-up procedures.

On-site construction vehicles including Contractor employee vehicles shall be monitored for leaks and shall receive regular preventative maintenance to reduce

the risk of leakage. Any equipment leaking oil, fuel, or hydraulic fluid shall be repaired immediately or removed from the site. Construction equipment and Contractor personal vehicles shall be parked at least 100 feet from a wetland, river, creek,

stream, lake, reservoir, spring, well or other ecologically sensitive site, or existing recreational area along the proposed rights-of-way at the end of the working day except where it is necessary to maintain continuity of construction.

Petroleum products and hydraulic fluids that are not in vehicles shall be stored in tightly sealed containers that are clearly labeled. All gasoline and fuel storage vessels with greater than a 25-gallon capacity must have secondary containment constructed of an impervious material and be capable of holding 110% of the vessel capacity. All state and federal regulations shall be followed for the storage, handling, application, usage, and disposal of pesticides, fertilizers, and petroleum products.

Equipment shall have sufficient spill containment equipment on board to provide for prompt control and cleanup, in the event of a release.

Management of Spills and Releases:
Should a fuel, oil, or chemical spill occur during the project, The Contractor will be responsible for reporting the spill or release to the NYSDEC Spill Hotline 1-800-457-7362 as applicable, within two hours of the release.
Contractor is also responsible for any and all response actions. Any contaminated soil shall be removed from the worksite and disposed of in accordance with product specific MSDS and NYSDEC guidance. Petroleum spills that do not need to be reported, are those that meet the following criteria:

- The quantity is known to be less than 5 gallons; and
- The spill is contained and under the control of the spiller; and
- The spill has not and will not reach the State's water or any land (A spill is considered to have not impacted land if it occurs on a paved surface such as asphalt or concrete. A spill in a dirt or gravel parking lot is considered to have impacted land and is reportable.); and
- The spill is cleaned up within 2 hours of discovery.

Concrete Slurry
The use of concrete slurry for directional boring is a fluid-assisted excavation technique that uses a semi-liquid mix to improve drilling effectiveness. It is used in

horizontal directional drilling (HDD) to create pilot boreholes. Slurry boring can stabilize borehole walls as well as remove suspended spoil from the excavation site.

Slurry Management Plan:
Contractor is to provide and adhere to a written Slurry Management Plan, using but not limited to tools and techniques (CSDA-BP-001, 10/24/2017) listed below:

- Determine the 'low point' of the specific work area to potentially let gravity assist the flow of the water/slurry and minimize the use of pumps.
- Restrict access to the worksite as needed to minimize hazards associated with the water/slurry and/or RCS exposure. Clearly post with appropriate hazard signs.
- Use polyurethane sheets or tarps to protect surfaces from slurry splash or spray.
- Collection and control – wet/slurry vacuums, shrouds/slurry collection rings, wands, squeegees, troughs/socks/bags/'pig' to direct flow and pumps (dewatering, semi-trash or trash pumps).
- For small to mid-sized vacuums in rough terrain, the slurry could possibly splash past the ball float and damage the vacuum motor. The size of the vacuum tank could be a limitation on the weight of a full vacuum. Slurry can sometimes foam up and the bubbles or slurry mist (both may be abrasive) can get past the ball float and damage the vacuum motors. Some slurry vacuums offer nylon or other filters to protect the motors to minimize the damage from abrasive mist/foam. Sometimes a surfactant can be added to the vacuum to minimize the foaming. Another alternative is using a superabsorbent polymer in the vacuum drum that can solidify/gel the slurry as it is being collected to minimize sloshing and splashing of the slurry/water in the drum. F. Thick paste slurries can be diluted with water to help the vacuum suck up the liquid.
- Drum vacuum heads using standard 55-gallon drums are very common to minimize the number of times the slurry is transferred (simply move the vacuum head to another drum). The drums can be used to help facilitate the settling of the slurry to recycle the water and later handling the sludge.
- Large vacuum trucks and other mobile devices are available to handle large amounts of slurry on road jobs. Some large systems utilize centrifuges to separate out the solids from the water in the slurry so the water can be treated for disposal or recycled.
- Flocculants can be used to accelerate the settling time in recycling the water by quickly separating the solids. Flocculants require some level of agitation of the slurry to mix in the floc to properly drop out the solids from the slurry. If the slurry is thick and pasty, additional water can be added to allow the floc to mix thoroughly in the slurry and to help drop more of the solids out of the slurry. It seems counter intuitive, but the additional water will separate back out and pull out more water from the original slurry, potentially creating an even more concentrated slurry. Air bubblers can be used to stir in the floc in lieu of mixers.

- Recycling slurry water. The water might have a high Ph, which could potentially damage equipment so it might be worth monitoring the pH level and adding an acid to lower the pH. Note high pH alkaline solutions can be irritating to the skin. Typically, a 9-1/2 pH is the threshold for a ground dump and typically 12.5 or more is considered hazardous. In 55-gallon drums, a large drill mixer can be used to mix in the floc and as solids sink the water can be transferred (or decanted) out using a small dewatering pump or a wet vacuum with a wand. On larger tanks or truck vacuums, a cascading system of weirs can be used to get a larger volume of clean water available faster. The weir system acts as a series of individual settling tanks. Only the cleanest of the water out of the slurry in each tank is able to flow over the weir into the next tank in the series.
- Storage of slurry. The slurry can be stored in pits, tanks, drums or other structures using liners. Be certain the structure can handle the weight of the slurry. Have a plan for handling potential leaks. 55-gallon drums are very common, and the water can be decanted off after settling. Drum dollies help move the barrels. Drums can be strapped to a pallet so a forklift or pallet jack can be used to move them around the jobsite.
- Filter presses can be used to process slurry to squeeze out the clean water and leave cakes/bricks for disposal of the solids from the slurry. The water can be recycled. Some filter presses work more efficiently when the slurry is pretreated with a flocculent. The floc will increase the particle size in the slurry so the small openings in the filter press are more open and less susceptible to being plugged up.
- Surfactants will make the water 'wetter' and reduce the surface tension on the water droplets. This makes the water more effective at dust control and can sometimes reduce the amount of water needed.
- Spoil areas may be provided on some jobsites by the owner for temporary storage.
- Regardless of how the slurry is collected or stored on the jobsite, plan for where and how the slurry will be properly disposed of.
- Hauling slurry. If you decant to water prior to moving, you will be hauling less weight and volume. The liquid's center of gravity shifts as it moved during transport. In large tanks or trucks, a large shift in the center of gravity can be potentially dangerous. One technique to handle sloshing liquid is to put baffles in the tank.
- Vacuum truck services are available in many areas. For some jobs it might be worth considering subcontracting a waste hauler/super sucker truck.
- Some concrete batch plants will accept slurry.

- Slurry can be solidified and treated as solid waste. Large dewatering/filter bags in a tank with a drain can allow the water to slowly drain out of the slurry. The solids remain in the bag for disposal. Settling pits or tanks can allow solids in the slurry to settle out and the water can evaporate or be decanted. Cascading tanks or weirs can be used to allow the solids to settle out of the water (used more in dynamic water flow scenarios whereby water is being continually recirculated). A filter press can be used to press out the water from the slurry and create a solid cake/brick. Flocculants can speed up the process of separating solids in slurry. Super Absorbent Polymers (SAPs) can be used to absorb the water and dry out slurry. The SAPs have been shown to pass a paint filter test (PFT) method 9095B, which is a key consideration for disposing in a solid waste landfill. The alkalinity of slurry and some dissolved elements in the slurry can reduce the effectiveness of the SAPs, thus requiring more than a theoretical ideal amount to be used, or the slurry can be pretreated to make it more efficient with the SAP.

3.2 EROSION AND SEDIMENT CONTROL

Temporary erosion and sedimentation controls will be implemented during construction. These measures are presented in detail in the attached Erosion and Sedimentation Control Plan within the plan set and are based upon the New York State Standards and Specifications for Erosion and Sediment Control (Nov 2016):

- Stabilized Construction Entrance: Install gravel entrance pursuant to construction details provided, and in the location indicated in the plans. To remain in place and functional for the duration of construction activities.
- Silt Fencing: Silt fencing to be installed as per the silt fencing plan and associated details. Silt fencing is to be inspected on a daily basis for damaged or failing sections. Silt fencing to be installed between graded and undisturbed areas to prevent sediment from entering the undisturbed areas or adjacent water bodies or runoff conveyances (i.e. culverts).
- Concrete Washout: Concrete washout areas are to be constructed and installed per the details provided and located adjacent to those areas where substantial concrete work is being performed (i.e. slabs).
- Rock check dams: Install check dams consisting of gravel and riprap at locations indicated on the approved plans, and in conformance with construction details.
- Topsoil Stockpile: Enclose perimeter of stockpile with silt fencing and vegetative matting or cover. Locate stockpile away from streams, ditches or other water bodies.

- Site Stabilization: Any disturbed areas of the site where construction activities have temporarily or permanently ceased for more than 14 days shall be stabilized with vegetative cover. Winter stabilization can be done using mulch or other Engineer approved products.

3.3 PERMANENT EROSION AND SEDIMENT CONTROL FACILITIES

Surface Stabilization: Stabilization of exposed disturbed soils following construction will be accomplished with grass and mulch.

4.0 CONSTRUCTION IMPLEMENTATION

4.1 CONSTRUCTION SCHEDULE AND SEQUENCE

The general site notes and anticipated construction sequence for the site improvements consist of the following:

4.1.a. GENERAL NOTES

1. One week prior to beginning earthwork operations, a pre-construction meeting will be held to discuss the erosion and sediment control plan and to finalize the paperwork for the Stormwater Pollution Prevention Plan, as specified in the DEC SPDES General Permit for Stormwater Discharge from Construction Activities.
2. Erosion and sediment control measures shall be provided prior to beginning any land disturbance activities. The devices providing protection to a given area shall not be removed until the disturbed lands in that area are stabilized.
3. No disturbed area shall remain exposed for more than 14 days, except for portions of the site in which work will be continuous beyond 14 days.

4.1.b. CONSTRUCTION SEQUENCE

1. Control dust on site to prevent dust leaving the site and creating off-site damage, health hazards, and traffic safety problems. Treatment includes but is not limited to spraying disturbed soil surfaces with water.
2. Install 12’ wide x 50’ long (min.) stabilized construction access.
3. Install 12’ wide temporary construction access road in the alignment of the proposed final access road.
4. Install perimeter silt fence as indicated in the plans and around any other ground disturbances within the project area.
5. Excavate and rough grade roadside collector and divertor swales. Install stabilization measures on the banks and flowline. Install check dams.
6. Clear and grub site. Strip topsoil and stockpile on-site with perimeter silt fence and vegetative cover. Perform earthwork grading and contouring in accordance with approved plans.
7. Install outfall structures and spillways with inlet protection as needed.
8. Construction of main project elements including infrastructure, trenching, panel racking structures and new access drive(s).
9. Perform soil restoration for all temporary construction access road segments and gravel staging/stockpile areas, that will be converted to pervious cover in post-construction conditions. Soil restoration includes deep ripping the subsoil to a minimum depth of 12-Inches, mixing 3-Inches of compost into the subsoil, and spreading 6-Inches of topsoil to the site.

10. Seed/Sod and mulch disturbed areas. No connection to the proposed downstream basins can be made until all upstream construction has been completed and stabilized with a vigorous vegetative cover established over all the pervious surfaces of the drainage basin.
11. Remove sediment from silt fences, concrete washouts, and inlet protection if necessary.
12. Remove all temporary erosion control methods when contributing drainage areas have reached final stabilization.

4.2 INSPECTION AND MAINTENANCE PROCEDURES

Refer to the Site Erosion Control Plan for guidelines concerning the inspection and maintenance procedures for the erosion and sediment control facilities. A Construction Site Inspection and Maintenance Log Book (Appendix I) is included with the SWPPP for inspections to be performed during construction. In addition to the Log Book, a Pre-Construction Site Assessment Checklist (Appendix I) is to be completed per the attached instructions.

4.2.a. SITE INSPECTIONS

1. The operator shall have a qualified professional conduct an assessment of the site prior to the commencement of construction and certify in an inspection report that the appropriate erosion and sediment controls described in the SWPPP have been adequately installed or implemented to ensure overall preparedness of the site for the commencement of construction. Following the commencement of construction, site inspections shall be conducted by the qualified professional at least every 7 calendar days for projects with less than 5 acres of ground disturbance. If more than 5 acres are disturbed at any time these inspections will be conducted twice during the seven calendar day time period, with a minimum separation of 2 full calendar days. If construction has been temporarily suspended and temporary stabilization measures have been applied to all disturbed areas, the site inspection cycles may be reduced to once every (30) thirty calendar days, after written notification has been made to the DOW Water Program Contact at the regional office. During each inspection, the qualified professional shall record the following information:
2. The purpose of site inspections is to assess performance of pollutant controls. Based on these inspections, the Owner/Developer designated

qualified professional may ascertain whether or not it is necessary to modify the Final SWPPP, add or relocate sediment barriers, or take whatever actions are deemed prudent to prevent pollutants from leaving the site via storm water runoff. The contractor is required to ensure any damaged ES&C measures are repaired, modified or replaced in order to safeguard their functionality.

3. The operator shall maintain a record of all inspection reports (Appendix I) in a site logbook. The site log book shall be maintained on-site and be made available to the permitting authority upon request. Prior to commencement of construction, the operator shall certify in the site logbook that the SWPPP meets all Federal, State and local erosion and sediment control requirements. In addition, the qualified professional shall complete monthly summaries of the compliance status of the site. The summaries of the site inspection activities will be stored on-site by the operator on a monthly basis.

4.2.b. MAINTENANCE

1. During construction, the contractor will be responsible for inspecting and maintaining the permanent and temporary erosion control facilities. Also, areas that have been seeded will be inspected regularly after seed germination to ensure complete coverage of exposed areas.
2. The operator shall initiate stabilization measures as soon as practicable in portions of the site where construction activities have temporarily or permanently ceased, but in no case more than 14 days after the construction activity in the portion of the site has temporarily or permanently ceased. This requirement does not apply in the following instances:
    a. Where the initiation of stabilization measures by the 14th day after construction activity temporarily or permanently ceased is precluded by snow cover or frozen ground conditions, stabilization measures shall be initiated as soon as practicable.
    b. Where construction activity on a portion of the site is temporarily ceased the application of soil stabilization measures must be initiated by the end of the next business day and completed within fourteen (14) days from the date the current soil disturbance activity ceased.
    c. Where construction activity associated with the footprint of the solar array and/or equipment area has temporarily

ceased, temporary stabilization measures need not be initiated on that portion of the site.

3. Inspections of all devices should be completed weekly and after each rainfall event. Repairs should be completed immediately upon discovery.

4.3. REVISIONS TO THE SWPPP

Based on construction activities and the results of inspections, changes to the erosion and sediment control plan are expected and shall be documented using the Report Form for Changes in Pollution Prevention Plan (Appendix J).

4.4 NOTICE OF TERMINATION

The operator shall certify that the requirements for Site Assessment and Inspections, Stabilization and Maintenance Completion have been satisfied within 48 hours of actually meeting such requirements.

When construction is completed and all areas that were disturbed by construction activities have been permanently stabilized, the operator or authorized representative of the operator shall prepare, sign, and submit a completed Notice of Termination.

Prior to filing of the Notice of Termination, the operator shall have a qualified professional perform a final site inspection. The qualified professional shall certify that the site has undergone final stabilization using either vegetative or structural stabilization methods and that all temporary erosion and sediment controls (such as silt fencing) not needed for long-term erosion control have been removed.

The completed form shall be submitted to the Town's Stormwater Officer.

A copy of the SWPPP and all documents associated with the permit shall be retained for three years from the submittal of the Notice of Termination.

4.5 MAINTENANCE OF STORMWATER MANAGEMENT PRACTICES

4.5.a. OPERATIONS AND MAINTENANCE

Post-construction inspections and maintenance shall be performed by the owner. Inspections and maintenance for the various site components and stormwater management facilities shall be performed in accordance with the accompanying project plans and this SWPPP. A summary of the stormwater management system inspection and maintenance parameters is provided in Table 6.5.a and 6.5.b. below.

Maintenance of the proposed stormwater facilities consist primarily of monthly mowing of the roadside swales and shoulders in order to maintain a grass height of 4 to 6 inches. It also includes monthly trash/debris removal from the catchment areas, although for this type of project those activities are expected to be minimal.

4.5.b. SEDIMENT MONITORING AND REMOVAL PRACTICES

Proposed stormwater ponds and/or swales utilized as temporary sediment basins or traps during construction shall be inspected at least every seven calendar days for accumulated buildup of sediment. Accumulated sediment buildup in excess of 50% capacity or 1/3 the height of the compost sock trap shall be removed off-site and any damages to the sediment basin/trap will be repaired immediately upon discovery.

For those ponds or swale areas, where a geofilter fabric has been installed as a temporary surface protection to prevent clogging of the underlying soils; the fabric shall be replaced each time accumulated sediment has to be removed.

Table 4.5.a.: General Site Post-Construction Inspection and Maintenance

Maintenance Item	Frequency	Description of Inspection Parameters	Description of Remedy Procedures
Site Structures	Annual & After Major Storms	-Accumulated sediment, debris and litter in outfall structures and drain basins -Damage of storm structures or associated components -Accumulation of pollutants, including oils or grease, in drain basins	-Remove -Replace and/or repair, as necessary -Remove pollutants from catch basins. Replace and/or repair pollutant source.
Pavement	Biannual/ Annual	-Accumulated sediment in paved areas -Accumulated debris and litter	-Remove (sweep min. 2 times/year) -Remove
Embankments	Annual	-Differential settlement of embankments -Embankment erosion -Animal burrows -Cracking, bulging, or sliding of embankment	-Stabilize and restore to original specs - Stabilize and restore to original specs -Remove - Stabilize and restore to original specs
Grass and Landscaped areas	Annual	-Vegetation: 80% coverage + less than 15% invasive plant species -Unauthorized plantings -Undesirable vegetative growth -Accumulated debris and litter	-Restore original specs -Remove -Mow a min. of 3 times/year. May increase -Remove
Winter Maintenance	Monthly	-Accumulation of snow and ice on catch basins, inlet and outlet structures, and end sections -Stock piled snow near inlets and outlets -Remaining deicing materials	-Remove -Remove -Remove in early spring by sweeping
Swales	Monthly	-Erosion of side slopes -Formation of rills or gullies -Excess grass growth -Undesirable vegetative growth -Accumulated debris, litter, or sediment -Residual deicing materials (sand)	- Stabilize and restore to original specs -Repair and restore to original specs -Mow -Remove -Remove -Remove & replace any damaged vegetation

Table 4.5.b.: General Site Post-Construction Inspection and Maintenance

Maintenance Item	Frequency	Description of Inspection Parameters	Description of Remedy Procedures
Pond Embankment	Annual	-Vegetation: 80% coverage + less than 15% invasive plant species -Embankment erosion -Animal burrows -Unauthorized plantings -Cracking, bulging, or sliding of embankment -Function of pond drain -Seeps and leaks of downstream face -Rip-rap failure -Vertical alignment of top of embankment "as-built" -Spillway weir erosion and debris	- Restore original specs -Stabilize & restore to original specs -Remove -Remove -Stabilize & restore to original specs -Clean as necessary -Stabilize & repair any breach -Restore rip-rap cover as necessary -Add/remove material & stabilize to original specs -Clean debris and add rip-rap as necessary
Outlet Structures	Annual & After Major Storm Events	-Trees and shrubs around inlets, outlets, and end sections -Rip-rap failure -Accumulated debris and sediment	-Remove -Restore rip-rap cover as necessary -Remove
Filter Bed	Annual	-Filter bed blocked or filled in -Water ponding for more than 48 hours	-Remove and replace filter media meeting original specifications
Infiltration Trench	Annual	-Trench Drain Basin blocked or filled in -Water ponding for more than 48 hours	-Remove -Remove and replace trench gravel

APPENDIX A
GENERAL PERMIT FOR CONSTRUCTION ACTIVITY (GP-0-25-001)

NEW YORK STATE
DEPARTMENT OF ENVIRONMENTAL
CONSERVATION (NYSDEC)

SPDES GENERAL PERMIT
FOR STORMWATER DISCHARGES

From

CONSTRUCTION ACTIVITY

Permit No. GP-0-25-001

Construction General Permit (CGP)

Issued Pursuant to Article 17, Titles 7, 8 and Article 70

of the Environmental Conservation Law

Effective Date: January 29, 2025 Expiration Date: January 28, 2030

Scott E. Sheeley

Chief Permit Administrator

Scott E. Sheeley JAN. 29, 2025

Authorized Signature Date

Address: NYSDEC
Division of Environmental Permits
625 Broadway, 4th Floor
Albany, N.Y. 12233-1750

PREFACE

Pursuant to Section 402 of the Clean Water Act (CWA), and 40 CFR 122.26(b)(14)(x), (15)(i), and (15)(ii), *stormwater discharges* from certain *construction activities* are unlawful unless they are authorized by a National Pollutant Discharge Elimination System (NPDES) permit or by a state permit program. New York State administers the approved State Pollutant Discharge Elimination System (SPDES) program with permits issued in accordance with the New York State Environmental Conservation Law (ECL) Article 17, Titles 7 and 8, and Article 70, as well as 6 NYCRR Parts 621 and 750.

C*onstruction activities* constitute construction of a *point source* and, therefore, pursuant to ECL sections 17-0505, 17-0701, and 17-0803, the *owner or operator* must have coverage under a SPDES permit prior to *commencement of construction activities*. The *owner or operator* cannot wait until there is an actual *discharge* from the *construction site* to obtain permit coverage.

***Note: The italicized words/phrases within this permit are defined in Appendix A.**

NEW YORK STATE DEPARTMENT OF ENVIRONMENTAL CONSERVATION
SPDES CONSTRUCTION GENERAL PERMIT (CGP) GP-0-25-001
FOR STORMWATER DISCHARGES FROM CONSTRUCTION ACTIVITIES

Table of Contents

Part I. How to Obtain Coverage and General Requirements 5
A. Eligibility Requirements 5
B. Types of *Discharges* Authorized 9
C. Prohibited *Discharges* 10
D. Electronic Notice of Intent (eNOI) Submittal 10
E. General Requirements for *Owners or Operators* with Permit Coverage 14
F. Permit Coverage for *Discharges* Authorized Under GP-0-20-001 18
G. Change of *Owner or Operator* 19
Part II. Water Quality-Based Effluent Limitations 20
A. Maintaining Water Quality 20
B. Effluent Limitations Applicable to *Discharges* from *Construction Activities* 20
C. Post-Construction Stormwater Management Practice (SMP) Requirements 23
Part III. Stormwater Pollution Prevention Plan (SWPPP) 28
A. General *SWPPP* Requirements 28
B. Required *SWPPP* Contents 32
C. Required *SWPPP* Components by Project Type 37
Part IV. Inspection and Maintenance Requirements 37
A. General Construction Site Inspection and Maintenance Requirements 37
B. Contractor Maintenance Inspection Requirements 37
C. *Qualified Inspector* Inspection Requirements 38
Part V. How to Terminate CGP Coverage 43
A. Electronic Notice of Termination (eNOT) Submittal 43
Part VI. Record Retention and Reporting 45
A. Record Retention 46
B. Reporting 46
Part VII. Standard Permit Requirements 46
A. Duty to Comply 46
B. Need to Halt or Reduce Activity Not a Defense 46
C. Penalties 46
D. False Statements 47
E. Re-Opener Clause 47
F. Duty to Mitigate 47
G. Requiring Another General Permit or Individual SPDES Permit 47
H. Duty to Provide Information 49
I. Extension 49
J. Signatories and Certification 50
K. Inspection and Entry 52
L. Confidentiality of Information 53
M. Other Permits May Be Required 53

N. NYSDEC Orders or Civil Decrees/Judgments 53
O. Property Rights 53
P. Compliance with Interstate Standards 53
Q. Oil and Hazardous Substance Liability 54
R. Severability 54
S. NYSDEC Approved Forms 54
APPENDIX A – Abbreviations and Definitions 55
Abbreviations 55
Definitions 56
APPENDIX B – Required SWPPP Components by Project Type 64
Table 1 64
Table 2 66
APPENDIX C – Watersheds Requiring Enhanced Phosphorus Removal 68
APPENDIX D – Impaired Waterbodies (by Construction Related Pollutants) 74
APPENDIX E – List of NYSDEC Regional Offices 80
APPENDIX F – SWPPP Preparer Certification Form 81
APPENDIX G – MS4 SWPPP Acceptance Form 83
APPENDIX H – NYCDEP SWPPP Acceptance/Approval Form 86
APPENDIX I – MS4 No Jurisdiction Form 89
APPENDIX J – Owner/Operator Certification Form 91

Part I. How to Obtain Coverage and General Requirements

To be covered under this permit, the *owner or operator* must meet all eligibility requirements in Part I.A. and follow the requirements for obtaining permit coverage in Part I.D., F., or G.

A. Eligibility Requirements

For a *common plan of development or sale*, the *phase(s)* that meet the eligibility requirements in Part I.A. may obtain coverage under this permit even if other *phase(s)* of the same *common plan of development or sale* do not meet the eligibility requirements and require an individual SPDES permit.

1. The *owner's or operator's construction activities* involve soil disturbances of:

    a. one or more acres; or

    b. less than one acre which are part of a *common plan of development or sale* that will ultimately disturb one or more acres; or

    c. less than one acre where NYSDEC has determined that a SPDES permit is required for *stormwater discharges* based on the potential for contribution to a violation of a *water quality standard* or for significant contribution of pollutants to *surface waters of the State*.

        i. 5,000 square feet or more, but less than one acre, and are in the New York City Watershed located east of the Hudson River, Appendix C Figure 1; or

        ii. 20,000 square feet or more, but less than one acre, within the municipal boundaries of the City of New York (NYC); or

        iii. less than 20,000 square feet which are part of a *common plan of development or sale* that will ultimately disturb 20,000 square feet or more, but less than one acre, within the municipal boundaries of NYC; or

        iv. that creates 5,000 square feet or more of *impervious area* within the municipal boundaries of NYC.

2. *Discharges* from the *owner's or operator's construction activities* are/were not:

    a. already covered by a different SPDES permit; or

    b. covered under a different SPDES permit that was denied, terminated, or revoked; or

    c. identified in an expired individual SPDES permit that was not renewed; or

    d. required to obtain an individual SPDES permit or another general SPDES permit in accordance with Part VII.K.

3. If *construction activities* may adversely affect a species that is endangered or threatened, the *owner or operator* must obtain a:

    a. permit issued pursuant to 6 NYCRR Part 182 for the project; or

    b. letter issued by NYSDEC of non-jurisdiction pursuant to 6 NYCRR Part 182 for the project.

4. If *construction activities* have the potential to affect an *historic property*, the *owner or operator* must obtain one of the following:

    a. documentation that the *construction activity* is not within an archeological buffer area indicated on the sensitivity map, and that the *construction activity* is not located on or immediately adjacent to a property listed or determined to be eligible for listing on the National or State Registers of Historic Places, and that there is no new permanent building on the *construction site* within the following distances from a building, structure, or object that is more than 50 years old, or if there is such a new permanent building on the *construction site* within those parameters that NYS Office of Parks, Recreation and Historic Preservation (OPRHP), a Historic Preservation Commission of a Certified Local Government, or a qualified preservation professional has determined that the building, structure, or object more than 50 years old is not historically/archeologically significant:

        i. 1-5 acres of disturbance - 20 feet; or

        ii. 5-20 acres of disturbance - 50 feet; or

iii. 20+ acres of disturbance - 100 feet.

b. NYSDEC consultation form sent to OPRHP,[1] and copied to NYSDEC's Agency Historic Preservation Officer (APO), and

i. the State Environmental Quality Review Act (SEQR) Environmental Assessment Form (EAF) with a negative declaration or the Findings Statement, with documentation of OPRHP's agreement with the resolution; or

ii. documentation from OPRHP that the *construction activity* will result in No Impact; or

iii. documentation from OPRHP providing a determination of No Adverse Impact; or

iv. a Letter of Resolution signed by the *owner or operator*, OPRHP and the DEC APO which allows for this *construction activity* to be eligible for coverage under the general permit in terms of the State Historic Preservation Act (SHPA).

c. documentation of satisfactory compliance with Section 106 of the National Historic Preservation Act for a coterminous project area:

i. No Affect; or

ii. No Adverse Affect; or

iii. Executed Memorandum of Agreement.

d. documentation that SHPA Section 14.09 has been completed by NYSDEC or another state agency.

5. If *construction activities* are subject to SEQR, the *owner or operator* must obtain documentation that SEQR has been satisfied.

6. If *construction activities* are not subject to SEQR, but subject to the equivalent environmental review from another New York State or federal agency, the

[1] The consultation form can be submitted, along with other project information, through OPRHP's Cultural Resource Information System (CRIS) portal. If submitted through CRIS, paper copies of the consultation form need not be mailed.

owner or operator must obtain documentation that project review, pursuant to a process equivalent to SEQR from another New York State or federal agency, has been satisfied.

7. If *construction activities* require Uniform Procedures Act (UPA) Permits (see 6 NYCRR Part 621) from NYSDEC, or the equivalent from another New York State or federal agency, the *owner or operator* must:

    a. obtain all such necessary permits; or

    b. receive notification from NYSDEC pursuant to 6 NYCRR 621.3(a)(4) excepting Part I.A.7.a.

8. *Construction activities* are not eligible if they meet the following criteria in Part I.A.8.a. or b.:

    a. For linear transportation and linear utility project types, the *construction activities*:

        i. are within the watershed of *surface waters of the State* classified as AA or AA-S identified utilizing the Stormwater Interactive Map on NYSDEC's website; and

        ii. are undertaken on land with no existing *impervious cover*; and

        iii. disturb two or more acres of *steep slope*.

    b. For all other project types, the *construction activities*:

        i. are within the watershed of *surface waters of the State* classified as AA or AA-S identified utilizing the Stormwater Interactive Map on NYSDEC's website; and

        ii. are undertaken on land with no existing *impervious cover*; and

        iii. disturb one or more acres of *steep slope*.

B. Types of *Discharges* Authorized

1. The following *stormwater discharges* are authorized under this permit:

   a. *Stormwater discharges*, including *stormwater* runoff, snowmelt runoff, and surface runoff and drainage, associated with *construction activity*, are authorized under this permit provided that appropriate *stormwater* controls are designed, installed, and maintained in accordance with Part II. and Part III.

   b. *Stormwater discharges* from construction support activities at the *construction site* (including concrete or asphalt batch plants, equipment staging yards, material storage areas, excavated material disposal areas, and borrow areas) if the following requirements are met:

      i. The support activity is directly related to the *construction site* required to have permit coverage for *stormwater discharges*; and

      ii. The support activity is not a commercial operation, nor does it serve multiple unrelated *construction sites*; and

      iii. The support activity does not continue to operate beyond the completion of the *construction activity* at the site it supports; and

      iv. *Stormwater* controls are implemented in accordance with Part II. and Part III. for *discharges* from the support activity areas.

2. The following non-*stormwater discharges* associated with *construction activity* are authorized under this permit:

   a. Non-*stormwater discharges* listed in 6 NYCRR 750-1.2(a)(29)(vi), with the following exception: "*Discharges* from firefighting activities are authorized only when the firefighting activities are emergencies/unplanned"; and

   b. Non-*stormwater discharges* of waters to which other components have not been added that are used in accordance with the *SWPPP* to control dust or irrigate vegetation in stabilized areas; and

   c. Uncontaminated *discharges* from *dewatering* operations

3. Authorized *discharges* of *stormwater* or authorized *discharges* of non-*stormwater*, commingled with a *discharge* authorized by a different SPDES permit and/or a *discharge* that does not require SPDES permit authorization, are also authorized under this permit.

C. Prohibited *Discharges*

1. Non-*stormwater discharges* prohibited under this permit include but are not limited to:

    a. Wastewater from washout of concrete; and

    b. Wastewater from washout and cleanout of stucco, paint, form release oils, curing compounds, and other construction materials; and

    c. Fuels, oils, or other *pollutants* used in vehicle and equipment operation and maintenance; and

    d. Soaps, solvents, or detergents used in vehicle and equipment washing or external building washdown; and

    e. Toxic or hazardous substances from a spill or other release.

D. Electronic Notice of Intent (eNOI) Submittal

To receive authorization in accordance with Part I.D.3.b., the *owner or operator* must submit a complete eNOI in accordance with the requirements in Part I.D. The eNOI contains questions to: ensure eligibility requirements in Part I.A. have been met; obtain *owner or operator* contact information; obtain the total area to be disturbed and the existing/future *impervious areas* (rounded to the nearest tenth of an acre); confirm *Traditional Land Use Control MS4 Operator* jurisdiction over construction projects; satisfy the EPA eRule requirements; confirm that the Water Quality-Based Effluent Limitations in Part II. have been met; demonstrate consideration of the future risks due to climate change in accordance with Part III.A.2.; and confirm that the other *Stormwater Pollution Prevention Plan (SWPPP)* requirements in Part III. have been met.

1. An eNOI may be submitted for:

    a. *construction activities* that are not part of a *common plan of development or sale*; or

b. an entire *common plan of development or sale*; or

c. separate *phase(s)* of a *common plan of development or sale* if the following requirements are met:

    i. the *common plan of development or sale* meets the eligibility requirements of Part I.A.5. or 6.; and

    ii. the *phase(s)* meet(s) all other eligibility requirements of Part I.A.; and

    iii. Part III.C. Required *SWPPP* Components by Project Type is based on the *common plan of development or sale*, not the *phase(s)*; or

d. *tree clearing* that is associated with, or will support, a *renewable energy* generation, transmission, or storage project that meets Part I.A.5. and 6., if the *tree clearing*:

    i. meets all other eligibility requirements of Part I.A.; and

    ii. will occur in NYSDEC's Regions 3-9; and

    iii. is not within ¼ mile of a bat hibernaculum protected pursuant to 6 NYCRR Part 182; and

    iv. will occur between November 1st and March 31st.

2. As prerequisites for submitting an eNOI, the *owner or operator* must:

    a. prepare a *SWPPP* for Part I.D.1.a., b., c., or d. in accordance with Part III.; and

    b. based on the following criteria, upload the following signature forms signed in accordance with Part VII.J. to the eNOI prior to submission:

        i. for all eNOIs:

            1. the SWPPP Preparer Certification Form, Appendix F, signed by the *SWPPP* preparer; and

2. the Owner/Operator Certification Form, Appendix J, signed by the *owner or operator*; and

ii. if an eNOI includes *construction activities* within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)* that will *discharge* to the *MS4(s)*:

1. determine if the *Traditional Land Use Control MS4 Operator(s)* have review authority. A *Traditional Land Use Control MS4 Operator* does not have review authority where:

a. the *owner or operator* of the *construction activities* in Part I.D.2.b.ii. is the same entity as the *Traditional Land Use Control MS4 Operator* identified in Part I.D.2.b.ii.; or

b. there is a statute exempting the *owner or operator* from zoning review by the *Traditional Land Use Control MS4 Operator*; or

c. there is no such statute per Part I.D.2.b.ii.1.b., the *Traditional Land Use Control MS4 Operator* concludes, after public hearing, that it does not have zoning review authority in accordance with Legal Memorandum LU14 Updated January 2020 “Governmental Immunity from Zoning and Other Legislation”; and

2. if the *Traditional Land Use Control MS4 Operator(s)* have review authority, submit the *SWPPP* to the *Traditional Land Use Control MS4 Operator(s)* for review and have:

a. if outside the municipal boundaries of NYC: the MS4 SWPPP Acceptance Form, Appendix G, signed by the principal executive officer or ranking elected official from the *Traditional Land Use Control MS4 Operator,* or by a duly authorized representative of that person in accordance with Part VII.J.2.; or

b. if within the municipal boundaries of NYC: The City of New York Department of Environmental Protection (NYCDEP) SWPPP Acceptance/Approval Form, Appendix H, signed by the principal executive officer or ranking elected official from the Traditional Land Use Control MS4 Operator, or by a duly authorized representative of that person in accordance with Part VII.J.2.; and

3. if the *Traditional Land Use Control MS4 Operator* does not have review authority, have the MS4 No Jurisdiction Form, Appendix I, signed by the principal executive officer or ranking elected official from the *Traditional Land Use Control MS4 Operator,* or by a duly authorized representative of that person in accordance with Part VII.J.2.

3. Submitting an eNOI:

a. The *owner or operator* must submit a complete Notice of Intent electronically using a NYSDEC approved form.[2]

b. The *owner or operator* is authorized to *commence construction activity* as of the authorization date indicated in the Letter of Authorization (LOA), which is sent by NYSDEC after a complete eNOI is submitted.

i. If an eNOI is received for a *SWPPP* that deviates from one of the technical standards but demonstrates *equivalence* in accordance with Part III.B.1.a.ii. or Part III.B.2.b.ii., if the *SWPPP* includes *construction activities* that are not within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)*, and/or if the *SWPPP* includes *construction activities* within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)* that do not have review authority in accordance with Part I.D.2.b.ii.1., the authorization date indicated in the LOA will be 60 business days after the eNOI submission date.

[2] Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

c. If *Traditional Land Use Control MS4 Operator(s)* have review authority in accordance with Part I.D.2.b.ii.2., the *owner or operator* must, within five business days of receipt of the LOA, send an electronic copy of the LOA to the *Traditional Land Use Control MS4 Operator(s)* with review authority.

E. General Requirements for *Owners or Operators* with Permit Coverage

1. As of the date the LOA is received, the *owner or operator* must make the eNOI, *SWPPP*, and LOA available for review and copying in accordance with the requirements in Part VII.H. When applicable, as of the date an updated LOA is received, the *owner or operator* must make the updated LOA available for review and copying in accordance with the requirements in Part VII.H.

2. The *owner or operator* must ensure compliance with all requirements of this permit and that the provisions of the *SWPPP*, including any changes made to the *SWPPP* in accordance with Part III.A.5., are properly implemented and maintained from the *commencement of construction activity* until:

   a. all areas of disturbance have achieved *final stabilization;* and

   b. the owner's or operator's coverage under this permit is terminated in accordance with Part V.A.5.a.

3. As of the date of the *commencement of construction activities* until Part I.E.2.a. and b. have been met, the *owner or operator* must maintain at the *construction site*, a copy of:

   a. all documentation necessary to demonstrate eligibility with this permit; and

   b. this permit; and

   c. the *SWPPP*; and

   d. the signed SWPPP Preparer Certification Form; and

   e. the signed MS4 SWPPP Acceptance Form or signed NYCDEP SWPPP Acceptance/Approval Form or signed MS4 No Jurisdiction Form (when applicable); and

   f. the signed Owner/Operator Certification Form; and

g. the eNOI; and

h. the LOA; and

i. the LOA transmittal to the Traditional Land Use Control MS4 Operator in accordance with Part I.D.3.c. (when applicable).

4. The *owner or operator* must maintain at the *construction site*, until Part I.E.2.a. and b. have been met, as of the date the documents become final or are received, a copy of the:

   a. responsible contractor's or subcontractor's certification statement(s) in accordance with Part III.A.7.; and

   b. inspection reports in accordance with Part IV.C.4. and 6.; and

   c. Request to Disturb Greater Than Five Acres and the Authorization Letter to Disturb Greater Than Five Acres in accordance with Part I.E.6. (when applicable); and

   d. Request to Continue Coverage and the Letter of Continued Coverage (LOCC) in accordance with Part I.F.2. and 4. (when applicable); and

   e. The updated LOA(s) in accordance with Part I.E.9. (when applicable).

5. The *owner or operator* must maintain the documents in Part I.E.3. and 4. in a secure location, such as a job trailer, on-site construction office, or mailbox with lock. The secure location must be accessible during normal business hours to an individual performing a compliance inspection. The documents must be paper documents unless electronic documents are accessible to the inspector during an inspection to the same extent as a paper copy stored at the site would be. If electronic documents are kept on site, the *owner or operator* must maintain functional equipment on site available to an inspector during normal hours of operation such that an inspector may view the electronic documents in a format that can be read in a similar manner as a paper record and in a legally dependable format with no less evidentiary value than their paper equivalent.

6. The *owner or operator* must meet the following requirements prior to disturbing greater than five acres of soil at any one time:

   a. The *owner or operator* must submit a written Request to Disturb Greater Than Five Acres to:

i. NYSDEC's Regional Office Division of Water staff based on the project location, Appendix E, if a *Traditional Land Use Control MS4 Operator* does not have review authority in accordance with Part I.D.2.b.ii.1.; or

ii. the *Traditional Land Use Control MS4 Operator*, if a *Traditional Land Use Control MS4 Operator* has review authority in accordance with Part I.D.2.b.ii.1.; or

iii. NYSDEC's Regional Office Division of Water staff based on the project location, Appendix E, and each involved *Traditional Land Use Control MS4 Operator*, if the project spans multiple municipalities with more than one *Traditional Land Use Control MS4 Operator* involved with review authority in accordance with Part I.D.2.b.ii.1.

b. The written Request to Disturb Greater Than Five Acres must include:

i. The SPDES permit identification number (Permit ID); and

ii. Full technical justification demonstrating why alternative methods of construction that would result in five acres of soil disturbance or less at any one time are not feasible; and

iii. The phasing plan for the project and sequencing plans for all *phases* from the *SWPPP* in accordance with Part III.B.1.d.; and

iv. Plans with locations and details of erosion and sediment control practices such that the heightened concern for erosion when disturbing greater than five acres at one time has been addressed; and

v. Acknowledgment that "the *owner or operator* will comply with the requirements in Part IV.C.2.b."; and

vi. Acknowledgment that "the *owner or operator* will comply with the requirements in Part II.B.1.b."

c. The *owner or operator* must be in receipt of an Authorization Letter to Disturb Greater Than Five Acres, which will include when the

authorization begins and ends and indicate a maximum area (acres) of soil disturbance allowed at any one time, from:

i. NYSDEC, if Part I.E.6.a.i. or iii. apply; or

ii. the *Traditional Land Use Control MS4 Operator*, if Part I.E.6.a.ii. applies.

7. Upon a finding of significant non-compliance with the practices described in the *SWPPP* or violation of this permit, NYSDEC may order an immediate stop to all *construction activity* at the site until the non-compliance is remedied. The stop work order must be in writing, describe the non-compliance in detail, and be sent to the *owner or operator*.

8. If any human remains or archaeological remains are encountered during excavation, the *owner or operator* must immediately cease, or cause to cease, all *construction activity* in the area of the remains and notify the appropriate Regional Water Engineer (RWE).[3] *Construction activity* shall not resume until written permission to do so has been received from the RWE.

9. To be authorized to implement modifications to the information previously submitted in the eNOI, the *owner or operator* must:

   a. notify NYSDEC via email at Stormwater_info@dec.ny.gov requesting access to update the eNOI; and

   b. update the eNOI to reflect the modifications and resubmit the eNOI in accordance with Part I.D.; and

   c. receive an updated LOA.

10. The eNOI, *SWPPP*, LOA, updated LOAs (when applicable), and inspection reports required by this permit are public documents that the *owner or operator* must make available for review and copying by any person within five business days of the *owner or operator* receiving a written request by any such person to review these documents. Copying of documents will be done at the requester's expense.

[3] The Regional Water Manager where a DEC Region does not have a RWE.

F. Permit Coverage for *Discharges* Authorized Under GP-0-20-001

When applicable:

1. Upon the effective date of this permit, an *owner or operator* of *a construction activity*, with coverage under GP-0-20-001, will have interim coverage under GP-0-25-001 for 45 calendar days starting on the effective date of GP-0-25-001 so long as the *owner or operator* maintains compliance with all applicable requirements of this permit.

2. Within 30 calendar days of the effective date of this permit, the *owner or operator*, with coverage under GP-0-20-001, must submit a complete Request to Continue Coverage electronically using a NYSDEC approved form,[4] which contains the information identified in Part I.F.3. below, if:

   a. the *owner or operator* continues to implement the SMP component in conformance with the technical standards in place at the time of initial project authorization; and

   b. the *owner or operator* will comply with all non-design requirements of GP-0-25-001.

3. The Request to Continue Coverage form contains questions to: ensure eligibility requirements in Part I.A. have been met; verify *owner or operator* contact information; verify the permit identification number; verify the original eNOI submission ID, if applicable; verify Part I.F.2.a. and b.; verify the version of the Design Manual that the technical/design components conform to; and receive an updated Owner/Operator Certification Form, Appendix I.

4. The *owner or operator* has obtained continued coverage under GP-0-25-001 as of the date indicated in the LOCC, which is sent by NYSDEC after a complete Request to Continue Coverage form is submitted.

5. If the owner or operator does not submit the Request to Continue Coverage form in accordance with Part I.F.2. and 3., coverage under this permit is automatically terminated after interim coverage expires.

[4] Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

G. Change of *Owner or Operator*

When applicable:

1. When property ownership changes, or when there is a change in operational control over the construction plans and specifications, the following process applies:

    a. The new *owner or operator* must meet the applicable prerequisites for submitting an eNOI in accordance with Part I.D.2.; and

    b. The new *owner or operator* must submit an eNOI in accordance with Part I.D.3.; and

    c. Permit coverage for the new *owner or operator* will be effective upon receipt of the LOA in accordance with Part I.D.3.b.; and

    d. The new *owner or operator*, upon receipt of their LOA, must provide their Permit ID to the original *owner or operator*; and

    e. If the original *owner or operator* will no longer be the *owner or operator* of the *construction activity* identified in the original *owner's or operator's* eNOI, the original *owner or operator*, upon receipt of the new *owner's or operator's* Permit ID in accordance with Part I.G.1.d., must submit to NYSDEC a completed eNOT in accordance with Part V. that includes the name and Permit ID of the new *owner or operator*; or

    f. If the original *owner or operator* maintains ownership of a portion of the *construction activity*, the original *owner or operator* must maintain their coverage under the permit by modifying their eNOI; modifications to the eNOI must include:

        i. the revised area of disturbance and/or *impervious area(s)*; and

        ii. the revised SMP information, if applicable; and

        iii. a narrative description of what has changed; and

        iv. the new *owner's or operator's* Permit ID for the portion of the project removed from the eNOI.

    Owners or operators must follow Part I.E.9. to modify the eNOI.

Part II. Water Quality-Based Effluent Limitations

A. Maintaining Water Quality

NYSDEC expects that compliance with the requirements of this permit will control *discharge*s necessary to meet applicable *water quality standards*. It shall be a violation of the *ECL* for any *discharge* to either cause or contribute to a violation of the following *water quality standards* as contained in Parts 700 through 705 of Title 6 of the Official Compilation of Codes, Rules and Regulations of the State of New York:

1. There must be no increase in turbidity that will cause a substantial visible contrast to natural conditions; and

2. There must be no increase in suspended, colloidal or settleable solids that will cause deposition or impair the waters for their best usages; and

3. There must be no residue from oil and floating substances, nor visible oil film, nor globules of grease.

If there is evidence indicating that the *stormwater discharge*s authorized by this permit are causing, have the reasonable potential to cause, or are contributing to a violation of the *water quality standard,* the *owner or operator* must take appropriate corrective action in accordance with Part IV.C.5. of this permit and document in accordance with Part IV.C.4. of this permit. To address the *water quality standard* violation the *owner or operator* must include and implement appropriate controls in the *SWPPP* to correct the problem or obtain an individual SPDES permit.

If, despite compliance with the requirements of this permit, it is demonstrated that the *stormwater discharge*s authorized by this permit are causing or contributing to a violation of *water quality standards*, or if NYSDEC determines that a modification of this permit is necessary to prevent a violation of *water quality standards*, the authorized *discharge*s will no longer be eligible for coverage under this permit, and the *owner or operator* must obtain an individual SPDES permit prior to further *discharges* from the *construction site*.

B. Effluent Limitations Applicable to *Discharges* from *Construction Activities*

*Discharge*s authorized by this permit must achieve, at a minimum, the effluent limitations in Part II.B.1.a., b., c., d., and e. These limitations represent the

degree of effluent reduction attainable by the application of best practicable technology currently available.

1. Erosion and Sediment Control Requirements - The *owner or operator* must select, design, install, implement, and maintain control measures to *minimize* the *discharge* of *pollutants* and prevent a violation of the *water quality standards*. The selection, design, installation, implementation, and maintenance of these control measures must meet the non-numeric effluent limitations in Part II.B.1.a., b., c., d., and e. and be in accordance with the New York State Standards and Specifications for Erosion and Sediment Control (BB), dated November 2016, using sound engineering judgment. Where control measures are not designed in conformance with the design criteria included in the technical standard, the *owner or operator* must include in *SWPPP* the reason(s) for the deviation, or alternative design, and provide information in the *SWPPP* demonstrating that the deviation or alternative design is *equivalent* to the technical standard.

    a. **Erosion and Sediment Controls.** At a minimum, erosion and sediment controls must be selected, designed, installed, implemented, and maintained to:

        i. *Minimize* soil erosion through application of runoff control and soil stabilization control measure to *minimize pollutant discharge*s; and

        ii. Control *stormwater discharge*s, including both peak flow rates and total *stormwater* volume, to *minimize* channel and *streambank* erosion and scour in the immediate vicinity of the *discharge* points; and

        iii. *Minimize* the amount of soil exposed during *construction activity*; and

        iv. *Minimize* the disturbance of *steep slope*; and

        v. *Minimize* sediment *discharge*s from the site; and

        vi. Provide and maintain *natural buffers* around surface waters, direct *stormwater* to vegetated areas and maximize *stormwater* infiltration to reduce *pollutant discharge*s, unless *infeasible*; and

        vii. *Minimize* soil compaction. *Minimizing* soil compaction is not required

where the intended function of a specific area of the site dictates that it be compacted; and

viii. Unless *infeasible*, preserve a sufficient amount of topsoil to complete soil restoration and establish a uniform, dense vegetative cover; and

ix. *Minimize* dust. On areas of exposed soil, *minimize* dust through the appropriate application of water or other dust suppression techniques to control the generation of *pollutants* that could be discharged from the site.

b. **Soil Stabilization**. In areas where soil disturbance activity has ceased, whether permanently or *temporarily ceased*, the application of soil stabilization measures must be initiated by the end of the next business day and completed within 14 calendar days from the date the current soil disturbance activity ceased. For *construction sites* that *directly discharge* to one of the 303(d) segments listed in Appendix D, or are located in one of the watersheds listed in Appendix C, or are authorized to disturb greater than five acres in accordance with Part I.E.5.a.viii., the application of soil stabilization measures must be initiated by the end of the next business day and completed within seven calendar days from the date the soil disturbance activity ceased.

c. **Dewatering**. *Discharge*s from *dewatering* activities, including *discharge*s from *dewatering* of trenches and excavations, must be managed by appropriate control measures.

d. **Pollution Prevention Measures**. Select, design, install, implement, and maintain effective pollution prevention measures to *minimize* the *discharge* of *pollutants* and prevent a violation of the *water quality standards*. At a minimum, such measures must be selected, designed, installed, implemented, and maintained to:

i. *Minimize* the *discharge* of *pollutants* from equipment and vehicle washing, wheel wash water, and other wash waters. Soaps, detergents and solvents cannot be used; and

ii. *Minimize* the exposure of building materials, building products, construction wastes, trash, landscape materials, fertilizers, pesticides, herbicides, detergents, sanitary waste, hazardous and toxic waste, and other materials present on the site to precipitation

and to *stormwater*. *Minimization* of exposure is not required in cases where the exposure to precipitation and to *stormwater* will not result in a *discharge* of *pollutants*, or where exposure of a specific material or product poses little risk of *stormwater* contamination (such as final products and materials intended for outdoor use); and

iii. Prevent the *discharge* of *pollutants* from spills and leaks and implement chemical spill and leak prevention and response procedures.

e. **Surface Outlets.** When discharging from basins and impoundments, the surface outlets must be designed, constructed, and maintained in such a manner that sediment does not leave the basin or impoundment and that erosion at or below the outlet does not occur.

C. Post-Construction Stormwater Management Practice (SMP) Requirements

1. The *owner or operator* of a *construction activity* that requires post-construction SMPs, in accordance with Part III.C., must select, design, install, implement, and maintain the SMPs to meet the *performance criteria* in the New York State Stormwater Management Design Manual, dated July 31, 2024 (DM), using sound engineering judgment. Where SMPs are not designed in conformance with the *performance criteria* in the DM, the *owner or operator* must include in the *SWPPP* the reason(s) for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the technical standard.

2. The *owner or operator* of a *construction activity*, that requires SMPs in accordance with Part III.C., must design the practices to meet the applicable *sizing criteria* in Part II.C.2.a., b., c., or d.

a. Sizing Criteria for *New Development*

i. Runoff Reduction Volume (RRv) and Water Quality Volume (WQv):

1. Reduce the total WQv by application of RR techniques and standard SMPs with RRv capacity. The total WQv must be calculated in accordance with the criteria in Section 4.2 of the DM; or

2. Minimum RRv and Treatment of Remaining Total WQv: *Construction activities* that cannot meet the requirements in Part II.C.2.a.i.1. due to *site limitations* must direct runoff from all newly constructed *impervious areas* to a RR technique or standard SMP with RRv capacity unless *infeasible*. The specific *site limitations* that prevent the reduction of 100% of the WQv must be documented in the *SWPPP*. For each *impervious area* that is not directed to a RR technique or standard SMP with RRv capacity, the *SWPPP* must include documentation which demonstrates that all options were considered and for each option explains why it is considered *infeasible*.

   In no case shall the runoff reduction achieved from the newly constructed *impervious areas* be less than the Minimum RRv as calculated using the criteria in Section 4.4 of the DM. The remaining portion of the total WQv that cannot be reduced must be treated by application of standard SMPs.

ii. Channel Protection Volume (CPv): Provide 24 hour extended detention of the post-developed 1-year, 24-hour storm event, remaining after runoff reduction. Where a CPv control orifice is provided, the minimum orifice size must be 3 inches, with acceptable external trash rack or orifice protection. The CPv requirement does not apply when:

   1. Reduction of the entire CPv is achieved by application of runoff reduction techniques or infiltration systems; or

   2. The 1-year post-development peak *discharge* is less than or equal to 2.0 cfs without detention or velocity controls; or

   3. The site *directly discharges* into a fifth order or larger water body (stream, river, or lake), or tidal waters, where the increase in smaller flows will not impact the stream bank or channel integrity. However, the point of *discharge* must be adequately protected against scour and erosion by the increased peak *discharge*.

iii. *Overbank* Flood Control Criteria (Qp): Requires storage to attenuate the post-development 10-year, 24-hour peak *discharge* rate (Qp) to predevelopment rates. The Qp requirement does not apply when:

1. the site *directly discharges* to tidal waters or fifth order or larger streams, or

2. A downstream analysis reveals that *overbank* control is not required.

iv. Extreme Flood Control Criteria (Qf): Requires storage to attenuate the post-development 100-year, 24-hour peak *discharge* rate (Qf) to predevelopment rates. The Qf requirement does not apply when:

1. the site *directly discharges* to tidal waters or fifth order or larger streams, or

2. A downstream analysis reveals that *overbank* control is not required.

b. *Sizing Criteria* for *New Development* in Enhanced Phosphorus Removal Watersheds

i. Runoff Reduction Volume (RRv) and Water Quality Volume (WQv):

1. Reduce the WQv by application of RR techniques and standard SMPs with RRv capacity. The total WQv is the runoff volume from the 1-year, 24-hour design storm over the post-developed watershed and must be calculated in accordance with the criteria in Section 4.3 of the DM; or

2. Minimum RRv and Treatment of Remaining Total WQv: *Construction activities* that cannot meet the criteria in Part II.C.2.b.i.1. due to *site limitations* must direct runoff from all newly constructed *impervious areas* to a RR technique or standard SMP with RRv capacity unless *infeasible*. The specific *site limitations* that prevent the reduction of 100% of the WQv must be documented in the *SWPPP*. For each *impervious area* that is not directed to a RR technique or standard SMP with RRv capacity, the *SWPPP* must include

documentation which demonstrates that all options were considered and for each option explains why it is considered *infeasible.*

In no case shall the runoff reduction achieved from the newly constructed *impervious areas* be less than the Minimum RRv as calculated using the criteria in Section 4.5 of the DM. The remaining portion of the total WQv that cannot be reduced must be treated by application of standard SMPs.

ii. Channel Protection Volume (CPv): Provide 24 hour extended detention of the post-developed 1-year, 24-hour storm event, remaining after runoff reduction. Where a CPv control orifice is provided, the minimum orifice size must be 3 inches, with acceptable external trash rack or orifice protection. The CPv requirement does not apply when:

1. Reduction of the entire CPv is achieved by application of runoff reduction techniques or infiltration systems; or

2. The 1-year post-development peak *discharge* is less than or equal to 2.0 cfs; or

3. The site *directly discharges* to tidal waters, or a fifth order or larger water body (stream, river, or lake) where the increase in smaller flows will not impact the stream bank or channel integrity. However, the point of *discharge* must be adequately protected against scour and erosion by the increased peak *discharge*.

iii. *Overbank* Flood Control Criteria (Qp): Requires storage to attenuate the post-development 10-year, 24-hour peak *discharge* rate (Qp) to predevelopment rates. The Qp requirement does not apply when:

1. the site *directly discharges* to tidal waters or fifth order or larger streams; or

2. A downstream analysis reveals that *overbank* control is not required.

iv. Extreme Flood Control Criteria (Qf): Requires storage to attenuate the post-development 100-year, 24-hour peak *discharge* rate (Qf) to predevelopment rates. The Qf requirement does not apply when:

1. the site *directly discharges* to tidal waters or fifth order or larger streams; or

2. A downstream analysis reveals that *overbank* control is not required.

c. *Sizing Criteria* for *Redevelopment Activity*

i. Water Quality Volume (WQv): The WQv treatment objective for *redevelopment activity* must be addressed by one of the following options, as outlined in Section 9.2.1. *Redevelopment activities* located in an Enhanced Phosphorus Removal Watershed (see Part III.B.3. and Appendix C) must calculate the WQv in accordance with Section 4.3 of the DM. All other *redevelopment activities* must calculate the WQv in accordance with Section 4.2 of the DM.

1. Reduce the existing *impervious cover* by a minimum of 25% of the total disturbed, *impervious area*. The Soil Restoration criteria in Section 5.1.6 of the DM must be applied to all newly created pervious areas; or

2. Capture and treat 100% of the required WQv, for a minimum of 25% of the disturbed redevelopment *impervious area*, by implementation of standard SMPs or reduced by application of runoff reduction techniques; or

3. Capture and treat 100% of the required WQv, for a minimum of 75% of the disturbed redevelopment *impervious area*, by implementation of a volume-based alternative SMP, as defined in Section 9.4 of the DM; or

4. Capture and treat 100% of the required WQv, for a minimum of 75% of the disturbed redevelopment *impervious area*, by implementation of a flow-through alternative SMP sized to treat the peak rate of runoff from the WQv design storm; or

5. Application of a combination of 1 through 4 above that provide a weighted average of at least two of the above methods. Application of this method must be in accordance with the criteria in Section 9.2.1(A)(V) of the DM; or

6. If there is an existing SMP located on the site that captures and treats runoff from the *impervious area* that is being disturbed, the WQv treatment option selected must, at a minimum, provide treatment equal to the treatment that was being provided by the existing practice(s) if that treatment is greater than the treatment required by options 1 through 5 above.

ii. Channel Protection Volume (CPv) is not required if there is 0% change to hydrology that increases the *discharge* rate and volume from the project site.

iii. *Overbank* Flood Control (Qp) is not required if there is 0% change to hydrology that increases the *discharge* rate from the project site.

iv. Extreme Flood Control (Qf) is not required if there is 0% change to hydrology that increases the *discharge* rate from the project site.

d. *Sizing Criteria* for Combination of *Redevelopment Activity* and *New Development*

Construction projects, that include both *new development* and *redevelopment activity*, must use SMPs that meet the *sizing criteria* calculated as an aggregate of the *sizing criteria* in Part II.C.2.a. or b. for the *new development* portion of the project and Part II.C.2.c. for the *redevelopment activity* portion of the project.

Part III. Stormwater Pollution Prevention Plan (SWPPP)

A. General *SWPPP* Requirements

1. A *SWPPP* must be prepared and implemented by the *owner or operator* of all *construction activity* covered by this permit. All authorized *discharges* must be identified in the *SWPPP*. The *SWPPP* must document the selection, design, installation, implementation and maintenance of the control measures and

practices that will be used to meet the effluent limitations in Part II.B. and, where applicable, the SMP requirements in Part II.C.

2. The *SWPPP* must demonstrate consideration in narrative format of the future physical risks due to climate change pursuant to the Community Risk and Resiliency Act (CRRA), 6 NYCRR Part 490, and associated guidance.

    a. The owner or operator must consider:

        i. the following physical risks due to climate change:

            (i) increasing temperature; and

            (ii) increasing precipitation; and

            (iii) increasing variability in precipitation, including chance of drought; and

            (iv) increasing frequency and severity of flooding; and

            (v) rising sea level; and

            (vi) increasing storm surge; and

            (vii) shifting ecology.

        ii. for each of the following:

            (i) overall site planning; and

            (ii) location, elevation, and sizing of:

                a. control measures and practices; and

                b. conveyance system(s); and

                c. detention system(s).

3. The *SWPPP* must describe the erosion and sediment control practices and where required, SMPs that will be used and/or constructed to reduce the *pollutants* in *stormwater discharges* and to assure compliance with the

requirements of this permit. In addition, the *SWPPP* must identify potential sources of pollution which may reasonably be expected to affect the quality of *stormwater discharges*.

4. All *SWPPPs*, that require the SMP component in accordance with Part III.B.2., must be prepared by a *qualified professional*.

5. The *owner or operator* must keep the *SWPPP* current so that, at all times, it accurately documents the erosion and sediment control practices that are being used or will be used during construction, and all SMPs that will be constructed on the site. At a minimum, the *owner or operator* must modify the *SWPPP*, including construction drawings:

   a. whenever the current provisions prove to be ineffective in *minimizing pollutants* in *stormwater discharges* from the site; and

   b. whenever there is a change in design, construction, or operation at the *construction site* that has or could have an effect on the *discharge* of *pollutants*; and

   c. to address issues or deficiencies identified during an inspection by the *qualified inspector,* NYSDEC, or other regulatory authority; and

   d. to document the final construction conditions in an as-built drawing.

6. NYSDEC may notify the *owner or operator* at any time that the *SWPPP* does not meet one or more of the minimum requirements of this permit. The notification must be in writing and identify the provisions of the *SWPPP* that require modification. Within fourteen (14) calendar days of such notification, or as otherwise indicated by NYSDEC, the *owner or operator* must make the required changes to the *SWPPP* and submit written notification to NYSDEC that the changes have been made. If the *owner or operator* does not respond to NYSDEC's comments in the specified time frame, NYSDEC may suspend the *owner's or operator's* coverage under this permit or require the *owner or operator* to obtain coverage under an individual SPDES permit in accordance with Part II.D.4.

7. Prior to the *commencement of construction activity*, the *owner or operator* must identify the contractor(s) and subcontractor(s) that will be responsible for installing, constructing, repairing, replacing, inspecting, and maintaining the erosion and sediment control practices included in the *SWPPP* and the

contractor(s) and subcontractor(s) that will be responsible for constructing the SMPs included in the *SWPPP*. The *owner or operator* must have each of the contractors and subcontractors identify at least one person from their company to be *trained contractor* that will be responsible for implementation of the *SWPPP*. The *owner or operator* must ensure that at least one *trained contractor* is on site daily when soil disturbance activities are being performed.

The *owner or operator* must have each of the contractors and subcontractors identified above sign a copy of the following certification statement below before the *commencement of construction activities*:

> "I hereby certify under penalty of law that I understand and agree to comply with the requirements of the *SWPPP* and agree to implement any corrective actions identified by the *qualified inspector* during a site inspection. I also understand that the *owner or operator* must comply with the requirements of the most current version of the New York State Pollutant Discharge Elimination System (SPDES) Construction General Permit (CGP) for Stormwater Discharges from Construction Activities and that it is unlawful for any person to cause or contribute to a violation of *water quality standards*. Furthermore, I am aware that there are significant penalties for submitting false information, that I do not believe to be true, including the possibility of fine and imprisonment for knowing violations"

In addition to providing the certification statement above, the certification page must also identify the specific elements of the *SWPPP* that each contractor and subcontractor will be responsible for and include the name and title of the person providing the signature; the name and title of the *trained contractor* responsible for *SWPPP* implementation; the name, address and telephone number of the contracting firm; the address (or other identifying description) of the site; and the date the certification statement is signed. The *owner or operator* must attach the certification statement(s) to the copy of the *SWPPP* that is maintained at the *construction site*. If new or additional contractors are hired to implement measures identified in the *SWPPP* after the *commencement of construction activities*, they must also sign the certification statement and provide the information listed above prior to performing *construction activities*.

B. Required *SWPPP* Contents

1. Erosion and sediment control component - The *owner or operator* must prepare a *SWPPP* that includes erosion and sediment control practices.

    a. Erosion and sediment control practices must be designed:

        i. in conformance with the BB; or

        ii. *equivalent* to the BB if deviating from Part III.B.1.a.i.

    b. If the erosion and sediment control practices are designed in conformance with Part III.B.1.a.ii., the *SWPPP* must include a demonstration of *equivalence* to the BB.

    c. At a minimum, the erosion and sediment control component of the *SWPPP* must include the following:

        i. Background information about the scope of the project, including the location, type and size of project; and

        ii. A site map/construction drawing(s) with north arrows for the project, including a general location map. At a minimum, the site map must show the total site area; all improvements; areas of disturbance; areas that will not be disturbed; existing vegetation; on-site and adjacent off-site surface water(s); floodplain/floodway boundaries; wetlands and drainage patterns that could be affected by the *construction activity*; existing and final contours; locations of different soil types with boundaries; material, waste, borrow or equipment storage areas located on adjacent properties; and location(s) of the *stormwater discharge*(s) and receiving surface water(s); and

        iii. A description of the soil(s) present at the site, including an identification of the Hydrologic Soil Group (HSG); and

        iv. A phasing plan for the project and sequencing plans for all *phases*, both of which must address clearing and grubbing, excavation and grading, utility and infrastructure installation, *final stabilization*,

and any other *construction activity* at the site that will result in soil disturbance.

1. The phasing plan must include:

    a. a map delineating and labeling the limits of soil disturbance for all *phases* of a project; and

    b. a table identifying the order and intended schedule of when each *phase* will begin and end its sequencing plan. The table must identify the total disturbed area for each *phase* at any one time and the total disturbed area for the overall project at any one time all on one timeline showing all overlapping quantities of disturbed area at any one time; and

2. A sequencing plan for a specific *phase* must include:

    a. a table indicating the order and intended schedule of *construction activities* within a *phase*, and corresponding construction drawings with a description of the work to be performed; and

    b. all permanent and *temporary stabilization* measures; and

v. A description of the minimum erosion and sediment control practices to be installed or implemented for each *construction activity* that will result in soil disturbance. Include a schedule that identifies the timing of initial placement or implementation of each erosion and sediment control practice and the minimum time frames that each practice should remain in place or be implemented; and

vi. A site map/construction drawing(s) showing the specific location(s), size(s), and length(s) of each erosion and sediment control practice; and

vii. The dimensions, material specifications, installation details, and operation and maintenance requirements for all erosion and sediment control practices. Include the location and sizing of any

temporary sediment basins and structural practices that will be used to divert flows from exposed soils; and

viii. A maintenance inspection schedule for the contractor(s) and subcontractor(s) identified in Part III.A.7. to ensure continuous and effective operation of the erosion and sediment control practices. The maintenance inspection schedule must be in accordance with the requirements in the BB technical standard; and

ix. A description of the pollution prevention measures that will be used to control litter, construction chemicals and construction debris from becoming a *pollutant* source in the *stormwater discharges*; and

x. A description and location of any *stormwater discharges* associated with industrial activity other than construction at the site, including, but not limited to, *stormwater discharges* from asphalt plants and concrete plants located on the *construction site*; and

xi. Identification of any elements of the design that are not in conformance with the design criteria in the BB technical standard. Include the reason for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the technical standard.

2. SMP component – The *owner or operator* of *construction activity* identified in Table 2 of Appendix B must prepare a *SWPPP* that includes SMPs.

   a. SMPs must be designed in conformance with the applicable *sizing criteria* in Part II.C.2.a., c., or d.; and

   b. SMPs must be designed in conformance with the *performance criteria*:

      i. in the DM; or

      ii. *equivalent* to the DM if deviating from Part III.B.2.b.i.; or

      iii. in the New York State Stormwater Management Design Manual, dated January 2015 (2015 Design Manual), or *equivalent* to it, if the following criteria are met:

1. The eNOI is submitted in accordance with Part I.D. before January 29, 2027 for *construction activities* that are either:

    a. subject to governmental review and approval:

        i. where the *owner or operator* made any application to that governmental entity prior to the effective date of this permit; and

        ii. such application included a *SWPPP* developed using the 2015 Design Manual or *equivalent* to it; or

    b. not subject to governmental review and approval:

        i. where a fiscal allocation for the *construction activities* has been developed and approved by a governmental entity; and

        ii. the *SWPPP* was developed using the 2015 Design Manual or *equivalent* to it; and

c. If SMPs are designed in conformance with Part III.B.2.b.ii., the *SWPPP* must include the reason(s) for the deviation or alternative design and a demonstration of *equivalence* to the DM; and

d. If SMPs are designed in conformance with Part III.B.2.b.iii., the *SWPPP* must include supporting information or documentation demonstrating that Part III.B.2.b.iii.1.a. or b. apply; and

e. The SMP component of the *SWPPP* must include the following:

    i. Identification of all SMPs to be constructed as part of the project, including which option the SMP designs conform to, either Part III.B.2.b.i., ii., or iii. Include the dimensions, material specifications and installation details for each SMP; and

    ii. A site map/construction drawing(s) showing the specific location and size of each SMP; and

iii. A Stormwater Modeling and Analysis Report that includes:

(i) Map(s) showing pre-development conditions, including watershed/subcatchments boundaries, flow paths/routing, and design points; and

(ii) Map(s) showing post-development conditions, including watershed/subcatchments boundaries, flow paths/routing, design points and SMPs; and

(iii) Results of *stormwater* modeling (i.e. hydrology and hydraulic analysis) for the required storm events. Include supporting calculations (model runs), methodology, and a summary table that compares pre- and post-development runoff rates and volumes for the different storm events; and

(iv) Summary table, with supporting calculations, which demonstrates that each SMP has been designed in conformance with the *sizing criteria* included in the DM; and

(v) Identification of any *sizing criteria* that is not required based on the requirements included in Part II.C.; and

(vi) Identification of any elements of the design that are not in conformance with the *performance criteria* in the DM. Include the reason(s) for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the DM.

iv. Soil testing results and locations (test pits, borings); and

v. Infiltration test results, when required in accordance with Part III.B.2.a.; and

vi. An operations and maintenance plan that includes inspection and maintenance schedules and actions to ensure continuous and effective operation of each SMP. The plan must identify the entity

that will be responsible for the long-term operation and maintenance of each practice; and

3. Enhanced Phosphorus Removal Standards - The *owner or operator* of *construction activity* identified in Table 2 of Appendix B that is located in a watershed identified in Appendix C must prepare a *SWPPP* that includes SMPs designed in conformance with the applicable *sizing criteria* in Part II.C.2.b., c., or d. and the *performance criteria* Enhanced Phosphorus Removal Standards included in the DM. At a minimum, the SMP component of the *SWPPP* must meet the requirements of Part III.B.2.

C. Required *SWPPP* Components by Project Type

Owners or operators of *construction activities*, identified in Table 1 of Appendix B, are required to prepare a *SWPPP* that only includes erosion and sediment control practices designed in accordance with Part III.B.1. *Owners or operators* of the *construction activities*, identified in Table 2 of Appendix B, must prepare a *SWPPP* that also includes SMPs designed in accordance with Part III.B.2 or 3.

For the entire area of disturbance, including the entire *common plan of development or sale* if applicable, the owner or operator must evaluate every bullet from Appendix B Table 1 and Table 2 separately. If bullets from both Table 1 and Table 2 apply, the *SWPPP* must include erosion and sediment control practices for all *construction activities* but SMPs for only those portions of the *construction activities* that fall under Table 2 bullet(s).

Part IV. Inspection and Maintenance Requirements

A. General Construction Site Inspection and Maintenance Requirements

1. The *owner or operator* must ensure that all erosion and sediment control practices (including pollution prevention measures), and all SMPs identified in the *SWPPP*, are inspected and maintained in accordance with Part IV.B. and C.

B. Contractor Maintenance Inspection Requirements

1. The *owner or operator* of each *construction activity*, identified in Tables 1 and 2 of Appendix B, must have a *trained contractor* inspect the erosion and sediment control practices and pollution prevention measures being

implemented within the active work area daily to ensure that they are being maintained in effective operating condition at all times. If deficiencies are identified, the contractor must:

a. if the corrective action does not require engineering design:

    i. begin implementing corrective actions within one business day; and

    ii. complete the corrective actions within five business days; or

b. if the corrective action requires engineering design:

    i. begin the engineering design process within five business days; and

    ii. complete the corrective action in a reasonable time frame but no later than within 60 calendar days.

2. For *construction sites* where soil disturbance activities have been temporarily suspended (e.g. winter shutdown) and *temporary stabilization* measures have been applied to all disturbed areas, the *trained contractor* can stop conducting the maintenance inspections in accordance with Part IV.B.1. The *trained contractor* must begin conducting the maintenance inspections in accordance with Part IV.B.1. as soon as soil disturbance activities resume.

3. For *construction sites* where soil disturbance activities have been shut down with partial project completion, the *trained contractor* can stop conducting the maintenance inspections in accordance with Part IV.B.1. if all areas disturbed as of the project shutdown date have achieved *final stabilization* and all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational.

C. *Qualified Inspector* Inspection Requirements

1. With the exception of the following *construction activities* identified in Tables 1 and 2 of Appendix B, a *qualified inspector* must conduct site inspections for all other *construction activities* identified in Tables 1 and 2 of Appendix B:

    a. the construction of a single-family residential subdivision with 25% or less *impervious cover* at total site build-out that involves a soil disturbance of one (1) or more acres of land but less than or equal to five (5) acres and is

not located in one of the watersheds listed in Appendix C and not *directly discharging* to one of the 303(d) segments listed in Appendix D; and

b. the construction of a single-family home that involves soil disturbances of one (1) or more acres but less than or equal to five (5) acres and is not located in one of the watersheds listed in Appendix C and not *directly discharging* to one of the 303(d) segments listed in Appendix D; and

c. construction on *agricultural property* that involves soil disturbances of one (1) or more acres but less than five (5) acres; and

d. *construction activities* located in the New York City Watershed located east of the Hudson River, see Appendix C Figure 1, that involve soil disturbances of 5,000 square feet or more, but less than one acre.

2. The *qualified inspector* must conduct site inspections in accordance with the following timetable:

a. For *construction sites* where soil disturbance activities are on-going, the *qualified inspector* must conduct a site inspection at least once every seven (7) calendar days; or

b. For *construction sites* where soil disturbance activities are on-going and the *owner or operator* has received authorization in accordance with Part I.E.6. to disturb greater than five (5) acres of soil at any one time, the *qualified inspector* must conduct at least two (2) site inspections every seven (7) calendar days. The two (2) inspections must be separated by a minimum of two (2) full calendar days; or

c. For *construction sites* where soil disturbance activities have been temporarily suspended (e.g. winter shutdown) and *temporary stabilization* measures have been applied to all disturbed areas, the *qualified inspector* must conduct a site inspection at least once every thirty (30) calendar days. The *owner or operator* must notify the DOW Water (SPDES) Program contact at the Regional Office (see contact information in Appendix E) or, in areas under the jurisdiction of a *Traditional Land Use Control MS4 Operator,* the *Traditional Land Use Control MS4 Operator* (provided the *Traditional Land Use Control MS4 Operator* is not the *owner or operator* of the *construction activity*) by hard copy or email prior to reducing the inspections to this frequency and again by hard copy or email prior to re-commencing construction; or

d. For *construction sites* where soil disturbance activities have been shut down with partial project completion, the requirement to have the *qualified inspector* conduct inspections ceases if all areas disturbed as of the project shutdown date have achieved *final stabilization* and all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational. The *owner or operator* must notify the DOW Water (SPDES) Program contact at the Regional Office (see contact information in Appendix E) or, in areas subject to the review authority of *Traditional Land Use Control MS4 Operator(s)* in accordance with Part I.D.2.b.ii.1., the *Traditional Land Use Control MS4 Operator(s)* (provided the *Traditional Land Use Control MS4 Operator(s)* are not the *owners or operators* of the *construction activity*) in writing prior to the shutdown and again in writing prior to resuming *construction activity*. If soil disturbance activities are not resumed within 2 years from the date of shutdown, the *owner or operator* must terminate coverage by meeting the requirements of Part V; or

e. For *construction sites* involving soil disturbance of one (1) or more acres that *directly discharge* to one of the 303(d) segments listed in Appendix D or is located in one of the watersheds listed in Appendix C, the *qualified inspector* must conduct at least two (2) site inspections every seven (7) calendar days. The two (2) inspections must be separated by a minimum of two (2) full calendar days.

3. At a minimum, the *qualified inspector* must inspect:

   a. all erosion and sediment control practices and pollution prevention measures to ensure integrity and effectiveness; and

   b. all SMPs under construction to ensure that they are constructed in conformance with the *SWPPP*; and

   c. all areas of disturbance that have not achieved *final stabilization*; and

   d. all points of *discharge* to *surface waters of the State* located within, or immediately adjacent to, the property boundaries of the *construction site*; and

   e. all points of *discharge* from the *construction site*.

4. The *qualified inspector* must prepare an inspection report subsequent to each and every inspection. At a minimum, the inspection report must include and/or address all of the following, for all *construction activities* except those listed in Part IV.C.1.:

   a. Permit identification number; and

   b. Date and time of inspection; and

   c. Name and title of person(s) performing inspection; and

   d. A description of the weather and soil conditions (e.g. dry, wet, saturated) at the time of the inspection, including the temperature at the time of the inspection; and

   e. A description of the condition of the runoff at all points of *discharge* from the *construction site*. This must include identification of any *discharges* of sediment from the *construction site*. Include *discharges* from conveyance systems (i.e. pipes, culverts, ditches, etc.) and overland flow; and

   f. A description of the condition of all *surface waters of the State* located within, or immediately adjacent to, the property boundaries of the *construction site* which receive runoff from disturbed areas. This must include identification of any *discharges* of sediment to the *surface waters of the State*; and

   g. Identification of all erosion and sediment control practices and pollution prevention measures that need repair or maintenance; and

   h. Identification of all erosion and sediment control practices and pollution prevention measures that were not installed properly or are not functioning as designed and need to be reinstalled or replaced; and

   i. Description and sketch (map) of areas with active soil disturbance activity, areas that have been disturbed but are inactive at the time of the inspection, and areas that have been stabilized (temporary and/or final) since the last inspection; and

   j. Estimates, in square feet or acres, of the following areas:

i. Total area with active soil disturbance (not requiring either *temporary stabilization* or *final stabilization*); and

ii. Total area with inactive soil disturbance (requiring either *temporary stabilization* or *final stabilization*); and

iii. Total area that has achieved *temporary stabilization*; and

iv. Total area that has achieved *final stabilization*; and

k. Current stage of construction of all SMPs and identification of all *construction activity* on site that is not in conformance with the *SWPPP* and technical standards; and

l. Corrective action(s) that must be taken to install, repair, replace or maintain erosion and sediment control practices and pollution prevention measures; and to correct deficiencies identified with the construction of the SMP(s); and

m. Identification and status of all corrective actions that were required by previous inspection; and

n. Digital photographs, with date stamp, that clearly show the condition of all practices that have been identified as needing corrective actions. The *qualified inspector* must attach color copies of the digital photographs to the inspection report being maintained onsite within seven (7) calendar days of the date of the inspection. The *qualified inspector* must also take digital photographs, with date stamp, that clearly show the condition of the practice(s) after the corrective action has been completed. The *qualified inspector* must attach paper color copies of the digital photographs to the inspection report that documents the completion of the corrective action work within seven (7) calendar days of that inspection.

5. Within one business day of the completion of an inspection, the *qualified inspector* must notify the *owner or operator*, and appropriate contractor or subcontractor identified in Part III.A.7., of any corrective actions that need to be taken. The contractor or subcontractor must:

a. if the corrective action does not require engineering design:

i. begin implementing corrective actions within one business day; and

ii. complete the corrective actions within five business days; or

b. if the corrective action requires engineering design:

i. begin the engineering design process within five business days; and

ii. complete the corrective action in a reasonable time frame but no later than within 60 calendar days.

6. All inspection reports must be signed by the *qualified inspector.* In accordance with Part I.E.3., the inspection reports must be maintained on site with the *SWPPP*.

Part V. How to Terminate CGP Coverage

A. Electronic Notice of Termination (eNOT) Submittal

The eNOT contains questions to ensure requirements in Part V.A. have been met.

1. An *owner or operator* must terminate coverage when one or more of the following requirements have been met:

a. Total project completion:

i. all *construction activity* identified in the *SWPPP* has been completed; and

ii. all areas of disturbance have achieved *final stabilization*; and

iii. all temporary, structural erosion and sediment control measures have been removed; and

iv. all SMPs have been constructed in conformance with the *SWPPP* and are operational; and

v. an as-built drawing has been prepared; or

b. Planned shutdown with partial project completion:

   i. all soil disturbance activities have ceased; and

   ii. all areas disturbed as of the project shutdown date have achieved *final stabilization*; and

   iii. all temporary, structural erosion and sediment control measures have been removed; and

   iv. all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational; and

   v. an as-built drawing has been prepared; or

c. In accordance with Part I.G. Change of Owner or Operator; or

d. The *owner or operator* has obtained coverage under an alternative general SPDES permit or an individual SPDES permit.

2. For *construction activities* that require *qualified inspector* inspections in accordance with Part IV.C.1. and have met Part V.A.1.a. or b., the *owner or operator* must have the *qualified inspector* perform a final site inspection prior to submitting the eNOT. The *qualified inspector* must, by signing the "Final Stabilization" and "Post-Construction Stormwater Management Practice(s)" certification statements on the eNOT, certify that all the requirements in Part V.A.1.a. or b. have been achieved.

3. For *construction activities* that are subject to the review authority of *Traditional Land Use Control MS4 Operator(s)* in accordance with Part I.D.2.b.ii.1. and meet Part V.A.1.a. or b., the *owner or operator* must have the *Traditional Land Use Control MS4 Operator(s)* sign the "MS4 Acceptance" statement on the eNOT in accordance with the requirements in Part VII.J. A *Traditional Land Use Control MS4 Operator* official, by signing this statement, determined that it is acceptable for the *owner or operator* to submit the eNOT in accordance with the requirements of this Part. A *Traditional Land Use Control MS4 Operator* can make this determination by performing a final site inspection themselves or by accepting the *qualified inspector*'s final site inspection certification(s) when required in Part V.A.2.

4. For *construction activities* that require SMPs and meet Part V.A.1.a. or b., the *owner or operator* must, prior to submitting the eNOT, ensure one of the following:

    a. for SMP(s) that were constructed by a private entity, but will be owned, operated, and maintained by a public entity, the SMP(s) and any right-of-way(s) needed to operate and maintain such practice(s) have been deeded to the municipality in which the practice(s) is located; or

    b. for SMP(s) that are privately owned, but will be operated and maintained by a public entity, an executed operation and maintenance agreement is in place with the municipality that will operate and maintain the SMP(s); or

    c. for SMP(s) that are privately owned, the *owner or operator* has a mechanism in place that requires operation and maintenance of the practice(s) in accordance with the operation and maintenance plan, such as a deed covenant in the *owner or operator's* deed of record; or

    d. for SMP(s) that are owned by a public or private institution (e.g. school, university, hospital), government agency or authority, or public utility, the *owner or operator* has policies and procedures in place that ensure operation and maintenance of the practices in accordance with the operation and maintenance plan.

5. An *owner or operator* that has met the requirements of Part V.A.1., 2., 3., and 4. must request termination of coverage under this permit by submitting a complete Notice of Termination form electronically using a NYSDEC approved form.[5]

    a. The owner's or operator's coverage is terminated as of the termination date indicated in the Letter of Termination (LOT), which is sent by NYSDEC after a complete eNOT is submitted.

[5] Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

Part VI. Record Retention and Reporting

A. Record Retention

The *owner or operator* must retain a copy of the documents listed in Part I.E.3. and a copy of the LOT for a period of at least five years from the date that NYSDEC accepts a complete NOT submitted in accordance with Part V.

B. Reporting

Except for the eNOI, the signature forms associated with the eNOI, and the eNOT, all other written correspondence requested by NYSDEC, including individual permit applications, must be sent to the address of the appropriate DOW (SPDES) Program contact at the Regional Office listed in Appendix E.

Part VII. Standard Permit Requirements

For the purposes of this permit, examples of contractors and subcontractors include: third-party maintenance and construction contractors.

A. Duty to Comply

The *owner or operator*, and all contractors or subcontractors, must comply with all requirements of this permit. Any non-compliance with the requirements of this permit constitutes a violation of the New York State Environmental Conservation Law (ECL), and its implementing regulations, and is grounds for enforcement action. Filing of a request for termination of coverage under this permit, or a notification of planned changes or anticipated non-compliance, does not limit, diminish or stay compliance with any requirements of this permit.

B. Need to Halt or Reduce Activity Not a Defense

The necessity to halt or reduce the *construction activity* regulated by this permit, in order to maintain compliance with the requirements of this permit, must not be a defense in an enforcement action.

C. Penalties

There are substantial criminal, civil, and administrative penalties associated with violating the requirements of this permit. Fines of up to $37,500 per day for each

violation and imprisonment for up to 15 years may be assessed depending upon the nature and degree of the offense.

D. False Statements

Any person who knowingly makes any false material statement, representation, or certification in any application, record, report, or other document filed or required to be maintained under this permit, including monitoring reports or reports of compliance or noncompliance must, upon conviction, be punished in accordance with ECL §71-1933 and or New York State Penal Law Articles 175 and 210.

E. Re-Opener Clause

Upon issuance of this permit, a determination has been made on the basis of a submitted Notice of Intent, plans, or other available information, that compliance with the specified permit requirements will reasonably protect classified water use and assure compliance with applicable *water quality standards*. Satisfaction of the requirements of this permit notwithstanding, if operation pursuant to this permit causes or contributes to a condition in contravention of State *water quality standards* or guidance values, or if NYSDEC determines that a modification is necessary to prevent impairment of the best use of the waters or to assure maintenance of *water quality standards* or compliance with other provisions of ECL Article 17 or the Clean Water Act (CWA), or any regulations adopted pursuant thereto, NYSDEC may require such modification and the Commissioner may require abatement action to be taken by the *owner or operator* and may also prohibit such operation until the modification has been implemented.

F. Duty to Mitigate

The *owner or operator*, and its contractors and subcontractors, must take all reasonable steps to *minimize* or prevent any *discharge* in violation of this permit which has a reasonable likelihood of adversely affecting human health or the environment.

G. Requiring Another General Permit or Individual SPDES Permit

NYSDEC may require any *owner or operator* authorized to *discharge* in accordance with this permit to apply for and obtain an individual SPDES permit or apply for authorization to *discharge* in accordance with another general SPDES permit.

1. Cases where an individual SPDES permit or authorization to discharge in accordance with another general SPDES permit may be required include, but is not limited to the following:

a. the *owner or operator* is not in compliance with the conditions of this permit or does not meet the requirements for coverage under this permit; and

b. a change has occurred in the availability of demonstrated technology or practices for the control or abatement of *pollutants* applicable to the *point source*; and

c. new effluent limitation guidelines or new source performance standards are promulgated that are applicable to *point sources* authorized to *discharge* in accordance with this permit; and

d. existing effluent limitation guidelines or new source performance standards that are applicable to *point sources* authorized to *discharge* in accordance with this permit are modified; and

e. a water quality management plan containing requirements applicable to such *point sources* is approved by NYSDEC; and

f. circumstances have changed since the time of the request to be covered so that the *owner or operator* is no longer appropriately controlled under this permit, or either a temporary or permanent reduction or elimination of the authorized *discharge* is necessary; and

g. the *discharge* is in violation of section 17-0501 of the ECL; and

h. the *discharge(s)* is a significant contributor of *pollutants*. In making this determination, NYSDEC may consider the following factors:

   i. the location of the *discharge(s)* with respect to *surface waters of the State*; and

   ii. the size of the *discharge(s)*; and

   iii. the quantity and nature of the *pollutants discharged* to *surface waters of the State*; and

   iv. other relevant factors including compliance with other provisions of ECL Article 17, or the CWA.

2. When NYSDEC requires any *owner or operator* authorized by this permit to apply for an individual SPDES permit as provided for in this subdivision, it must notify the *owner or operator* in writing that a permit application is required. This notice must include a brief statement of the reasons for this decision, an application

form, a statement setting a time for the *owner or operator* to file the application for an individual SPDES permit, and a deadline, not sooner than 180 days from the *owner's or operator's* receipt of the notification letter, whereby the authorization to *discharge* under this permit must be terminated. NYSDEC may grant additional time upon demonstration, to the satisfaction of the RWE,[6] that additional time to apply for an alternative authorization is necessary or where NYSDEC has not provided a permit determination in accordance with 6 NYCRR Part 621.

3. When an individual SPDES permit is issued to an *owner or operator* authorized to *discharge* under this permit for the same *discharge(s)*, this permit authorization for *construction activities* authorized under the individual SPDES permit is automatically terminated on the effective date of the individual SPDES permit unless termination is earlier in accordance with 6 NYCRR Part 750.

H. Duty to Provide Information

The *owner or operator* must furnish to NYSDEC, within five business days, unless otherwise set forth by NYSDEC, any information that NYSDEC may request to determine whether cause exists to determine compliance with this permit or to determine whether cause exists for requiring an individual SPDES permit in accordance with 6 NYCRR 750-1.21(e) (see Part VII.G. Requiring Another General Permit or Individual Permit).

The *owner or operator* must make available to NYSDEC, for inspection and copying, or furnish to NYSDEC within 25 business days of receipt of a NYSDEC request for such information, any information retained in accordance with this permit.

Except for Part I.D.4. and 5. and Part I.G., the following applies: where the *owner or operator* becomes aware that it failed to submit any relevant facts on the Notice of Intent, or submitted incorrect information in a Notice of Intent or in any report to NYSDEC, the *owner or operator* must submit such facts or corrected information to NYSDEC within five business days.

I. Extension

In the event a new permit is not issued and effective prior to the expiration of this permit, and this permit is extended pursuant to the State Administrative Procedure Act and 6 NYCRR Part 621, then the *owner or operator* with coverage under this permit may continue to operate and *discharge* in accordance with the requirements of this permit until a new permit is issued and effective.

[6] The Regional Water Manager where a DEC Region does not have a RWE.

J. Signatories and Certification

The Notice of Intent, Notice of Termination, and reports required by this permit must be signed as provided in 40 CFR §122.22.

1. All Notices of Intent and Notices of Termination must be signed as follows:

    a. For a corporation. By a responsible corporate officer. For the purpose of this section, a responsible corporate officer means:

        (i) a president, secretary, treasurer, or vice-president of the corporation in charge of a principal business function, or any other person who performs similar policy- or decision-making functions for the corporation; or

        (ii) the manager of one or more manufacturing, production or operating facilities, provided, the manager is authorized to make management decisions which govern the operation of the regulated facility including having the explicit or implicit duty of making major capital investment recommendations, and initiating and directing other comprehensive measures to assure long term environmental compliance with environmental laws and regulations; the manager can ensure that the necessary systems are established or actions taken to gather complete and accurate information for Notice of Intent or Notice of Termination requirements; and where authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures.

        Note: NYSDEC does not require specific assignments or delegations of authority to responsible corporate officers identified in 40 CFR §122.22(a)(1)(i). NYSDEC will presume that these responsible corporate officers have the requisite authority to sign the Notice of Intent or Notice of Termination unless the corporation has notified NYSDEC to the contrary. Corporate procedures governing authority to sign a Notice of Intent or Notice of Termination may provide for assignment or delegation to applicable corporate positions under 40 CFR §122.22(a)(1)(ii) rather than to specific individuals.

    b. For a partnership or sole proprietorship. By a general partner or the proprietor, respectively.

c. For a municipality, State, Federal, or other public agency. By either a principal executive officer or ranking elected official. For purposes of this section, a principal executive officer of a Federal agency includes:

    1. the chief executive officer of the agency; or

    2. a senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency (e.g., Regional Administrators of EPA).

2. All reports required by this permit, and other information requested by NYSDEC, must be signed by a person described in Part VII.J.1., or by a duly authorized representative of that person. A person is a duly authorized representative only if:

    a. The authorization is made in writing by a person described in Part VII.J.1. or using the Duly Authorized Form, found on the DEC website; and

    b. The authorization specifies either an individual or a position having responsibility for the overall operation of the regulated facility or activity, position of equivalent responsibility, or an individual or position having overall responsibility for environmental matters for the company. (A duly authorized representative may thus be either a named individual or any individual occupying a named position); and

    c. The written authorization is submitted to NYSDEC.

3. Changes to authorization. If an authorization under Part VII.J.2. is no longer accurate because a different individual or position has responsibility for the overall operation of the *construction activity*, a new authorization satisfying the requirements of Part VII.J.2. must be submitted to NYSDEC prior to or together with any reports, information, or applications to be signed by an authorized representative.

4. Certification. Any person signing a document under Part VII.J.1. or 2. must make the following certification:

    I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who

manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

5. Electronic reporting. If documents described in Part VII.J.1. or 2. are submitted electronically by or on behalf of the *construction activity* with coverage under this permit, any person providing the electronic signature for such documents must meet all relevant requirements of this section, and must ensure that all of the relevant requirements of 40 CFR Part 3 (including, in all cases, subpart D to Part 3) (Cross-Media Electronic Reporting) and 40 CFR Part 127 (NPDES Electronic Reporting Requirements) are met for that submission.

K. Inspection and Entry

The *owner or operator* must allow NYSDEC, the USEPA Regional Administrator, the applicable county health department, or any authorized representatives of those entities, or, in the case of a *construction site* which *discharges* through an *MS4*, an authorized representative of the *MS4* receiving the *discharge*, upon the presentation of credentials and other documents as may be required by law, to:

1. enter upon the *owner's or operator's* premises where a regulated facility or activity is located or conducted or where records must be kept under the requirements of this permit; and

2. have access to and copy at reasonable times, any records that must be kept under the requirements of this permit, including records required to be maintained for purposes of operation and maintenance; and

3. inspect at reasonable times any facilities, equipment (including monitoring and control equipment), practices or operations regulated or required under this permit; and

4. sample or monitor at reasonable times, for the purposes of assuring general SPDES permit compliance or as otherwise authorized by the CWA or ECL, any substances or parameters at any location; and

5. enter upon the property of any contributor to the regulated facility or activity under authority of the *owner or operator*.

L. Confidentiality of Information

The following must not be held confidential: this permit, the fact sheet for this permit, the name and address of any *owner or operator*, effluent data, the Notice of Intent, and information regarding the need to obtain an individual permit or an alternative general SPDES permit. This includes information submitted on forms themselves and any attachments used to supply information required by the forms (except information submitted on usage of substances). Upon the request of the *owner or operator*, NYSDEC must make determinations of confidentiality in accordance with 6 NYCRR Part 616, except as set forth in the previous sentence. Any information accorded confidential status must be disclosed to the Regional Administrator upon his or her written request. Prior to disclosing such information to the Regional Administrator, NYSDEC will notify the Regional Administrator of the confidential status of such information.

M. Other Permits May Be Required

Nothing in this permit relieves the *owner or operator* from a requirement to obtain any other permits required by law.

N. NYSDEC Orders or Civil Decrees/Judgments

The issuance of this permit by the NYSDEC, and the coverage under this permit by the *owner or operator*, does not supersede, revoke, or rescind any existing order on consent or civil Decree/Judgment, or modification to any such documents or to any order issued by the Commissioner, or any of the terms, conditions, or requirements contained in such order or modification therefore, unless expressly noted.

O. Property Rights

Coverage under this permit does not convey any property rights in either real or personal property, or any exclusive privileges, nor does it authorize any injury to private property or any invasion of personal rights, nor any infringement of Federal, State, or local laws or regulations, nor does it obviate the necessity of obtaining the assent of any other jurisdiction as required by law for the *discharge* authorized.

P. Compliance with Interstate Standards

If the *construction activity* covered by this permit originates within the jurisdiction of an interstate water pollution control agency, then the *construction activity* must also comply with any applicable effluent standards or *water quality standards* promulgated by that interstate agency and as set forth in this permit for such *construction activities*.

Q. Oil and Hazardous Substance Liability

Coverage under this permit does not affect the imposition of responsibilities upon, or the institution of any legal action against, the *owner or operator* under section 311 of the CWA, which must be in conformance with regulations promulgated pursuant to section 311 governing the applicability of section 311 of the CWA to *discharges* from facilities with *NPDES* permits, nor must such issuance preclude the institution of any legal action or relieve the *owner or operator* from any responsibilities, liabilities, or penalties to which the *owner or operator* is or may be subject pursuant to the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. section 9601 et seq. (CERCLA).

R. Severability

The provisions of this permit are severable, and if any provision of this permit, or the application of any provision of this permit to any circumstance, is held invalid, the application of such provision to other circumstances, and the remainder of this permit, must not be affected thereby.

S. NYSDEC Approved Forms

The *owner or operator* must provide all relevant information that is requested by NYSDEC, and required by this permit, on all NYSDEC approved forms.

APPENDIX A – Abbreviations and Definitions

Abbreviations

APO – Agency Preservation Officer
BB – New York State Standards and Specifications for Erosion and Sediment Control (Blue Book), dated November 2016
BMP – Best Management Practice
CPESC – Certified Professional in Erosion and Sediment Control
CPv – Channel Protection Volume
CWA – Clean Water Act (or the Federal Water Pollution Control Act, 33 U.S.C. §1251 et seq)
DM – New York State Stormwater Management Design Manual (Design Manual), dated July 31, 2024
DOW – Division of Water
EAF – Environmental Assessment Form
ECL – chapter 43-B of the Consolidated Laws of the State of New York, entitled the Environmental Conservation Law
EPA – U.S. Environmental Protection Agency
HSG – Hydrologic Soil Group
MS4 – Municipal Separate Storm Sewer System
NOI – Notice of Intent
NOT – Notice of Termination
NPDES – National Pollutant Discharge Elimination System
NYC – The City of New York
NYCDEP – The City of New York Department of Environmental Protection
NYSDEC – The New York State Department of Environmental Conservation
OPRHP – Office of Parks, Recreation and Historic Places
Qf – Extreme Flood
Qp – Overbank Flood
RR – Runoff Reduction
RRv – Runoff Reduction Volume
RWE – Regional Water Engineer
SEQR – State Environmental Quality Review Act
SHPA – State Historic Preservation Act
SMP – Post-Construction Stormwater Management Practice
SPDES – State Pollutant Discharge Elimination System
SWPPP – Stormwater Pollution Prevention Plan
TMDL – Total Maximum Daily Load
UPA – Uniform Procedures Act
USDA – United States Department of Agriculture
WQv – Water Quality Volume

Definitions

All definitions in this section are solely for the purposes of this permit. If a word is not italicized in the permit, use its common definition.

Agricultural Building – a structure designed and constructed to house farm implements, hay, grain, poultry, livestock or other horticultural products; excluding any structure designed, constructed or used, in whole or in part, for human habitation, as a place of employment where agricultural products are processed, treated or packaged, or as a place used by the public.

Agricultural Property – the land for construction of a barn, *agricultural building*, silo, stockyard, pen or other structural practices identified in Table II in the "Agricultural Best Management Practice Systems Catalogue" (dated June 2023).

Alter Hydrology from Pre- to Post-Development Conditions – the post-development peak flow rate(s) has increased by more than 5% of the pre-developed condition for the design storm of interest (e.g. 10 yr and 100 yr).

Combined Sewer System – a sewer system which conveys sewage and *stormwater* through a single pipe system to a publicly owned treatment works.

Commence (Commencement of) Construction Activities – the initial disturbance of soils associated with clearing, grading or excavation activities; or other construction related activities that disturb or expose soils such as demolition, stockpiling of fill material, and the initial installation of erosion and sediment control practices required in the *SWPPP*. See definition for "*Construction Activity(ies)*" also.

Common Plan of Development or Sale – a contiguous area where multiple separate and distinct *construction activities* are occurring, or may occur, under one plan. The "common plan" of development or sale is broadly defined as any announcement or piece of documentation (including a sign, public notice or hearing, marketing plan, advertisement, drawing, permit application, State Environmental Quality Review Act (SEQR) environmental assessment form or other documents, zoning request, computer design, etc.) or physical demarcation (including boundary signs, lot stakes, surveyor markings, etc.) indicating *construction activities* may occur on a specific plot. A *common plan of development or sale* is comprised of two or more *phases*.

Common plan of development or sale does not include separate and distinct *construction activities* that are occurring, or may occur, under one plan that are at least 1/4 mile apart provided any interconnecting road, pipeline or utility project that is part of the same "common plan" is not concurrently being disturbed.

Construction Activity(ies) – identified within 40 CFR 122.26(b)(14)(x), 122.26(b)(15)(i), and 122.26(b)(15)(ii), any clearing, grading, excavation, filling, demolition or stockpiling activities that result in soil disturbance. Clearing activities can include, but are not limited to, mechanized logging equipment operation, the cutting and skidding of trees, stump removal and/or brush root removal.

Construction activity does not include routine maintenance that is performed to maintain the original line and grade, hydraulic capacity, or original purpose of a facility, which is excluded from the calculation of the soil disturbance for a project. Routine maintenance includes, but is not limited to:

- Re-grading of gravel roads or parking lots; and
- Cleaning and shaping of existing roadside ditches and culverts that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity of the ditch; and
- Replacement of existing culverts that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity of a ditch; and
- Replacement of existing bridges that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity beneath the bridges; and
- Cleaning and shaping of existing roadside ditches that does not maintain the approximate original grade, hydraulic capacity and purpose of the ditch if the changes to the line and grade, hydraulic capacity or purpose of the ditch are installed to improve water quality and quantity controls (e.g. installing grass lined ditch); and
- Placement of aggregate shoulder backing that stabilizes the transition between the road shoulder and the ditch or *embankment*; and
- Full depth milling and filling of existing asphalt pavements, replacement of concrete pavement slabs, and similar work that does not expose soil or disturb the bottom six (6) inches of subbase material; and
- Long-term use of equipment storage areas at or near highway maintenance facilities; and
- Removal of sediment from the edge of the highway to restore a previously existing sheet-flow drainage connection from the highway surface to the highway ditch or *embankment*; and
- Existing use of Canal Corp owned upland disposal sites for the canal, and
- Replacement of curbs, gutters, sidewalks and guide rail posts; and
- Maintenance of ski trails including brush hog use and mowing; and
- Above ground snowmaking pipe replacement; and
- Replacement of existing utility poles; etc.

Construction Site – the land area where *construction activity(ies)* will occur. See also the definitions for "*Commence (Commencement of) Construction Activities"* and "*Common Plan of Development or Sale."*

Dewatering – the act of draining rainwater and/or groundwater from building foundations, vaults or excavations/trenches.

Directly Discharge(s)(ing) (to a specific surface waterbody) – runoff flows from a *construction site* by overland flow and the first point of *discharge* is the specific surface waterbody, or runoff flows from a *construction site* to a separate storm sewer system and the first point of *discharge* from the separate storm sewer system is the specific surface waterbody.

Discharge(s)(d) – any addition of any *pollutant* to waters of the State through an outlet or *point source*.

Embankment – an earthen or rock slope that supports a road/highway.

Equivalent (Equivalence) – the practice or measure meets all the performance, longevity, maintenance, and safety objectives of the technical standard and will provide an equal or greater degree of water quality protection.

Final Stabilization – all soil disturbance activities have ceased and a uniform, perennial vegetative cover with a density of eighty (80) percent over the entire pervious surface has been established; or other *equivalent* stabilization measures, such as permanent landscape mulches, rock rip-rap or washed/crushed stone have been applied on all disturbed areas that are not covered by permanent structures, concrete or pavement.

Historic Property – any building, structure, site, object or district that is listed on the State or National Registers of Historic Places or is determined to be eligible for listing on the State or National Registers of Historic Places.

Impervious Area (Cover) – all impermeable surfaces that cannot effectively infiltrate rainfall. This includes paved, concrete and compacted gravel surfaces (i.e. parking lots, driveways, roads, runways and sidewalks); building rooftops and miscellaneous impermeable structures such as patios, pools, and sheds.

Infeasible – not technologically possible, or not economically practicable and achievable considering best industry practices.

Minimize(ing)(ation) – reduce and/or eliminate to the extent achievable using control measures (including best management practices) that are technologically available and economically practicable and achievable in light of best industry practices.

Municipal Separate Storm Sewer System (MS4) - a conveyance or system of conveyances (including roads with drainage systems, municipal streets, catch basins, curbs, gutters, ditches, man-made channels, or storm drains):

1. owned or operated by a State, city, town, village, borough, county, parish, district, association, or other public body (created by or pursuant to State law) having jurisdiction over disposal of sewage, industrial wastes, *stormwater*, or other wastes, including special districts under State law such as a sewer district, flood control district or drainage district, or similar entity, or an Indian tribe or an authorized Indian tribal organization, or a designated and approved management agency under section 208 of the CWA, that *discharges* to *surface waters of the State*; and

2. designed or used for collecting or conveying *stormwater*; and

3. which is not a *combined sewer system*; and

4. which is not part of a Publicly Owned Treatment Works (POTW) as defined at 40 CFR 122.2.

Natural Buffer(s) – an undisturbed area with natural cover running along a surface water (e.g. wetland, stream, river, lake, etc.).

New Development – any land disturbance that does not meet the definition of *Redevelopment Activity* included in this appendix.

New York State Erosion and Sediment Control Certificate Program – a certificate program that establishes and maintains a process to identify and recognize individuals who are capable of developing, designing, inspecting and maintaining erosion and sediment control plans on projects that disturb soils in New York State. The certificate program is administered by the New York State Conservation District Employees Association.

Nonpoint Source(s) – any source of water pollution or *pollutants* which is not a discrete conveyance or *point source* permitted pursuant to Title 7 or 8 of Article 17 of the Environmental Conservation Law (see ECL Section 17-1403).

Overbank – flow events that exceed the capacity of the stream channel and spill out into the adjacent floodplain.

Owner or Operator – the person, persons, or legal entity which owns or leases the property on which the *construction activity* is occurring; an entity that has operational control over the construction plans and specifications, including the ability to make modifications to the plans and specifications; and/or an entity that has day-to-day operational control of those activities at a project that are necessary to ensure compliance with the permit requirements.

Performance Criteria – the six performance criteria for each group of SMPs in Chapters 5 and 6 of the technical standard, New York State Stormwater Management Design Manual (DM), dated July 31, 2024. These include feasibility, conveyance, pretreatment, treatment, landscaping, and maintenance. It does not include the *Sizing Criteria* (i.e. WQv, RRv, CPv, Qp and Qf) in Part I.C.2. of the permit.

Phase – a defined area in which *construction activities* are occurring or will occur separate from other defined area(s).

Point Source – any discernible, confined, and discrete conveyance, including but not limited to any pipe, ditch, channel, tunnel, conduit, well, discrete fissure, container, rolling stock, concentrated animal feeding operation, vessel or other floating craft, or landfill leachate collection system from which *pollutants* are or may be *discharged*.

Pollutant(s) – dredged spoil, filter backwash, solid waste, incinerator residue, sewage, garbage, sewage sludge, munitions, chemical wastes, biological materials, radioactive materials, heat, wrecked or discarded equipment, rock, sand and industrial, municipal, agricultural waste and ballast *discharged* into water; which may cause or might reasonably be expected to cause pollution of the waters of the state in contravention of the standards or guidance values adopted as provided in 6 NYCRR Parts 700 et seq.

Qualified Inspector – a person that is knowledgeable in the principles and practices of erosion and sediment control, such as a licensed Professional Engineer, Certified Professional in Erosion and Sediment Control (CPESC), Registered Landscape Architect, *New York State Erosion and Sediment Control Certificate Program* holder or other NYSDEC endorsed individual(s).

It can also mean someone working under the direct supervision of, and at the same company as, the licensed Professional Engineer or Registered Landscape Architect, provided that person has training in the principles and practices of erosion and sediment control. Training in the principles and practices of erosion and sediment control means that the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect has received four (4) hours of NYSDEC endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity. After receiving the initial training, the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect shall receive four (4) hours of training every three (3) years.

It can also mean a person that meets the *Qualified Professional* qualifications in addition to the *Qualified Inspector* qualifications.

Note: Inspections of any SMPs that include structural components, such as a dam for an impoundment, shall be performed by a licensed Professional Engineer.

Qualified Professional – a person that is knowledgeable in the principles and practices of *stormwater* management and treatment, such as a licensed Professional Engineer, Registered Landscape Architect or other NYSDEC endorsed individual(s). Individuals preparing *SWPPPs* that require the SMP component must have an understanding of the principles of hydrology, water quality management practice design, water quantity control design, and, in many cases, the principles of hydraulics. All components of the *SWPPP* that involve the practice of engineering, as defined by the NYS Education Law (see Article 145), shall be prepared by, or under the direct supervision of, a professional engineer licensed to practice in the State of New York.

Redevelopment Activity(ies) – the disturbance and reconstruction of existing *impervious area*, including *impervious areas* that were removed from a project site within five (5) years of preliminary project plan submission to the local government (i.e. site plan, subdivision, etc.).

Renewable Energy – electricity or thermal energy generated by renewable energy systems through use of the following technologies: solar thermal, photovoltaics, on land and offshore wind, hydroelectric, geothermal electric, geothermal ground source heat, tidal energy, wave energy, ocean thermal, and fuel cells which do not utilize a fossil fuel resource in the process of generating electricity.

Site Limitations – site conditions that prevent the use of an infiltration technique and or infiltration of the total WQv. Typical *site limitations* include: seasonal high groundwater, shallow depth to bedrock, and soils with an infiltration rate less than 0.5 inches/hour. The existence of *site limitations* shall be confirmed and documented using actual field testing (i.e. test pits, soil borings, and infiltration test) or using information from the most current United States Department of Agriculture (USDA) Soil Survey for the County where the project is located.

Sizing Criteria – the criteria included in Part I.C.2 of the permit that are used to size SMPs. The criteria include; Water Quality Volume (WQv), Runoff Reduction Volume (RRv), Channel Protection Volume (Cpv), *Overbank* Flood (Qp), and Extreme Flood (Qf).

Steep Slope – land area designated on the current United States Department of Agriculture (USDA) Soil Survey as Soil Slope Phase D, (provided the map unit name or description is inclusive of slopes greater than 25%), or Soil Slope Phase E or F, (regardless of the map unit name), or a combination of the three designations.

Stormwater – that portion of precipitation that, once having fallen to the ground, is in excess of the evaporative or infiltrative capacity of soils, or the retentive capacity of surface features, which flows or will flow off the land by surface runoff to waters of the State.

Streambank – the terrain alongside the bed of a creek or stream. The bank consists of the sides of the channel, between which the flow is confined.

Stormwater Pollution Prevention Plan (SWPPP) – a project specific report, including construction drawings, that among other things: describes the *construction activity(ies)*, identifies the potential sources of pollution at the *construction site*; describes and shows the *stormwater* controls that will be used to control the *pollutants* (i.e. erosion and sediment controls; for many projects, includes SMPs); and identifies procedures the *owner or operator* will implement to comply with the requirements of the permit. See Part III of the permit for a complete description of the information that must be included in the *SWPPP*.

Surface Waters of the State – shall be construed to include lakes, bays, sounds, ponds, impounding reservoirs, springs, rivers, streams, creeks, estuaries, marshes, inlets, canals, the Atlantic ocean within the territorial seas of the state of New York and all other bodies of surface water, natural or artificial, inland or coastal, fresh or salt, public or private (except those private waters that do not combine or effect a junction with natural surface waters), which are wholly or partially within or bordering the state or within its jurisdiction. Waters of the state are further defined in 6 NYCRR Parts 800 to 941.

Temporarily Ceased – an existing disturbed area will not be disturbed again within 14 calendar days of the previous soil disturbance.

Temporary Stabilization – exposed soil has been covered with material(s) as set forth in the technical standard, New York Standards and Specifications for Erosion and Sediment Control, to prevent the exposed soil from eroding. The materials can include, but are not limited to, mulch, seed and mulch, and erosion control mats (e.g. jute twisted yarn, excelsior wood fiber mats).

Total Maximum Daily Load (TMDL) – the sum of the allowable loads of a single *pollutant* from all contributing point and *nonpoint source*s. It is a calculation of the maximum amount of a *pollutant* that a waterbody can receive and still meet *water quality standards*, and an allocation of that amount to the *pollutant's* sources. A TMDL stipulates Waste Load Allocations (WLA) for *point source discharges*, Load Allocations (LA) for *nonpoint source*s, and a margin of safety (MOS).

Traditional Land Use Control MS4 Operator – a city, town, or village with land use control authority that is authorized to *discharge* under New York State DEC's SPDES General Permit For Stormwater Discharges from Municipal Separate Stormwater Sewer Systems (MS4s) or the City of New York's Individual SPDES Permit for their Municipal Separate Storm Sewer Systems (NY-0287890).

Trained Contractor – an employee from the contracting (construction) company, identified in Part III.A.7., that has received four (4) hours of NYSDEC endorsed training

in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity. After receiving the initial training, the *trained contractor* shall receive four (4) hours of training every three (3) years.

It can also mean an employee from the contracting (construction) company, identified in Part III.A.7., that meets the *qualified inspector* qualifications (e.g. licensed Professional Engineer, Certified Professional in Erosion and Sediment Control (CPESC), Registered Landscape Architect, *New York State Erosion and Sediment Control Certificate Program* holder, or someone working under the direct supervision of, and at the same company as, the licensed Professional Engineer or Registered Landscape Architect, provided they have received four (4) hours of NYSDEC endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity).

The *trained contractor* is responsible for the day-to-day implementation of the *SWPPP*.

Tree Clearing – *construction activities* limited to felling and removal of trees.

Tree clearing does not include hand felling and leaving the trees in place with no support from mechanized equipment, which is not considered *construction activity* requiring coverage under this permit.

Water Quality Standard – such measures of purity or quality for any waters in relation to their reasonable and necessary use as promulgated in 6 NYCRR Part 700 et seq.

APPENDIX B – Required SWPPP Components by Project Type

Table 1
CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A *SWPPP* THAT ONLY INCLUDES EROSION AND SEDIMENT CONTROLS

The following *construction activities* that involve soil disturbances of one (1) or more acres of land, but less than five (5) acres:

- Single-family home not located in one of the watersheds listed in Appendix C and not *directly discharging* to one of the 303(d) segments listed in Appendix D
- Single-family residential subdivisions with 25% or less *impervious cover* at total site build-out and not located in one of the watersheds listed in Appendix C and not *directly discharging* to one of the 303(d) segments listed in Appendix D
- Construction of a barn or other *agricultural building*, silo, stock yard or pen.
- Structural agricultural conservation practices as identified in Table II in the "Agricultural Best Management Practice Systems Catalogue" (dated June 2023) that include construction or reconstruction of *impervious area* or *alter hydrology from pre- to post-development* conditions.

The following *construction activities* that involve soil disturbances between five thousand (5000) square feet and one (1) acre of land:

- All construction activities located in the New York City Watershed located east of the Hudson River, see Appendix C Figure 1, that involve soil disturbances between five thousand (5,000) square feet and one (1) acre of land.

Within the municipal boundaries of NYC:

- Stand-alone road reconstruction, where the total soil disturbance from only that road construction, is less than one (1) acre of land.

The following *construction activities*:

- Installation of underground linear utilities; such as gas lines, fiber-optic cable, cable TV, electric, telephone, sewer mains, and water mains
- Environmental enhancement projects, such as wetland mitigation, *stormwater* retrofits, stream restoration, and resiliency projects that reconstruct shoreline areas to address sea level rise
- Pond construction
- Linear bike paths running through areas with vegetative cover, including bike paths surfaced with an *impervious cover*
- Cross-country ski trails, walking/hiking trails, and mountain biking trails, including a de minimis parking lot (maximum 10 spaces total, sized for passenger cars) with 35 feet minimum preservation of undisturbed area downgradient from the parking lot
- Dam rehabilitation (the structure of the dam itself)
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are not part of residential, commercial, or institutional development;
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that include incidental shoulder or curb work along an existing highway to support construction of the sidewalk, bike path, or walking path.

Table 1 (Continued)
CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A *SWPPP* THAT ONLY INCLUDES EROSION AND SEDIMENT CONTROLS

The following *construction activities*:

- Slope stabilization
- Slope flattening that changes the grade of the site, but does not significantly change the runoff characteristics
- Spoil areas that will be covered with vegetation
- Vegetated open space (i.e. recreational parks, lawns, meadows, fields, downhill ski trails) that do not *alter hydrology from pre- to post-development* conditions
- Athletic fields (natural grass) that do not include the construction or reconstruction of *impervious area* and do not *alter hydrology from pre- to post-development* conditions
- Demolition where vegetation will be established, and no *redevelopment activity* is planned[1]
- Installation or replacement of either an overhead electric transmission line or a ski lift tower that does not include the construction of permanent access roads or parking areas surfaced with *impervious cover*.
- Solar array field areas that have tables elevated off the ground, spaced one table width apart, do not *alter hydrology from pre- to post-development conditions*, and address water quality volume and runoff reduction volume by maintaining sheet flow on slopes less than 8%.
- Structural agricultural conservation practices as identified in Table II in the "Agricultural Best Management Practice Systems Catalogue" (dated June 2023) that do not include construction or reconstruction of *impervious area* and do not *alter hydrology from pre- to post-development* conditions.
- Temporary access roads, median crossovers, detour roads, lanes, or other temporary *impervious areas* that will be restored to pre-construction conditions once the *construction activity* is complete (in this context, "temporary" means the *impervious area* will be in place for two years or less)
- Other *construction activities* that do not include the construction or reconstruction of *impervious area*, and do not *alter hydrology from pre- to post-development* conditions, and are not listed in Table 2.

1. If the site is redeveloped in the future, a new eNOI must be submitted.

Table 2
CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A *SWPPP* THAT INCLUDES POST-CONSTRUCTION STORMWATER MANAGEMENT PRACTICES (SMPS)

The following *construction activities*:

- Single-family home located in one of the watersheds listed in Appendix C or *directly discharging* to one of the 303(d) segments listed in Appendix D
- Single-family home that disturbs five (5) or more acres of land
- Single-family residential subdivisions located in one of the watersheds listed in Appendix C or *directly discharging* to one of the 303(d) segments listed in Appendix D
- Single-family residential subdivisions that involve soil disturbances of between one (1) and five (5) acres of land with greater than 25% *impervious cover* at total site build-out
- Single-family residential subdivisions that involve soil disturbances of between 20,000 square feet and one (1) acre of land within the municipal boundaries of NYC with greater than 25% *impervious cover* at total site build-out
- Single-family residential subdivisions that involve soil disturbances of five (5) or more acres of land, and single-family residential subdivisions that involve soil disturbances of less than five (5) acres that are part of a *common plan of development or sale* that will ultimately disturb five (5) or more acres of land
- Multi-family residential developments; includes duplexes, townhomes, condominiums, senior housing complexes, apartment complexes, and mobile home parks
- Creation of 5,000 square feet or more of *impervious area* in the municipal boundaries of NYC
- Airports
- Amusement parks
- Breweries, cideries, and wineries, including establishments constructed on agricultural land
- Campgrounds
- Cemeteries that include the construction or reconstruction of *impervious area* (>5% of disturbed area) or *alter the hydrology from pre- to post-development* conditions
- Commercial developments
- Churches and other places of worship
- Construction of a barn or other *agricultural building* (e.g. silo) that involves soil disturbance greater than five acres.
- Structural agricultural conservation practices as identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023) that involves soil disturbance greater than five acres and include the construction or reconstruction of *impervious area* or *alter hydrology from pre- to post-development* conditions.
- Facility buildings, including ski lodges, restroom buildings, pumphouses, ski lift terminals, and maintenance and groomer garages
- Institutional development; includes hospitals, prisons, schools and colleges
- Industrial facilities; includes industrial parks
- Landfills; including creation of landfills or capping landfills.
- Municipal facilities; includes highway garages, transfer stations, office buildings, POTWs, water treatment plants, and water storage tanks
- Golf courses
- Office complexes

Table 2 (Continued)

CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A *SWPPP* THAT INCLUDES POST-CONSTRUCTION STORMWATER MANAGEMENT PRACTICES (SMPS)

The following *construction activities*:

- Permanent laydown yards and equipment storage lots
- Playgrounds that include the construction or reconstruction of *impervious area*
- Sports complexes
- Racetracks; includes racetracks with earthen (dirt) surfaces
- Road construction or reconstruction, outside the municipal boundaries of NYC
- Road construction within the municipal boundaries of NYC
- Stand-alone road reconstruction, within the municipal boundaries of NYC where the total soil disturbance from that road reconstruction involves soil disturbance of one (1) acre or more of land
- Parking lot construction or reconstruction (as with all Table 2 bullets, this includes parking lots constructed as part of the *construction activities* listed in Table 1, unless a Table 1 bullet specifies otherwise)
- Athletic fields (natural grass) that include the construction or reconstruction of *impervious area* (>5% of disturbed area) or *alter the hydrology from pre- to post-development* conditions
- Athletic fields with artificial turf
- Permanent access roads, parking areas, substations, compressor stations, and well drilling pads, surfaced with *impervious cover,* and constructed as part of an overhead electric transmission line, wind-power, cell tower, oil or gas well drilling, sewer or water main, ski lift, or other linear utility project
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are part of a residential, commercial or institutional development
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are part of highway construction or reconstruction
- Solar array field areas on slopes greater than 8% that cannot maintain sheet flow using management practices identified in the BB or the DM
- Solar array field areas on slopes less than 8% that will *alter the hydrology from pre- to post-development* conditions
- Solar array field areas with tables that are not elevated high enough to achieve *final stabilization* beneath the tables
- Traditional *impervious areas* associated with solar development (e.g. roads, buildings, transformers)
- Utility pads surfaced with *impervious cover*, including electric vehicle charging stations
- All other *construction activities* that include the construction or reconstruction of *impervious area* or *alter the hydrology from pre- to post-development* conditions, and are not listed in Table 1

APPENDIX C – Watersheds Requiring Enhanced Phosphorus Removal

Watersheds where *owners or operators* of *construction activities* identified in Table 2 of Appendix B must prepare a *SWPPP* that includes SMPs designed in conformance with the Enhanced Phosphorus Removal Standards included in the DM technical standard.

- Entire New York City Watershed located east of the Hudson River – Figure 1
- Onondaga Lake Watershed – Figure 2
- Greenwood Lake Watershed – Figure 3
- Oscawana Lake Watershed – Figure 4
- Kinderhook Lake Watershed – Figure 5

Figure 1 - New York City Watershed East of the Hudson

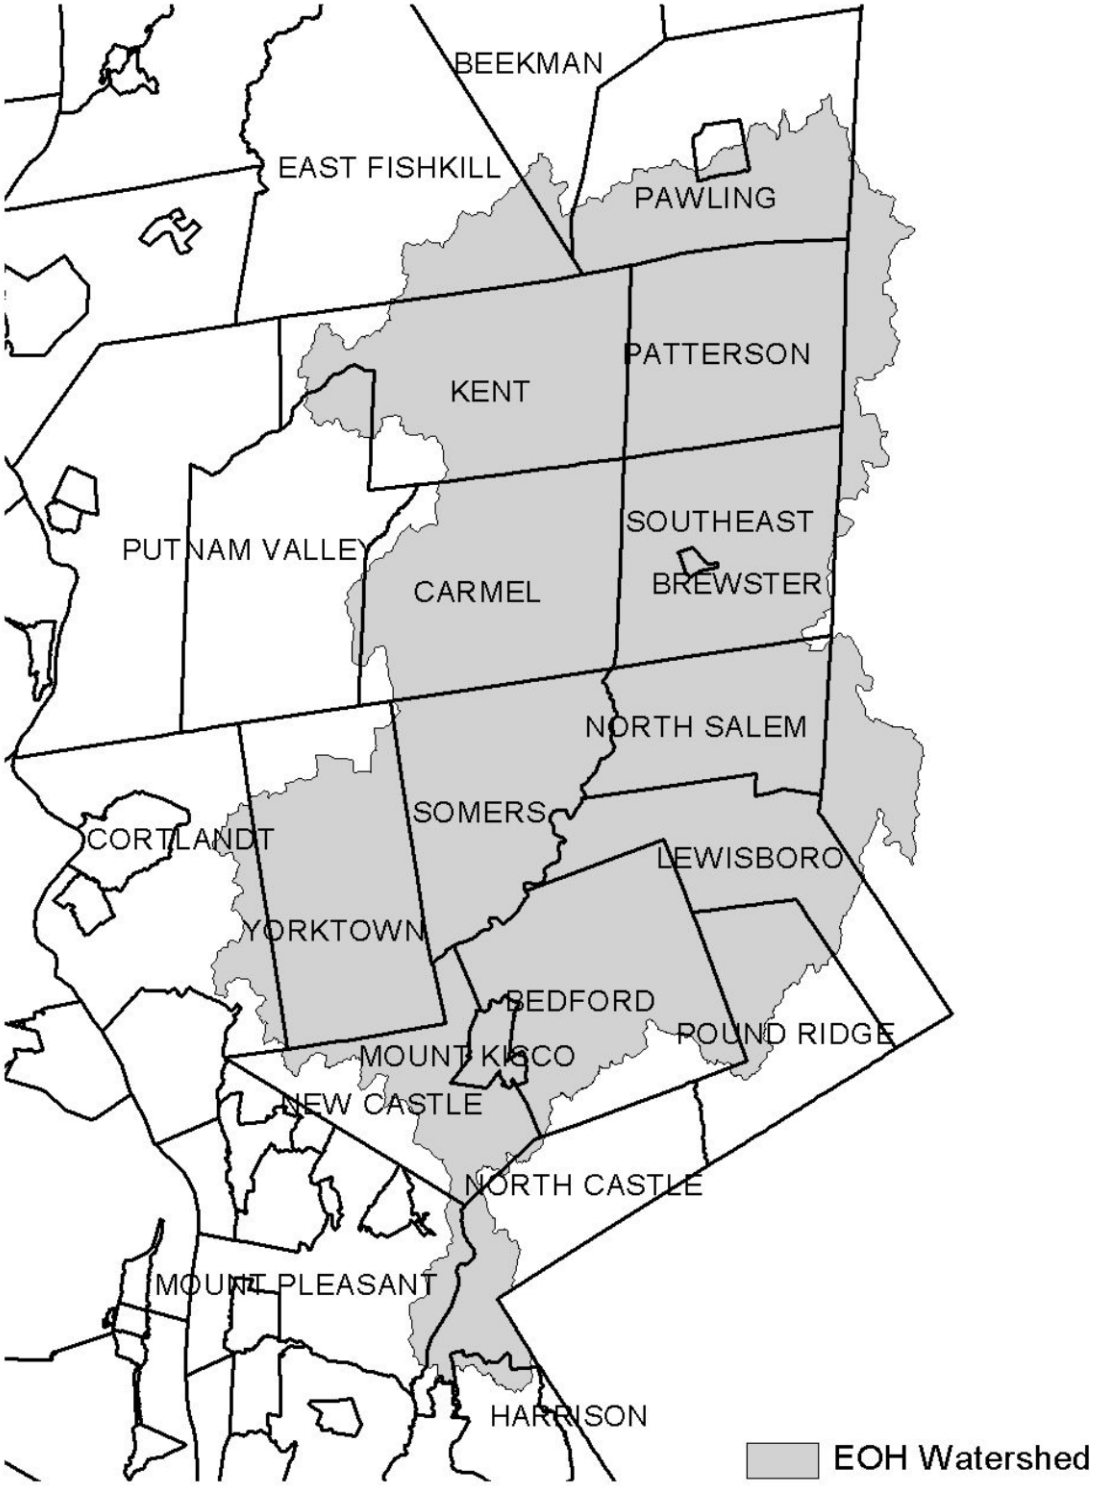

Figure 2 - Onondaga Lake Watershed



Figure 3 - Greenwood Lake Watershed

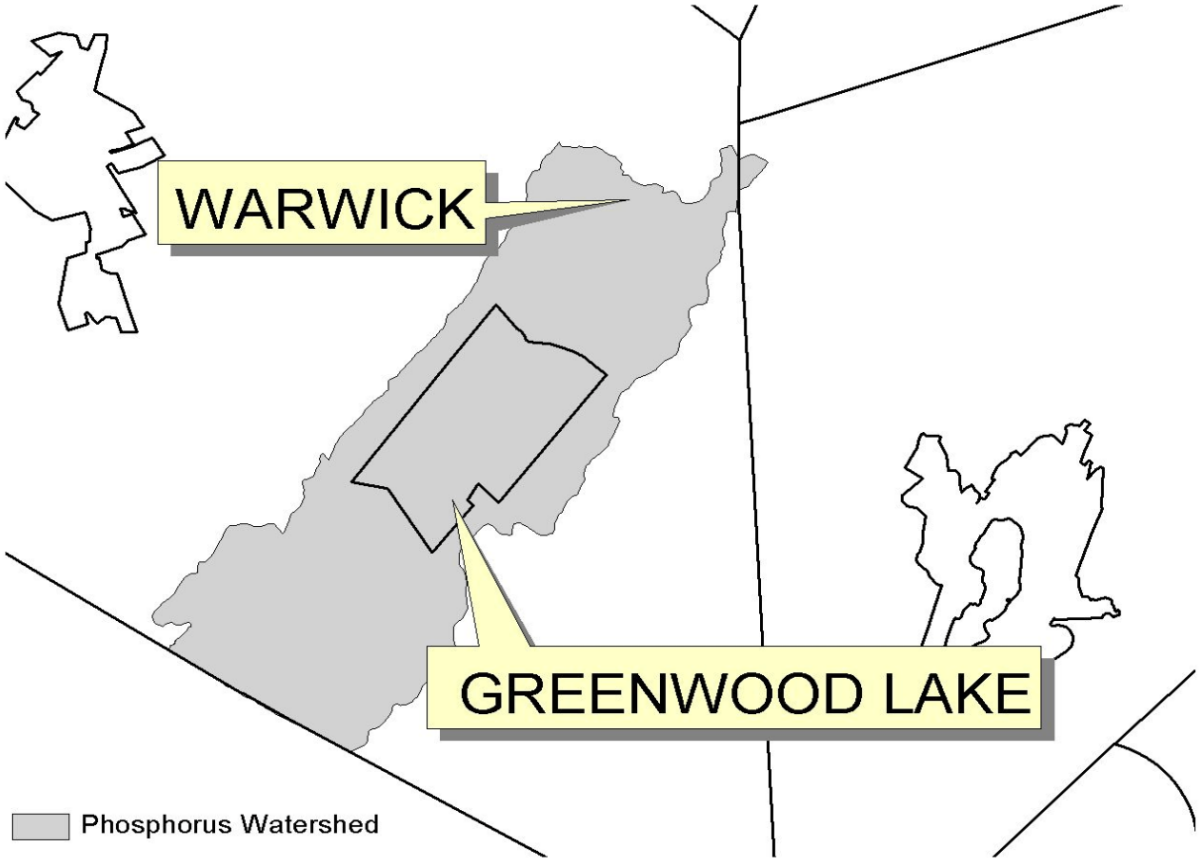

Figure 4 - Oscawana Lake Watershed

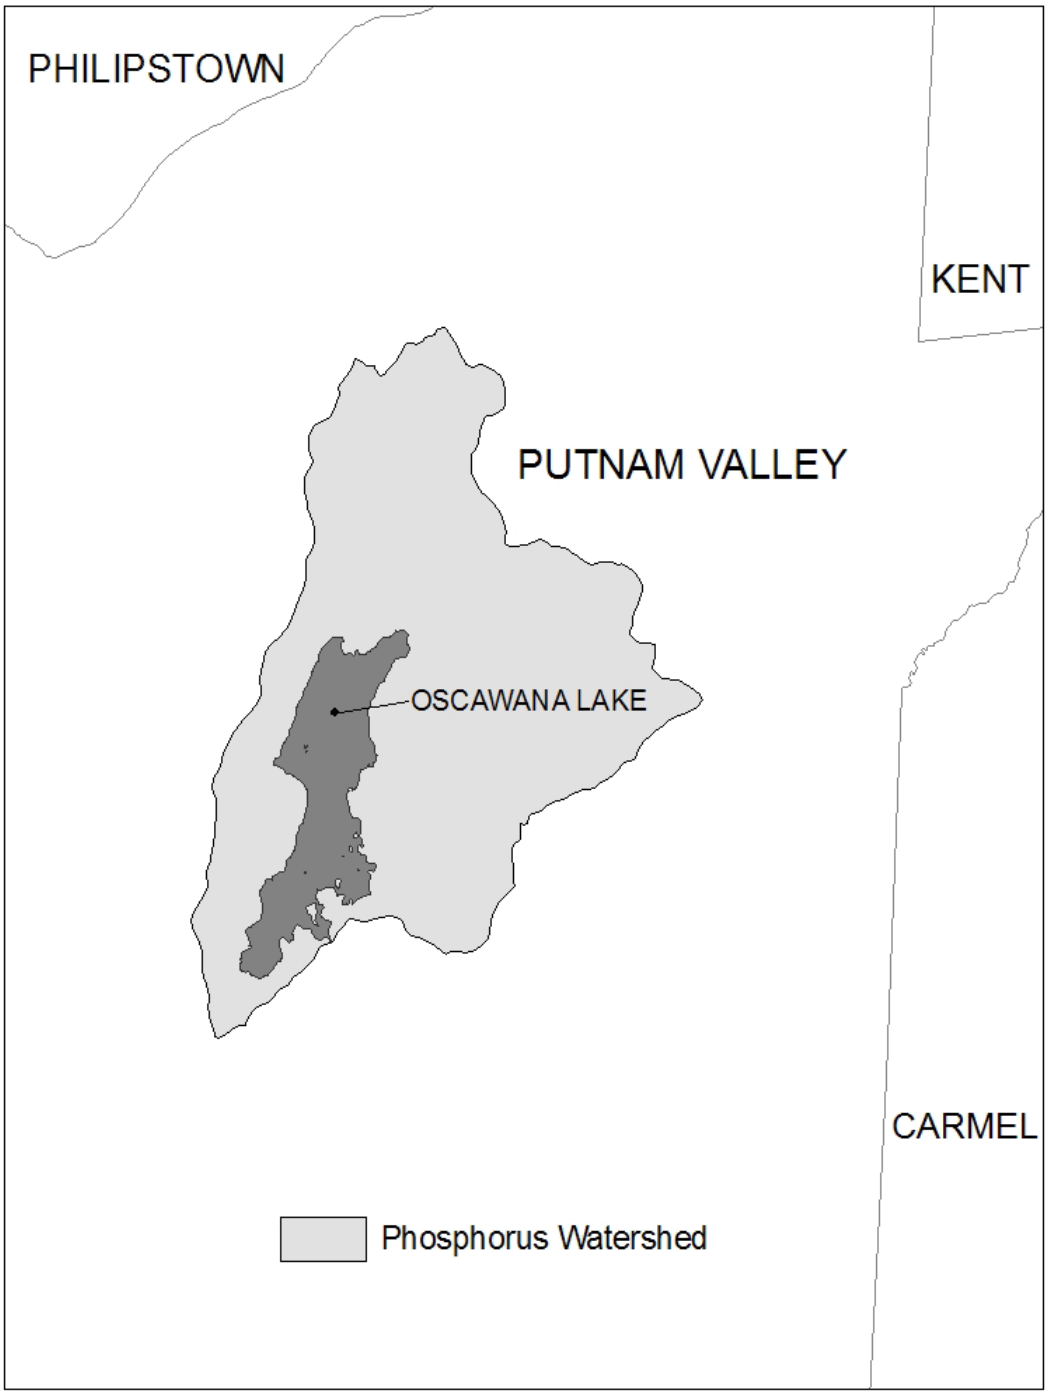

Figure 5 - Kinderhook Lake Watershed

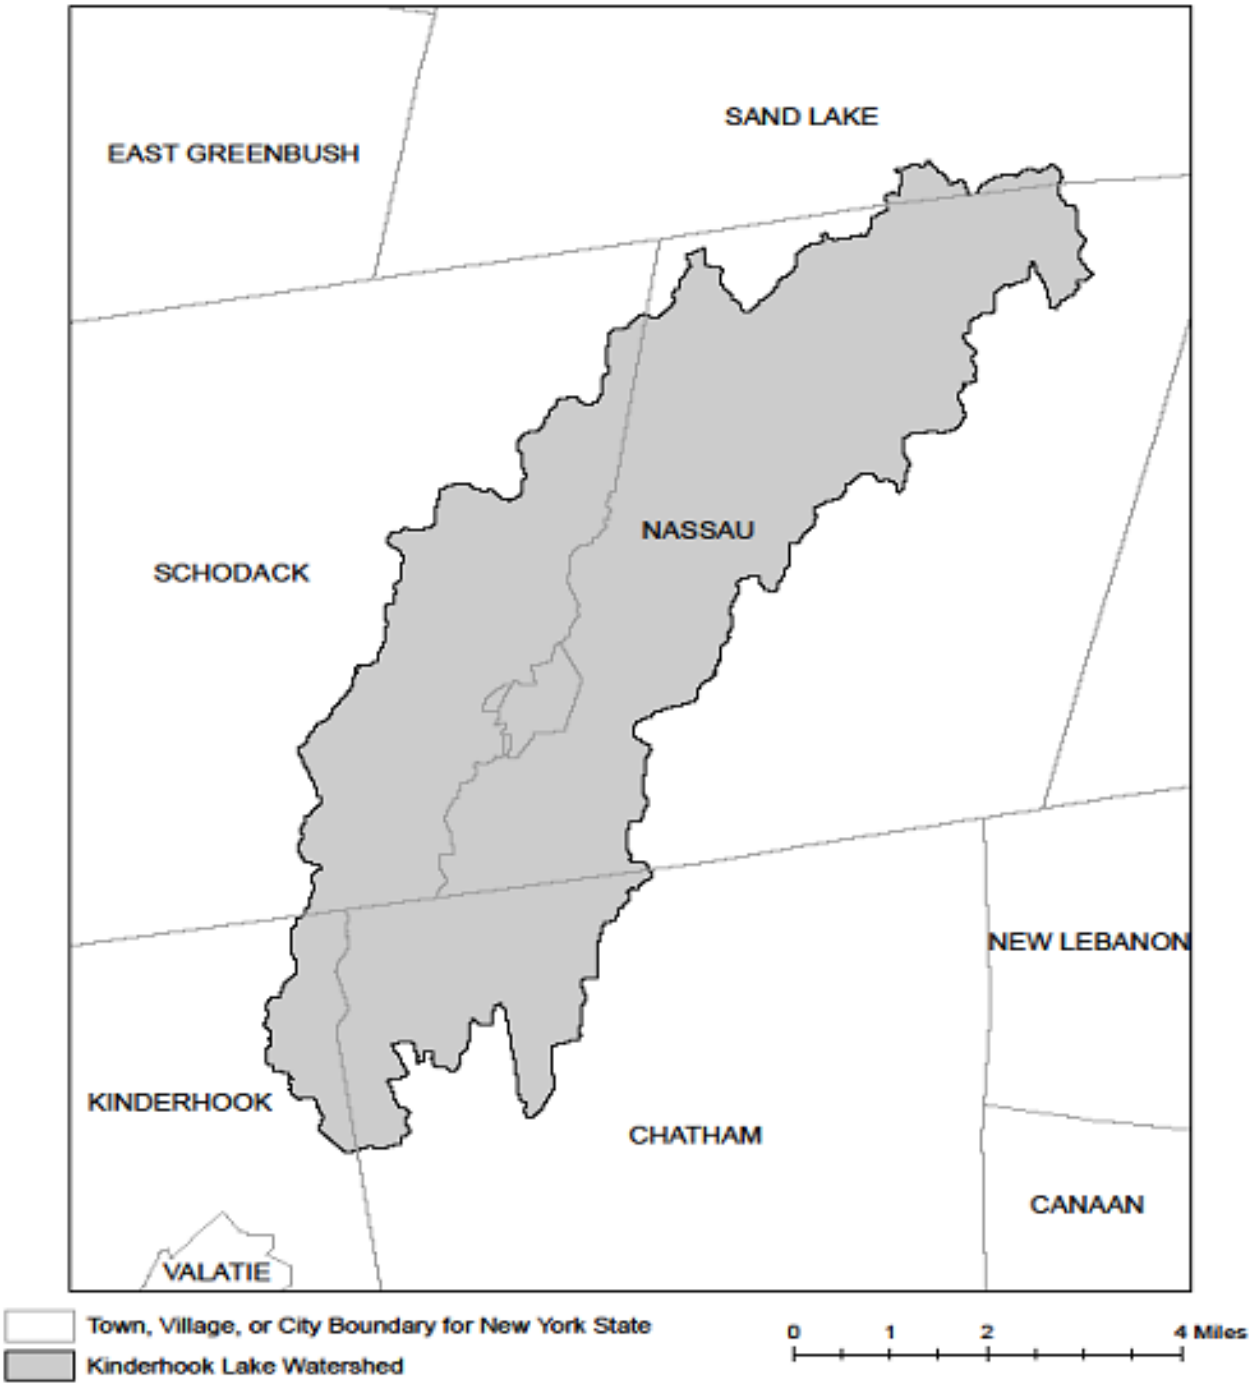

APPENDIX D – Impaired Waterbodies (by Construction Related Pollutants)

List of waterbodies impaired by *pollutants* related to *construction activity*, including turbidity, silt/sediment, and nutrients (e.g. nitrogen, phosphorus). This list is a subset of "The Final New York State 2018 Section 303(d) List of Impaired Waters Requiring a TMDL" dated June 2020.

County	Waterbody	Pollutant
Albany	Ann Lee (Shakers) Pond, Stump Pond (1201-0096)	Phosphorus
Albany	Lawsons Lake (1301-0235)	Phosphorus
Allegany	Amity Lake, Saunders Pond (0403-0054)	Phosphorus
Allegany	Andover Pond (0403-0056)	Phosphorus
Bronx	Reservoir No.1/Lake Isle (1702-0075)	Phosphorus
Bronx	Van Cortlandt Lake (1702-0008)	Phosphorus
Broome	Blueberry, Laurel Lakes (1404-0033)	Phosphorus
Broome	Fly Pond, Deer Lake (1404-0038)	Phosphorus
Broome	Minor Tribs to Lower Susquehanna (0603-0044)	Phosphorus
Broome	Whitney Point Lake/Reservoir (0602-0004)	Phosphorus
Cattaraugus	Allegheny River/Reservoir (0201-0023)	Phosphorus
Cattaraugus	Beaver Lake/Alma Pond (0201-0073)	Phosphorus
Cattaraugus	Case Lake (0201-0020)	Phosphorus
Cattaraugus	Linlyco/Club Pond (0201-0035)	Phosphorus
Cayuga	Duck Lake (0704-0025)	Phosphorus
Cayuga	Owasco Inlet, Upper, and tribs (0706-0014)	Nutrients
Chautauqua	Chadakoin River and tribs (0202-0018)	Phosphorus
Chautauqua	Hulburt/Clymer Pond (0202-0079)	Phosphorus
Chautauqua	Middle Cassadaga Lake (0202-0002)	Phosphorus
Clinton	Great Chazy River, Lower, Main Stem (1002-0001)	Silt/Sediment
Columbia	Robinson Pond (1308-0003)	Phosphorus
Cortland	Dean Pond (0602-0077)	Phosphorus
Dutchess	Fallkill Creek (1301-0087)	Phosphorus
Dutchess	Hillside Lake (1304-0001)	Phosphorus
Dutchess	Wappingers Lake (1305-0001)	Phosphorus
Dutchess	Wappingers Lake (1305-0001)	Silt/Sediment
Erie	Beeman Creek and tribs (0102-0030)	Phosphorus
Erie	Delaware Park Pond (0101-0026)	Phosphorus
Erie	Ellicott Creek, Lower, and tribs (0102-0018)	Phosphorus
Erie	Ellicott Creek, Lower, and tribs (0102-0018)	Silt/Sediment
Erie	Green Lake (0101-0038)	Phosphorus
Erie	Little Sister Creek, Lower, and tribs (0104-0045)	Phosphorus
Erie	Murder Creek, Lower, and tribs (0102-0031)	Phosphorus

Erie	Rush Creek and tribs (0104-0018)	Phosphorus
Erie	Scajaquada Creek, Lower, and tribs (0101-0023)	Phosphorus
Erie	Scajaquada Creek, Middle, and tribs (0101-0033)	Phosphorus
Erie	Scajaquada Creek, Upper, and tribs (0101-0034)	Phosphorus
Erie	South Branch Smoke Cr, Lower, and tribs (0101-0036)	Phosphorus
Erie	South Branch Smoke Cr, Lower, and tribs (0101-0036)	Silt/Sediment
Genesee	Bigelow Creek and tribs (0402-0016)	Phosphorus
Genesee	Black Creek, Middle, and minor tribs (0402 0028)	Phosphorus
Genesee	Black Creek, Upper, and minor tribs (0402-0048)	Phosphorus
Genesee	Bowen Brook and tribs (0102-0036)	Phosphorus
Genesee	LeRoy Reservoir (0402-0003)	Phosphorus
Genesee	Mill Pond (0402-0050)	Phosphorus
Genesee	Oak Orchard Cr, Upper, and tribs (0301-0014)	Phosphorus
Genesee	Oatka Creek, Middle, and minor tribs (0402-0031)	Phosphorus
Genessee	Tonawanda Cr, Middle, Main Stem (0102-0002)	Phosphorus
Greene	Schoharie Reservoir (1202-0012)	Silt/Sediment
Greene	Sleepy Hollow Lake (1301-0059)	Silt/Sediment
Herkimer	Steele Creek tribs (1201-0197)	Phosphorus
Herkimer	Steele Creek tribs (1201-0197)	Silt/Sediment
Kings	Hendrix Creek (1701-0006) 18	Nitrogen
Kings	Prospect Park Lake (1701-0196)	Phosphorus
Lewis	Mill Creek/South Branch, and tribs (0801-0200)	Nutrients
Livingston	Christie Creek and tribs (0402-0060)	Phosphorus
Livingston	Conesus Lake (0402-0004)	Phosphorus
Livingston	Mill Creek and minor tribs (0404-0011)	Silt/Sediment
Monroe	Black Creek, Lower, and minor tribs (0402-0033)	Phosphorus
Monroe	Buck Pond (0301-0017)	Phosphorus
Monroe	Cranberry Pond (0301-0016)	Phosphorus
Monroe	Durand, Eastman Lakes (0302-0037)	Phosphorus
Monroe	Lake Ontario Shoreline, Western (0301-0069) 9	Phosphorus
Monroe	Long Pond (0301-0015)	Phosphorus
Monroe	Mill Creek and tribs (0302-0025)	Phosphorus 2
Monroe	Mill Creek/Blue Pond Outlet and tribs (0402-0049)	Phosphorus
Monroe	Minor Tribs to Irondequoit Bay (0302-0038)	Phosphorus
Monroe	Rochester Embayment - East (0302-0002) [9]	Phosphorus
Monroe	Rochester Embayment - West (0301-0068) 9	Phosphorus
Monroe	Shipbuilders Creek and tribs (0302-0026)	Phosphorus 2
Monroe	Thomas Creek/White Brook and tribs (0302-0023)	Phosphorus

Nassau	Bannister Creek/Bay (1701-0380)	Nitrogen
Nassau	Beaver Lake (1702-0152)	Phosphorus
Nassau	Browswere Bay (1701-0383)	Nitrogen
Nassau	Camaans Pond (1701-0052)	Phosphorus
Nassau	East Meadow Brook, Upper, and tribs (1701-0211)	Silt/Sediment
Nassau	East Rockaway Channel (1701-0381)	Nitrogen
Nassau	Glen Cove Creek, Lower, and tribs (1702-0146)	Silt/Sediment
Nassau	Grant Park Pond (1701-0054)	Phosphorus
Nassau	Hempstead Bay, Broad Channel (1701-0032)	Nitrogen
Nassau	Hempstead Lake (1701-0015)	Phosphorus
Nassau	Hewlett Bay (1701-0382)	Nitrogen
Nassau	Hog Island Channel (1701-0220)	Nitrogen
Nassau	Massapequa Creek, Upper, and tribs (1701-0174)	Phosphorus
Nassau	Milburn/Parsonage Creeks, Upp, and tribs (1701-0212)	Phosphorus
Nassau	Reynolds Channel, East (1701-0215) [12]	Nitrogen
Nassau	Reynolds Channel, West (1701-0216) 12	Nitrogen
Nassau	Tidal Tribs to Hempstead Bay (1701-0218)	Nitrogen
Nassau	Tribs (fresh) to East Bay (1701-0204)	Silt/Sediment
Nassau	Tribs (fresh) to East Bay (1701-0204)	Phosphorus
Nassau	Tribs to Smith Pond/Halls Pond (1701-0221)	Phosphorus
Nassau	Woodmere Channel (1701-0219)	Nitrogen
New York	Harlem Meer (1702-0103)	Phosphorus
New York	The Lake in Central Park (1702-0105)	Phosphorus
Niagara	Bergholtz Creek and tribs (0101-0004)	Phosphorus
Niagara	Hyde Park Lake (0101-0030)	Phosphorus
Niagara	Lake Ontario Shoreline, Western (0301-0053) 9	Phosphorus
Niagara	Lake Ontario Shoreline, Western (0301-0072) 9	Phosphorus
Oneida	Ballou, Nail Creeks (1201-0203)	Phosphorus
Onondaga	Ley Creek and tribs (0702-0001) 10	Nutrients (phosphorus)
Onondaga	Minor Tribs to Onondaga Lake (0702-0022) 10	Nutrients (phosphorus)
Onondaga	Minor Tribs to Onondaga Lake (0702-0022) 10	Nitrogen (NH3, NO2)
Onondaga	Onondaga Creek, Lower (0702-0023) 10	Nutrients (phosphorus)
Onondaga	Onondaga Creek, Lower, and tribs (0702-0023)	Turbidity
Onondaga	Onondaga Creek, Middle, and tribs (0702-0004)	Turbidity
Onondaga	Onondaga Creek, Upper, and tribs (0702-0024)	Turbidity
Ontario	Great Brook and minor tribs (0704-0034)	Phosphorus 2
Ontario	Great Brook and minor tribs (0704-0034)	Silt/Sediment

Ontario	Hemlock Lake Outlet and minor tribs (0402-0013)	Phosphorus
Ontario	Honeoye Lake (0402-0032)	Phosphorus
Orange	Brown Pond Reservoir (1303-0013)	Phosphorus
Orange	Lake Washington (1303-0012)	Phosphorus
Orange	Minor Tribs to Middle Wallkill (1306-0061)	Phosphorus
Orange	Monhagen Brook and tribs (1306-0074)	Phosphorus
Orange	Orange Lake (1301-0008) [16]	Phosphorus
Orange	Quaker Creek and tribs (1306-0025)	Phosphorus
Orange	Wallkill River, Middle, Main Stem (1306-0038)	Phosphorus
Orange	Wallkill River, Upper, and Minor tribs (1306-0017)	Phosphorus
Orleans	Glenvwood Lake (0301-0041)	Phosphorus
Orleans	Lake Ontario Shoreline, Western (0301-0070) 9	Phosphorus
Orleans	Lake Ontario Shoreline, Western (0301-0071) 9	Phosphorus
Oswego	Lake Neatahwanta (0701-0018)	Nutrients (phosphorus)
Oswego	Pleasant Lake (0703-0047)	Phosphorus
Putnam	Lost Lake, Putnam Lake (1302-0053)	Phosphorus
Putnam	Minor Tribs to Croton Falls Reservoir (1302-0001)	Phosphorus
Queens	Bergen Basin (1701-0009) 18	Nitrogen
Queens	Jamaica Bay, Eastern, and tribs, Queens (1701-0005) 18	Nitrogen
Queens	Kissena Lake (1702-0258)	Phosphorus
Queens	Meadow Lake (1702-0030)	Phosphorus
Queens	Shellbank Basin (1701-0001) 18	Nitrogen
Queens	Willow Lake (1702-0031)	Phosphorus
Rensselaer	Nassau Lake (1310-0001)	Phosphorus
Rensselaer	Snyders Lake (1301-0043)	Phosphorus
Richmond	Grassmere Lake/Bradys Pond (1701-0357)	Phosphorus
Rockland	Congers Lake, Swartout Lake (1501-0019)	Phosphorus
Rockland	Rockland Lake (1501-0021)	Phosphorus
Saratoga	Ballston Lake (1101-0036)	Phosphorus
Saratoga	Dwaas Kill and tribs (1101-0007)	Phosphorus
Saratoga	Dwaas Kill and tribs (1101-0007)	Silt/Sediment
Saratoga	Lake Lonely (1101-0034)	Phosphorus
Saratoga	Round Lake (1101-0060)	Phosphorus
Saratoga	Tribs to Lake Lonely (1101-0001)	Phosphorus
Schenectady	Collins Lake (1201-0077)	Phosphorus
Schenectady	Duane Lake (1311-0006)	Phosphorus
Schenectady Lake	Mariaville Lake (1201-0113)	Phosphorus
Schuyler	Cayuta Lake (0603-0005)	Phosphorus

Seneca	Reeder Creek and tribs (0705-0074)	Phosphorus
St.Lawrence	Black Lake Outlet, Black Lake (0906-0001)	Phosphorus
St.Lawrence	Fish Creek and minor tribs (0906-0026)	Phosphorus
Steuben	Smith Pond (0502-0012)	Phosphorus
Suffolk	Agawam Lake (1701-0117)	Phosphorus
Suffolk	Big/Little Fresh Ponds (1701-0125)	Phosphorus
Suffolk	Canaan Lake (1701-0018)	Phosphorus
Suffolk	Canaan Lake (1701-0018)	Silt/Sediment
Suffolk	Fresh Pond (1701-0241)	Phosphorus
Suffolk	Great South Bay, East (1701-0039)	Nitrogen
Suffolk	Great South Bay, Middle (1701-0040)	Nitrogen
Suffolk	Great South Bay, West (1701-0173)	Nitrogen
Suffolk	Lake Ronkonkoma (1701-0020)	Phosphorus
Suffolk	Mattituck/Marratooka Pond (1701-0129)	Phosphorus
Suffolk	Mill and Seven Ponds (1701-0113)	Phosphorus
Suffolk	Millers Pond (1702-0013)	Phosphorus
Suffolk	Moriches Bay, East (1701-0305)	Nitrogen
Suffolk	Moriches Bay, West (1701-0038)	Nitrogen
Suffolk	Quantuck Bay (1701-0042)	Nitrogen
Suffolk	Shinnecock Bay and Inlet (1701-0033)	Nitrogen
Suffolk	Tidal Tribs to West Moriches Bay (1701-0312)	Nitrogen
Sullivan	Bodine, Mongomery Lakes (1401-0091)	Phosphorus
Sullivan	Davies Lake (1402-0047)	Phosphorus
Sullivan	Evens Lake (1402-0004)	Phosphorus
Sullivan	Pleasure Lake (1402-0055)	Phosphorus
Sullivan	Swan Lake (1401-0063)	Phosphorus
Tompkins	Cayuga Lake, Southern End (0705-0040)	Phosphorus
Tompkins	Cayuga Lake, Southern End (0705-0040)	Silt/Sediment
Ulster	Ashokan Reservoir (1307-0004)	Silt/Sediment
Ulster	Esopus Creek, Lower, Main Stem (1307-0010) [17]	Turbidity
Ulster	Esopus Creek, Middle, Main Stem (1307-0003) 17	Turbidity
Ulster	Esopus Creek, Upper, and minor tribs (1307-0007)[3]	Silt/Sediment
Ulster	Wallkill River, Lower, Main Stem (1306-0027)	Phosphorus
Warren	Hague Brook and tribs (1006-0006)	Silt/Sediment
Warren	Huddle/Finkle Brooks and tribs (1006-0003)	Silt/Sediment
Warren	Indian Brook and tribs (1006-0002)	Silt/Sediment
Warren	Lake George (1006-0016) and tribs	Silt/Sediment
Warren	Tribs to Lake George, East Shore (1006-0020)	Silt/Sediment
Warren	Tribs to Lake George, Lk.George Village (1006-0008)	Silt/Sediment

Washington	Wood Cr/Champlain Canal and tribs (1005-0036)	Phosphorus
Westchester	Lake Katonah (1302-0136)	Phosphorus
Westchester	Lake Lincolndale (1302-0089)	Phosphorus
Westchester	Lake Meahagh (1301-0053)	Phosphorus
Westchester	Lake Mohegan (1301-0149)	Phosphorus
Westchester	Lake Shenorock (1302-0083)	Phosphorus
Westchester	Mamaroneck River, Lower (1702-0071)	Silt/Sediment
Westchester	Mamaroneck River, Upp, & minor tribs (1702-0123)	Silt/Sediment
Westchester	Saw Mill River (1301-0007)	Phosphorus
Westchester	Saw Mill River, Middle, and tribs (1301-0100)	Phosphorus
Westchester	Sheldrake River (1702-0069)	Phosphorus
Westchester	Sheldrake River (1702-0069)	Silt/Sedimnt
Westchester	Silver Lake (1702-0040)	Phosphorus
Westchester	Teatown Lake (1302-0150)	Phosphorus
Westchester	Truesdale Lake (1302-0054)	Phosphorus
Westchester	Wallace Pond (1301-0140)	Phosphorus

APPENDIX E – List of NYSDEC Regional Offices

Region	Covering the following counties:	DIVISION OF ENVIRONMENTAL PERMITS (DEP) Permit Administrators	DIVISION OF WATER (DOW) Water (SPDES) Program
1	Nassau and Suffolk	50 Circle Road Stony Brook, NY 11790 Tel. (631) 444-0365	50 Circle Road Stony Brook, NY 11790-3409 Tel. (631) 444-0405
2	Bronx, Kings, New York, Queens and Richmond	1 Hunters Point Plaza, 47-40 21st St. Long Island City, NY 11101-5407 Tel. (718) 482-4997	1 Hunters Point Plaza, 47-40 21st St. Long Island City, NY 11101-5407 Tel. (718) 482-4933
3	Dutchess, Orange, Putnam, Rockland, Sullivan, Ulster and Westchester	21 South Putt Corners Road New Paltz, NY 12561-1696 Tel. (845) 256-3059	220 White Plains Road, Suite 110 Tel. (914) 428 - 2505
4	Albany, Columbia, Delaware, Greene, Montgomery, Otsego, Rensselaer, Schenectady and Schoharie	1130 North Westcott Road Schenectady, NY 12306-2014 Tel. (518) 357-2069	1130 North Westcott Road Schenectady, NY 12306-2014 Tel. (518) 357-2045
5	Clinton, Essex, Franklin, Fulton, Hamilton, Saratoga, Warren and Washington	1115 State Route 86, Po Box 296 Ray Brook, NY 12977-0296 Tel. (518) 897-1234	232 Golf Course Road Warrensburg, NY 12885-1172 Tel. (518) 623-1200
6	HERKIMER, JEFFERSON, LEWIS, ONEIDA AND ST. LAWRENCE	STATE OFFICE BUILDING 317 WASHINGTON STREET WATERTOWN, NY 13601-3787 TEL. (315) 785-2245	STATE OFFICE BUILDING 207 GENESEE STREET UTICA, NY 13501-2885 TEL. (315) 793-2554
7	BROOME, CAYUGA, CHENANGO, CORTLAND, MADISON, ONONDAGA, OSWEGO, TIOGA AND TOMPKINS	5786 WIDEWATERS PARKWAY SYRACUSE, NY 13214-1867 TEL. (315) 426-7438	5786 WIDEWATERS PARKWAY SYRACUSE, NY 13214-1867 TEL. (315) 426-7500
8	CHEMUNG, GENESEE, LIVINGSTON, MONROE, ONTARIO, ORLEANS, SCHUYLER, SENECA, STEUBEN, WAYNE AND YATES	6274 EAST AVON-LIMA ROADAVON, NY 14414-9519 TEL. (585) 226-2466	6274 EAST AVON-LIMA RD. AVON, NY 14414-9519 TEL. (585) 226-2466
9	ALLEGANY, CATTARAUGUS, CHAUTAUQUA, ERIE, NIAGARA AND WYOMING	700 DELAWARE AVENUE BUFFALO, NY 14209-2999 TEL. (716) 851-7165	700 DELAWARE AVENUE BUFFALO, NY 14209-2999 TEL. (716) 851-7070

APPENDIX B
ENGINEER'S CERTIFICATION

SWPPP Preparer Certification Form

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b., the completed form must be attached to the eNOI and submitted to NYSDEC electronically.)

Project/Site Name:	Torview Community Storage NY, LLC
eNOI Submission ID:	N.A.
Owner/Operator Name:	Luminace Holdings, LLC

Certification Statement – SWPPP Preparer

I hereby certify that the Stormwater Pollution Prevention Plan (SWPPP) has been prepared in accordance with the requirements of GP-0-25-001. I certify under penalty of law that the SWPPP and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

James	M	Privette, PE
SWPPP Preparer First Name	MI	SWPPP Preparer Last Name



Signature

130 Oct 2026

Date

Revised: January 2025

APPENDIX C
OWNER/OPERATOR CERTIFICATION

Owner/Operator Certification Form

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b. or Part I.F.2. and 3., the completed form must be attached to the eNOI or the Request to Continue Coverage, and submitted to NYSDEC electronically.

Project/Site Name: Torview Community Storage NY, LLC

eNOI Submission ID: N.A.

eNOI Submitted by: ☑ **Owner/Operator** ☐ **SWPPP Preparer** ☐ **Other**

Certification Statement - Owner/Operator

I hereby certify that I read, and will comply with, the GP-0-25-001 permit requirements. I understand that authorization to discharge under the permit for the project/site named above is dependent on receipt of a Letter of Authorization (LOA) or a Letter of Continued Coverage (LOCC) from the New York State Department of Environmental Conservation (NYSDEC) in accordance with CGP Part I.D.3.b. or Part I.F.4. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Owner/Operator First Name MI Owner/Operator Last Name

_____

Signature

_____

Date

Revised: January 2025

APPENDIX D
CONTRACTOR/SUBCONTRACTOR CERTIFICATION

CONR 5
(10/19)

Contractor / Subcontractor SPDES Permit Certification

Contract No.: _____ PIN: _____

Description: _____

Town, Village, City: _____

County: _____

Check Applicable Box: ☐ Prime Contractor ☐ Subcontractor

Name of Contractor/
Subcontractor: _____

Address: _____

City: _____ State: _____ ZIP: _____

Phone: _____ Fax: _____

Core Pay Item Groups for which the Contractor/Subcontractor will be responsible (e.g. 203, 207, 209, etc.): _____ _____ _____ _____ _____ _____ _____ _____

Mandatory Certification: The SPDES General Permit for Stormwater Discharges from Construction Activities requires the Prime Contractor and subcontractors to certify they understand the Stormwater Pollution Prevention Plan (SWPPP), the General Permit conditions, and their responsibilities for compliance. The certification must be signed prior to performing any contract work. The certification shall be signed by an Owner, Principal, President, Secretary or Treasurer of the firm in accordance with the signature requirements of 102-05 *Proposal Submission* of the Standard Specifications.

"I hereby certify under penalty of law that I understand and agree to comply with the terms and conditions of the SWPPP and agree to implement any corrective actions identified by the qualified inspector during a site inspection. I also understand that the owner or operator must comply with the terms and conditions of the most current version of the New York State Pollutant Discharge Elimination System ("SPDES") general permit for stormwater discharges from construction activities and that it is unlawful for any person to cause or contribute to a violation of water quality standards. Furthermore, I am aware that there are significant penalties for submitting false information, that I do not believe to be true, including the possibility of fine and imprisonment for knowing violations."

Signature: _____ Date: _____

Name: _____ Title: _____

Required Training: Effective April 30, 2010, the SPDES General Permit also requires the Prime Contractor and all subcontractors ***performing earthwork or soil-disturbing activities*** to identify at least one trained individual ***from each company*** who will be responsible for implementing the SWPPP and who shall be on-site on a daily basis when the company is performing soil disturbance activities. These activities include clearing, grubbing, grading, filling, excavation, stockpiling, demolition, landscaping, and installation and maintenance of Erosion & Sediment Control practices. Training must consist of 4 hours of NYSDEC-endorsed Erosion & Sediment Control Training every 3 years. (Training is not required if the individual is a licensed Professional Engineer, registered licensed Landscape Architect, or CPESC.) Provide the information below for trained individuals who will be on-site and responsible for SWPPP implementation on this Contract (attach a separate sheet if needed for additional Trained Individuals):

Trained Individual Name/Title : _____

Name of Training Course: _____

Trainee Number: _____ Date of Training: _____

Trained Individual Name/Title : _____

Name of Training Course: _____

Trainee Number: _____ Date of Training: _____

APPENDIX E
LIST OF CONTRACTORS AND SUBCONTRACTORS

LIST OF CONTRACTORS/SUBCONTRACTORS

Project Name:	Torview Community Storage NY, LLC

Contractor:	
Address:	
Contact Name:	
Contact Phone:	
Contact email:	

Contractor:	
Address:	
Contact Name:	
Contact Phone:	
Contact email:	

Subcontractor:	
Address:	
Contact Name:	
Contact Phone:	
Contact email:	

Subcontractor:	
Address:	
Contact Name:	
Contact Phone:	
Contact email:	

Subcontractor:	
Address:	
Contact Name:	
Contact Phone:	
Contact email:	

Subcontractor:	
Address:	
Contact Name:	
Contact Phone:	
Contact email:	

APPENDIX F
NRCS SOILS MAPPING

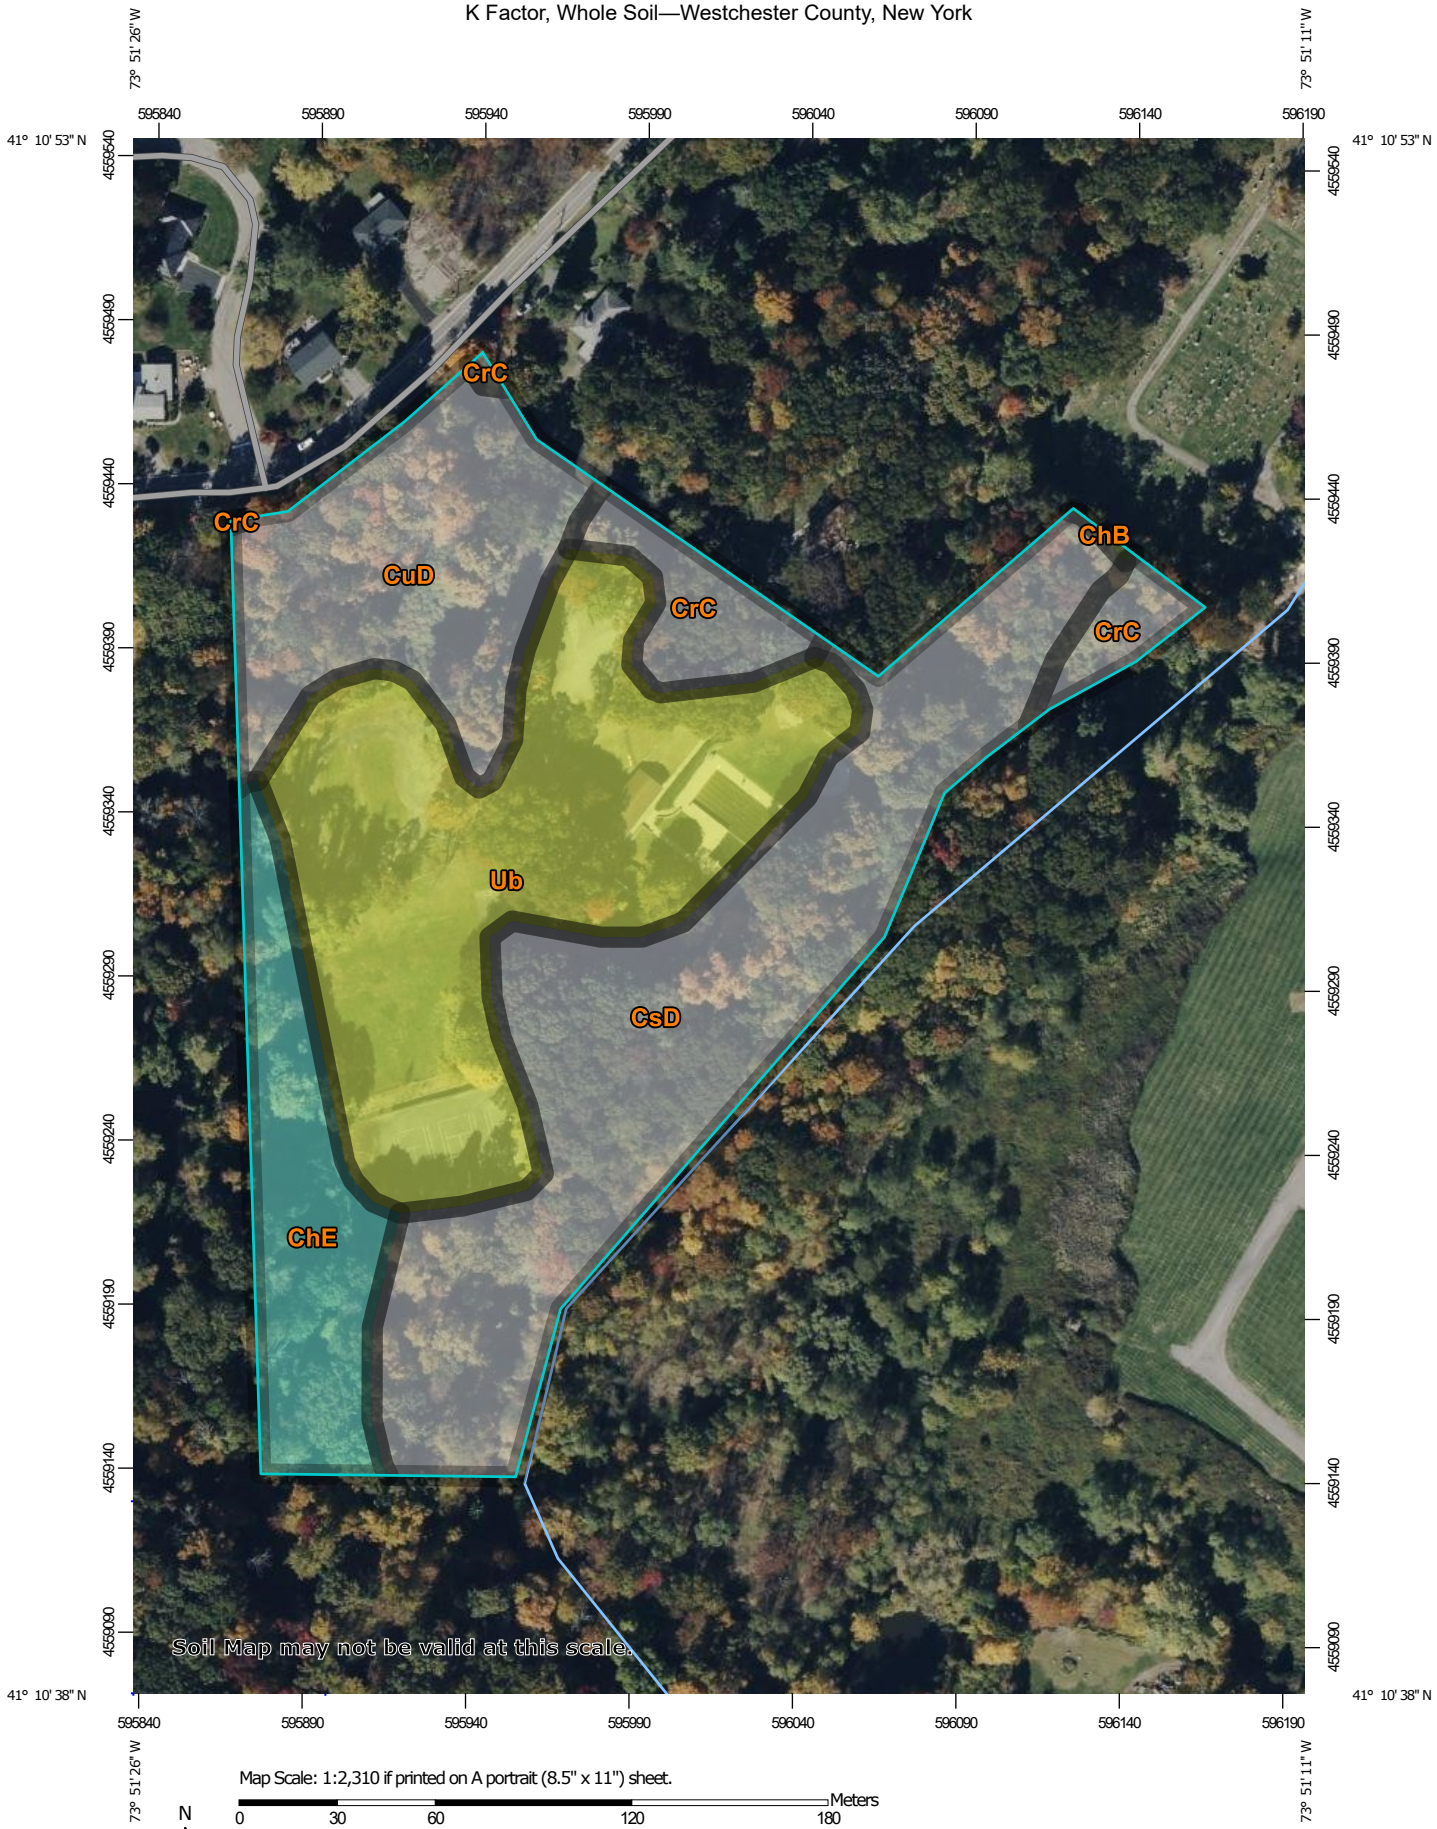

Map Scale: 1:2,310 if printed on A portrait (8.5" x 11") sheet.

N

Meters: 0 30 60 120 180

Feet: 0 100 200 400 600

Map projection: Web Mercator Corner coordinates: WGS84 Edge tics: UTM Zone 18N WGS84

MAP LEGEND

Area of Interest (AOI)
- Area of Interest (AOI)

Soils

Soil Rating Polygons
- .02
- .05
- .10
- .15
- .17
- .20
- .24
- .28
- .32
- .37
- .43
- .49
- .55
- .64
- Not rated or not available

Soil Rating Lines
- .02
- .05
- .10
- .15
- .17
- .20
- .24
- .28
- .32
- .37
- .43
- .49
- .55
- .64
- Not rated or not available

Soil Rating Points
- .02
- .05
- .10
- .15
- .17
- .20
- .24
- .28
- .32
- .37
- .43
- .49
- .55
- .64
- Not rated or not available

Water Features
- Streams and Canals

Transportation
- Rails
- Interstate Highways
- US Routes
- Major Roads
- Local Roads

Background
- Aerial Photography

MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:12,000.

Warning: Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service
Web Soil Survey URL:
Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: Westchester County, New York
Survey Area Data: Version 22, Sep 1, 2026

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Oct 21, 2022—Oct 27, 2022

The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

K Factor, Whole Soil

Map unit symbol	Map unit name	Rating	Acres in AOI	Percent of AOI
ChB	Charlton fine sandy loam, 3 to 8 percent slopes	.24	0.0	0.1%
ChE	Charlton loam, 25 to 35 percent slopes	.32	1.4	11.1%
CrC	Charlton-Chatfield complex, 0 to 15 percent slopes, very rocky		0.8	6.1%
CsD	Chatfield-Charlton complex, 15 to 35 percent slopes, very rocky		4.2	33.3%
CuD	Chatfield-Hollis-Rock outcrop complex, 15 to 35 percent slopes		2.0	15.9%
Ub	Udorthents, smoothed	.20	4.3	33.5%
Totals for Area of Interest			**12.7**	**100.0%**

Description

Erosion factor K indicates the susceptibility of a soil to sheet and rill erosion by water. Factor K is one of six factors used in the Universal Soil Loss Equation (USLE) and the Revised Universal Soil Loss Equation (RUSLE) to predict the average annual rate of soil loss by sheet and rill erosion in tons per acre per year. The estimates are based primarily on percentage of silt, sand, and organic matter and on soil structure and saturated hydraulic conductivity (Ksat). Values of K range from 0.02 to 0.69. Other factors being equal, the higher the value, the more susceptible the soil is to sheet and rill erosion by water.

"Erosion factor Kw (whole soil)" indicates the erodibility of the whole soil. The estimates are modified by the presence of rock fragments.

Factor K does not apply to organic horizons and is not reported for those layers.

Rating Options

Aggregation Method: Dominant Condition

Component Percent Cutoff: None Specified

Tie-break Rule: Higher

Layer Options (Horizon Aggregation Method): Surface Layer (Not applicable)

APPENDIX G
FEMA FLOOD MAP

National Flood Hazard Layer FIRMette

FEMA

73°51'39"W 41°11'1"N

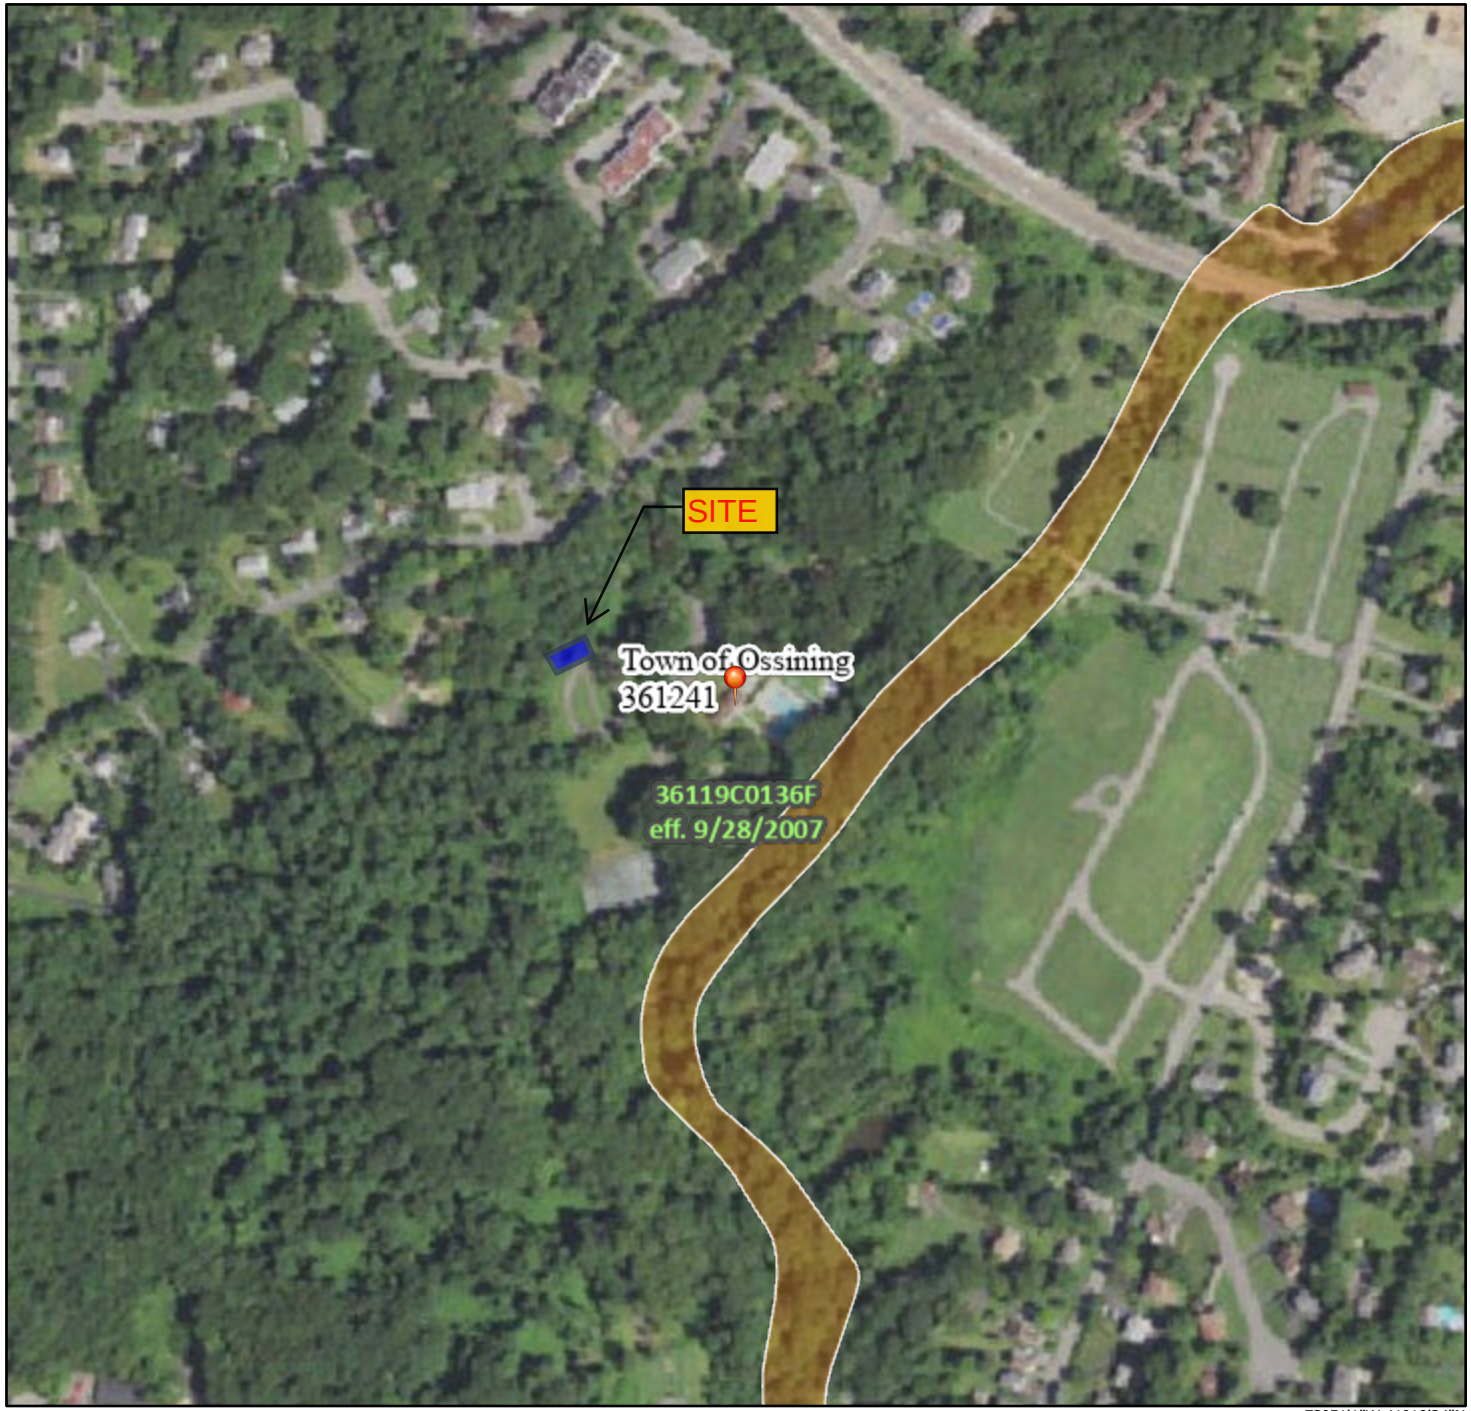

73°51'1"W 41°10'34"N

0 250 500 1,000 1,500 2,000 Feet

1:6,000

Basemap Imagery Source: USGS National Map 2023

Legend

SEE FIS REPORT FOR DETAILED LEGEND AND INDEX MAP FOR FIRM PANEL LAYOUT

SPECIAL FLOOD HAZARD AREAS
- Without Base Flood Elevation (BFE) *Zone A, V, A99*
- With BFE or Depth *Zone AE, AO, AH, VE, AR*
- Regulatory Floodway

OTHER AREAS OF FLOOD HAZARD
- 0.2% Annual Chance Flood Hazard, Areas of 1% annual chance flood with average depth less than one foot or with drainage areas of less than one square mile *Zone X*
- Future Conditions 1% Annual Chance Flood Hazard *Zone X*
- Area with Reduced Flood Risk due to Levee. See Notes. *Zone X*
- Area with Flood Risk due to Levee *Zone D*

OTHER AREAS
- NO SCREEN Area of Minimal Flood Hazard *Zone X*
- Effective LOMRs
- Area of Undetermined Flood Hazard *Zone D*

GENERAL STRUCTURES
- Channel, Culvert, or Storm Sewer
- Levee, Dike, or Floodwall

OTHER FEATURES
- 20.2 Cross Sections with 1% Annual Chance
- 17.5 Water Surface Elevation
- Coastal Transect
- Base Flood Elevation Line (BFE)
- Limit of Study
- Jurisdiction Boundary
- Coastal Transect Baseline
- Profile Baseline
- Hydrographic Feature

MAP PANELS
- Digital Data Available
- No Digital Data Available
- Unmapped

N

The pin displayed on the map is an approximate point selected by the user and does not represent an authoritative property location.

This map complies with FEMA's standards for the use of digital flood maps if it is not void as described below. The basemap shown complies with FEMA's basemap accuracy standards

The flood hazard information is derived directly from the authoritative NFHL web services provided by FEMA. This map was exported on 10/29/2026 at 7:35 AM and does not reflect changes or amendments subsequent to this date and time. The NFHL and effective information may change or become superseded by new data over time.

This map image is void if the one or more of the following map elements do not appear: basemap imagery, flood zone labels, legend, scale bar, map creation date, community identifiers, FIRM panel number, and FIRM effective date. Map images for unmapped and unmodernized areas cannot be used for regulatory purposes.

APPENDIX H
CONSTRUCTION INSPECTION LOG BOOK AND CERTIFICATION FORMS

APPENDIX I
CONSTRUCTION SITE INSPECTION AND MAINTENANCE LOG BOOK

STATE POLLUTANT DISCHARGE ELIMINATION SYSTEM FOR CONSTRUCTION ACTIVITIES

CONSTRUCTION SITE LOG BOOK

Table of Contents

I. Pre-Construction Meeting Documents
   a. Preamble to Site Assessment and Inspections
   b. Pre-Construction Site Assessment Checklist

II. Construction Duration Inspections
   a. Directions
   b. Modification to the SWPPP

I. **PRE-CONSTRUCTION MEETING DOCUMENTS**

Project Name _____

Permit No. _____ **Date of Authorization** _____

Name of Operator _____

Prime Contractor _____

a. **Preamble to Site Assessment and Inspections**

The Following Information To Be Read By All Person's Involved in The Construction of Stormwater Related Activities:

The Operator agrees to have a qualified inspector[1] conduct an assessment of the site prior to the commencement of construction[2] and certify in this inspection report that the appropriate erosion and sediment controls described in the SWPPP have been adequately installed or implemented to ensure overall preparedness of the site for the commencement of construction.

Prior to the commencement of construction, the Operator shall certify in this site logbook that the SWPPP has been prepared in accordance with the State's standards and meets all Federal, State and local erosion and sediment control requirements. A preconstruction meeting should be held to review all of the SWPPP requirements with construction personnel.

When construction starts, site inspections shall be conducted by the qualified inspector at least every 7 calendar days. The Operator shall maintain a record of all inspection reports in this site logbook. The site logbook shall be maintained on site and be made available to the permitting authorities upon request.

Prior to filing the Notice of Termination or the end of permit term, the Operator shall have a qualified inspector perform a final site inspection. The qualified inspector shall certify that the site has undergone final stabilization[3] using either vegetative or structural stabilization methods and that all temporary erosion and sediment controls (such as silt fencing) not needed for long-term erosion control have been removed. In addition, the Operator must identify and certify that all permanent structures described in the SWPPP have been constructed and provide the owner(s) with an operation and maintenance plan that ensures the structure(s) continuously functions as designed.

1 Refer to "Qualified Inspector" inspection requirements in the current SPDES General Permit for Stormwater Discharges from Construction Activity for complete list of inspection requirements.
2 "Commencement of construction" means the initial removal of vegetation and disturbance of soils associated with clearing, grading or excavating activities or other construction activities.
3 "Final stabilization" means that all soil-disturbing activities at the site have been completed and a uniform, perennial vegetative cover with a density of eighty (80) percent has been established or equivalent stabilization measures (such as the use of mulches or geotextiles) have been employed on all unpaved areas and areas not covered by permanent structures.

b. Pre-construction Site Assessment Checklist
(NOTE: Provide comments below as necessary)

1. Notice of Intent, SWPPP, and Contractors Certification:

Yes No NA

[ ] [ ] [ ] Has a Notice of Intent been filed with the NYS Department of Conservation?
[ ] [ ] [ ] Is the SWPPP on-site? Where?_____
[ ] [ ] [ ] Is the Plan current? What is the latest revision date?_____
[ ] [ ] [ ] Is a copy of the NOI (with brief description) onsite? Where?_____
[ ] [ ] [ ] Have all contractors involved with stormwater related activities signed a contractor's certification?

2. Resource Protection

Yes No NA

[ ] [ ] [ ] Are construction limits clearly flagged or fenced?
[ ] [ ] [ ] Important trees and associated rooting zones, on-site septic system absorption fields, existing vegetated areas suitable for filter strips, especially in perimeter areas, have been flagged for protection.
[ ] [ ] [ ] Creek crossings installed prior to land-disturbing activity, including clearing and blasting.

3. Surface Water Protection

Yes No NA

[ ] [ ] [ ] Clean stormwater runoff has been diverted from areas to be disturbed.
[ ] [ ] [ ] Bodies of water located either on site or in the vicinity of the site have been identified and protected.
[ ] [ ] [ ] Appropriate practices to protect on-site or downstream surface water are installed.
[ ] [ ] [ ] Are clearing and grading operations divided into areas <5 acres?

4. Stabilized Construction Access

Yes No NA

[ ] [ ] [ ] A temporary construction entrance to capture mud and debris from construction vehicles before they enter the public highway has been installed.
[ ] [ ] [ ] Other access areas (entrances, construction routes, equipment parking areas) are stabilized immediately as work takes place with gravel or other cover.
[ ] [ ] [ ] Sediment tracked onto public streets is removed or cleaned on a regular basis.

5. Sediment Controls

Yes No NA

[ ] [ ] [ ] Silt fence material and installation comply with the standard drawing and specifications.
[ ] [ ] [ ] Silt fences are installed at appropriate spacing intervals
[ ] [ ] [ ] Sediment/detention basin was installed as first land disturbing activity.
[ ] [ ] [ ] Sediment traps and barriers are installed.

6. Pollution Prevention for Waste and Hazardous Materials

Yes No NA

[ ] [ ] [ ] The Operator or designated representative has been assigned to implement the spill prevention avoidance and response plan.
[ ] [ ] [ ] The plan is contained in the SWPPP on page _____
[ ] [ ] [ ] Appropriate materials to control spills are onsite. Where? _____

II. CONSTRUCTION DURATION INSPECTIONS

a. Directions:

Inspection Forms will be filled out during the entire construction phase of the project.

Required Elements:

1) On a site map, indicate the extent of all disturbed site areas and drainage pathways. Indicate site areas that are expected to undergo initial disturbance or significant site work within the next 14-day period;

2) Indicate on a site map all areas of the site that have undergone temporary or permanent stabilization;

3) Indicate all disturbed site areas that have not undergone active site work during the previous 14-day period;

4) Inspect all sediment control practices and record the approximate degree of sediment accumulation as a percentage of sediment storage volume (for example, 10 percent, 20 percent, 50 percent);

5) Inspect all erosion and sediment control practices and record all maintenance requirements such as verifying the integrity of barrier or diversion systems (earthen berms or silt fencing) and containment systems (sediment basins and sediment traps). Identify any evidence of rill or gully erosion occurring on slopes and any loss of stabilizing vegetation or seeding/mulching. Document any excessive deposition of sediment or ponding water along barrier or diversion systems. Record the depth of sediment within containment structures, any erosion near outlet and overflow structures, and verify the ability of rock filters around perforated riser pipes to pass water; and

6) Immediately report to the Operator any deficiencies that are identified with the implementation of the SWPPP.

SITE PLAN/SKETCH

Inspector (print name)	**Date of Inspection**
Qualified Inspector (print name)	**Qualified Inspector Signature**

The above signed acknowledges that, to the best of his/her knowledge, all information provided on the forms is accurate and complete.

Maintaining Water Quality

Yes No NA

[ ] [ ] [ ] Is there an increase in turbidity causing a substantial visible contrast to natural conditions at the outfalls?
[ ] [ ] [ ] Is there residue from oil and floating substances, visible oil film, or globules or grease at the outfalls?
[ ] [ ] [ ] All disturbance is within the limits of the approved plans.
[ ] [ ] [ ] Have receiving lake/bay, stream, and/or wetland been impacted by silt from project?

Housekeeping

1. General Site Conditions

Yes No NA

[ ] [ ] [ ] Is construction site litter, debris and spoils appropriately managed?
[ ] [ ] [ ] Are facilities and equipment necessary for implementation of erosion and sediment control in working order and/or properly maintained?
[ ] [ ] [ ] Is construction impacting the adjacent property?
[ ] [ ] [ ] Is dust adequately controlled?

2. Temporary Stream Crossing

Yes No NA

[ ] [ ] [ ] Maximum diameter pipes necessary to span creek without dredging are installed.
[ ] [ ] [ ] Installed non-woven geotextile fabric beneath approaches.
[ ] [ ] [ ] Is fill composed of aggregate (no earth or soil)?
[ ] [ ] [ ] Rock on approaches is clean enough to remove mud from vehicles & prevent sediment from entering stream during high flow.

3. Stabilized Construction Access

Yes No NA

[ ] [ ] [ ] Stone is clean enough to effectively remove mud from vehicles.
[ ] [ ] [ ] Installed per standards and specifications?
[ ] [ ] [ ] Does all traffic use the stabilized entrance to enter and leave site?
[ ] [ ] [ ] Is adequate drainage provided to prevent ponding at entrance?

Runoff Control Practices

1. Excavation Dewatering

Yes No NA

[ ] [ ] [ ] Upstream and downstream berms (sandbags, inflatable dams, etc.) are installed per plan.
[ ] [ ] [ ] Clean water from upstream pool is being pumped to the downstream pool.
[ ] [ ] [ ] Sediment laden water from work area is being discharged to a silt-trapping device.
[ ] [ ] [ ] Constructed upstream berm with one-foot minimum freeboard.

Runoff Control Practices (continued)

2. Flow Spreader

Yes No NA

[ ] [ ] [ ] Installed per plan.
[ ] [ ] [ ] Constructed on undisturbed soil, not on fill, receiving only clear, non-sediment laden flow.
[ ] [ ] [ ] Flow sheets out of level spreader without erosion on downstream edge.

3. Interceptor Dikes and Swales

Yes No NA

[ ] [ ] [ ] Installed per plan with minimum side slopes 2H:1V or flatter.
[ ] [ ] [ ] Stabilized by geotextile fabric, seed, or mulch with no erosion occurring.
[ ] [ ] [ ] Sediment-laden runoff directed to sediment trapping structure

4. Stone Check Dam

Yes No NA

[ ] [ ] [ ] Is channel stable? (flow is not eroding soil underneath or around the structure).
[ ] [ ] [ ] Check is in good condition (rocks in place and no permanent pools behind the structure).
[ ] [ ] [ ] Has accumulated sediment been removed?.

5. Rock Outlet Protection

Yes No NA

[ ] [ ] [ ] Installed per plan.
[ ] [ ] [ ] Installed concurrently with pipe installation.

Soil Stabilization

1. Topsoil and Spoil Stockpiles

Yes No NA

[ ] [ ] [ ] Stockpiles are stabilized with vegetation and/or mulch.
[ ] [ ] [ ] Sediment control is installed at the toe of the slope.

2. Revegetation

Yes No NA

[ ] [ ] [ ] Temporary seedings and mulch have been applied to idle areas.
[ ] [ ] [ ] 4 inches minimum of topsoil has been applied under permanent seedings

Sediment Control Practices

1. Silt Fence and Linear Barriers

Yes No NA

[ ] [ ] [ ] Installed on Contour, 10 feet from toe of slope (not across conveyance channels).
[ ] [ ] [ ] Joints constructed by wrapping the two ends together for continuous support.
[ ] [ ] [ ] Fabric buried 6 inches minimum.
[ ] [ ] [ ] Posts are stable, fabric is tight and without rips or frayed areas.
Sediment accumulation is ___% of design capacity.

Sediment Control Practices (continued)

2. Storm Drain Inlet Protection (Use for Stone & Block; Filter Fabric; Curb; or, Excavated; Filter Sock or Manufactured practices)

Yes No NA

[ ] [ ] [ ] Installed concrete blocks lengthwise so open ends face outward, not upward.
[ ] [ ] [ ] Placed wire screen between No. 3 crushed stone and concrete blocks.
[ ] [ ] [ ] Drainage area is 1acre or less.
[ ] [ ] [ ] Excavated area is 900 cubic feet.
[ ] [ ] [ ] Excavated side slopes should be 2:1.
[ ] [ ] [ ] 2" x 4" frame is constructed and structurally sound.
[ ] [ ] [ ] Posts 3-foot maximum spacing between posts.
[ ] [ ] [ ] Fabric is embedded 1 to 1.5 feet below ground and secured to frame/posts with staples at max 8-inch spacing.
[ ] [ ] [ ] Posts are stable, fabric is tight and without rips or frayed areas.
[ ] [ ] [ ] Manufactured insert fabric is free of tears and punctures.
[ ] [ ] [ ] Filter Sock is not torn or flattened and fill material is contained within the mesh sock.

Sediment accumulation ___% of design capacity.

3. Temporary Sediment Trap

Yes No NA

[ ] [ ] [ ] Outlet structure is constructed per the approved plan or drawing.
[ ] [ ] [ ] Geotextile fabric has been placed beneath rock fill.
[ ] [ ] [ ] Sediment trap slopes and disturbed areas are stabilized.

Sediment accumulation is ___% of design capacity.

4. Temporary Sediment Basin

Yes No NA

[ ] [ ] [ ] Basin and outlet structure constructed per the approved plan.
[ ] [ ] [ ] Basin side slopes are stabilized with seed/mulch.
[ ] [ ] [ ] Drainage structure flushed and basin surface restored upon removal of sediment basin facility.
[ ] [ ] [ ] Sediment basin dewatering pool is dewatering at appropriate rate.

Sediment accumulation is ___% of design capacity.

Note: Not all erosion and sediment control practices are included in this listing. Add additional pages to this list as required by site specific design. All practices shall be maintained in accordance with their respective standards.

Construction inspection checklists for post-development stormwater management practices can be found in Appendix F of the New York Stormwater Management Design Manual.

CONSTRUCTION DURATION INSPECTIONS

b. Modifications to the SWPPP (To be completed as described below)

The Operator shall amend the SWPPP whenever:

1. There is a significant change in design, construction, operation, or maintenance which may have a significant effect on the potential for the discharge of pollutants to the waters of the United States and which has not otherwise been addressed in the SWPPP; or
2. The SWPPP proves to be ineffective in:
   a. Eliminating or significantly minimizing pollutants from sources identified in the SWPPP and as required by this permit; or
   b. Achieving the general objectives of controlling pollutants in stormwater discharges from permitted construction activity; and
3. Additionally, the SWPPP shall be amended to identify any new contractor or subcontractor that will implement any measure of the SWPPP.

Modification & Reason:

APPENDIX I
CORRECTIVE ACTION AND SWPPP AMENDMENTS LOGS

Corrective Action Log

Project Name: **Torview Community Storage NY, LLC**
SWPPP Contact:

Inspection Date	Inspector's Name	Description of BMP Deficiency	Corrective Action Needed (including planned date/responsible person)	Date Action Taken/Responsible person

SWPPP Amendment Log

Project Name: **Torview Community Storage NY, LLC**
SWPPP Contact:

Amendment Number	Inspector's Name	Description of the Amendment	Date of Amendment	Date Action Taken/Responsible Person

APPENDIX J
SITE CONSTRUCTION PLANS

SITE CONSTRUCTION PLANS:

This SWPPP has been prepared in conjunction with the Site Construction Plans titled TORVIEW COMMUNITY STORAGE NY, LLC, as prepared by Tectonic Engineering Consultants, Geologists & Land Surveyors, D.P.C., dated 10/30/2026.

A copy of the plans are to be kept on-site with this document pursuant to Section 1.6. and considered as an essential supporting document under separate cover.
